

allegiant stadium

Monthly Report - March 2020





LV Stadium Events Company, LLC

April 30, 2020

Mr. Steve Hill Chairman Las Vegas Stadium Authority c/o Applied Analysis 6385 S. Rainbow Blvd, Ste 105 Las Vegas, NV 89118

Dear Mr. Hill:

Enclosed is StadCo's monthly Project Status Report covering the development of **allegiant stadium**.

Despite the severe impact of a global pandemic, the Stadium's construction remains on track for substantial completion on July 31, 2020. The Project also remains within its budget.

In addition to implementing the CDC and OSHA guidelines for reducing the transmission of COVID-19, the Design-Build contractor is actively exploring the possibility of instituting wide-scale virus testing among the construction workforce. This will be challenging since the on-site construction workforce typically consists of 2,000 or more people per day.

The outstanding culture of job-site safety, with reportable incidents running at about one-third the national average, continues.

We have made adjustments to the transportation and delivery plans for select critical components in order to avoid delays caused by global supply chain interruptions.

Clark County has committed to provide uninterrupted support for plan review, permitting and field inspections. We are, however, attempting to overcome challenges to the furniture and equipment installation schedule resulting from special County Department of Building & Fire Prevention requirements. We hope to overcome these *ex cathedra* requirements in order to avoid delaying the use of the Stadium following the completion of construction.

We continue to far outperform the SBE contracting goal (24% actual versus 15% goal) as well as workforce diversity goal (62% actual versus 38% goal) and more than 75% of both contractors and construction workers have been Nevada residents.

Sincerely

Don C. Webb Chief Operating Officer







TABLE OF CONTENTS

| Certification | 1 |
|----------------------------------|----|
| Project Budget | 2 |
| Status of Design Planning | 3 |
| Permit Tracker | 4 |
| Project Schedule | 5 |
| Compliance / SBE | 7 |
| Workforce Utilization | 69 |
| Additional Information / Updates | 75 |

CERTIFICATION

Pursuant to Article 8, Section 8.1 of the Development Agreement between Clark County Stadium Authority and LV Stadium Events Company, LLC dated March 28, 2018, I hereby certify that the information contained within this "Project Status Report" is true and accurate to the best of my knowledge.

Sincerely,

Don C. Webb Chief Operating Officer LV Stadium Events Company, LLC



Stadium Project Budget Report

As of April 15 / Draw #32 / Funding Notice No. 26

| Wa Good service | Initial Budget | Adjustments | Revised Budget | Total Expende | d | Balance | |
|--|-----------------|---------------|-----------------|-----------------|------|---------------|------|
| Raiders Equity, PSL and Permanent Financin [1] | \$850,000,000 | \$170,000,000 | \$1,020,000,000 | \$810,109,925 | 79% | \$209,890,075 | 21% |
| Raiders NFL G-4 Contribution [2] | \$200,000,000 | \$0 | \$200,000,000 | \$162,221,160 | 81% | \$37,778,840 | 19% |
| Clark County Bond Proceeds & Room Tax Pay-Go | \$750,000,000 | \$0 | \$750,000,000 | \$636,307,632 | 85% | \$113,692,368 | 15% |
| Other | \$0 | \$0 | \$0 | \$0 | 0% | \$0 | 100% |
| Total Stadium Development Sources | \$1,800,000,000 | \$170,000,000 | \$1,970,000,000 | \$1,608,638,717 | 82% | \$361,361,283 | 18% |
| Stadium Land Acquisition | \$77,780,128 | \$12,975 | \$77,793,103 | \$77,793,103 | 100% | \$0 | 0% |
| Stadium Construction | \$1,334,455,080 | \$70,963,204 | \$1,405,418,284 | \$1,196,283,421 | 85% | \$209,134,863 | 15% |
| Stadium Furniture, Fixtures & Equipment | \$122,854,543 | \$34,455,325 | \$157,309,868 | \$62,756,413 | 40% | \$94,553,455 | 60% |
| Stadium Design, Engineering & Soft Costs | \$233,852,243 | \$7,068,496 | \$240,920,739 | \$205,466,362 | 85% | \$35,454,377 | 15% |
| Stadium Utility & Infrastructure Costs | \$31,058,006 | -\$2,500,000 | \$28,558,006 | \$15,981,359 | 56% | \$12,576,647 | 44% |
| Premium Seating & Marketing Program [3] | \$0 | \$60,000,000 | \$60,000,000 | \$50,358,059 | 84% | \$9,641,941 | 16% |
| Total Stadium Development Uses | \$1,800,000,000 | \$170,000,000 | \$1,970,000,000 | \$1,608,638,717 | 82% | \$361,361,283 | 18% |

^[1] Includes closed construction debt financing pursuant to Senate Bill 1 (2016 Special Session), Section 36.1(e)(2). Raiders Equity Contribution, above, includes \$40 million in PSL sales used to fund Premium Seating & Marketing Programs, on behalf of the Clark County Stadium Authority.

- [2] Includes approved NFL financing through the G-4 loan program of the NFL.
- [3] Excludes Third-Party Activation Sources and Uses Itemized Below

Stadium Project Budget Report

As of April 15 / Draw #32 / Funding Notice No. 26

| us record threads | Initial Budget | Adjustments | Revised Budget | Total Expended | | Balance |
|------------------------------------|----------------|--------------|----------------|----------------|-----|--------------|
| | | | | | | |
| Total Raiders 3rd-Party Activation | \$0 | \$46,190,126 | \$46,190,126 | \$3,116,914 | \$0 | \$43,073,212 |

Summary Notes:

- 1) "Initial Budget" is as of March 17, 2018
- 2) "Revised Budget" reflects adjustments under consideration & does not include all costs borne solely by StadCo or the Raiders such as costs of developing the team headquarters and training facilities
- 3) "Expended" is based upon actual costs & accrual estimates booked, including retention amounts withheld, as of April 15, 2020
- 4) "Expended" excludes certain predevelopment costs recovered through bond proceeds at closing
- 5) Excludes StadCo or Raiders payroll costs, legal & similar administrative expenses incidental to Stadium development but borne solely by StadCo or Raiders
- 6) Excludes NFL Relocation Fee
- 7) Excludes Temporary Venue Costs
- 8) Excludes certain costs associated with financing and transactional expenses borne by the Raiders
- 9) Actual Balance on individual Sources may vary from that shown above since certain sources are funded on a reimbursable, rather than advance, basis
- 10) Projections are based upon assumptions and information received from others and therefore actual results may vary and the variations may be material

STATUS OF DESIGN PLANNING

To date, HNTB and the AE Team have reviewed a handful of spaces for punch-list. The process is still being refined and is now scheduled to move forward in earnest toward the end of April. In March, SSR's Cx team began the first steps in the commissioning process for the mechanical, electrical and plumbing systems within the building. This will carry on through May and likely into June.

HNTB and the resident members of the AE Team relocated to our new, and hopefully, final field office location. The AE Team is fully operational and our network is established to support the project. The AE Team is adjusting to no longer being co-located with MMcJV (as we have been for the past year).

In terms of design activities, HNTB and the AE Team continue the implementation of infrastructure to support sponsorship integration at select locations within the stadium. There continue to be a steady flow of RFQ's related to additions/modifications to the base building design – primarily to accommodate sponsorship elements.

Permits received to date include all foundations (Package 2), and all concrete construction permits (Packages 3A & 3B) and the structural steel frame package (permit package 4). All structural building permits for the project are now secured. Non-structural permits received include the Shell, Core and all non-premium spaces (Package 5). Premium spaces – clubs, typical suites and select Team spaces (Package 6).

Phased Building Application

Proposed Permit Packages / Valuations Revised 2/1/2019






HNTB

| | | · | | | |
|-----|--------------|---|--|--|-------------------|
| | IT PACKAGE | DESCRIPTION / SCOPE OF WORK | Permit Submission Date (estimates in italics) | Permit Pick-up & Fee Payment Date (estimates in italics) | ANTICIPATED VALUE |
| No# | PAC NO | | | | |
| 1 | | EGRESS DESIGN | | | \$ |
| 2 | | FIDE DOCTECTION DEPONT | | | \$ |
| | | FIRE PROTECTION REPORT | | | \$ |
| 2 | 1 | EXCAVATION & GRADING | 11/13/2017 | 12/19/2017 | \$12,700,000 |
| , | - | EXCHANGE & GIVEING | 11/15/2017 | 12/13/2017 | \$12,700,000 |
| 4 | 1a | ON-SITE UTILITIES | | | \$5,800,000 |
| | | | | | |
| 5 | 2 | FOUNDATIONS / DEEP UTILITIES | 1/10/2018 | 2/20/2018 | \$46,000,000 |
| | | Piles, Pile caps, dowels into first lift | | | |
| | | | | | |
| 6 | | CABLE TRUSS ANALYSIS REVIEW | | | |
| | | | | 1.1 | |
| 7 | 3a | STRUCTURAL FRAME - CONCRETE | 3/13/2018 | 4/6/2018 | \$84,000,000 |
| | | Concrete columns & walls to Level 050, Areas AFBE only | | | |
| 8 | 3b | STRUCTURAL FRAME - CONCRETE | 3/19/2018 | 5/10/2018 | \$42,000,000 |
| 0 | 30 | Concrete to Level 0100, Areas AFBE only | 3/13/2018 | 3/10/2018 | 342,000,000 |
| | | Condition to Edver 0100, All Cus All BE Only | | | |
| 9 | 4 | STRUCTURAL FRAME - STEEL / ROOF | 4/6/2018 | 6/22/2018 | \$290,200,000 |
| | | Remaining structtre in AFBE & all Areas C & D | | . , | |
| | | | | | |
| 10 | 5 | CONSTRUCTION PACKAGE 5 (Arch,Mech,Elect,Plumb) | 7/10/2018 | 11/16/2018 | \$552,200,000 |
| | | Core & Shell Package | | | |
| | _ | | | - 1. 1 | |
| 11 | 6 | FINISHES PACKAGE - Premium Spaces | 11/9/2018 | 2/1/2019 | \$54,500,000 |
| | | Ancillary Permits | | | |
| | | Trailer City permit (Tortoise fees paid with this permit) | 10/5/2017 | 11/9/2017 | |
| | | On-site Utility for Trailer City | 11/5/2017 | 11/29/2017 | |
| | | on site of me, for frame, only | 11/9/2017 | 11/25/2017 | |
| | | | | | |
| | | | | | |
| | | DEFERRED SUBMITTALS | | | |
| | | | | | |
| 12 | | STRUCTURAL PRECAST SYSTEMS | | | \$32,400,000 |
| | | | | | |
| 13 | | FIRE SUPRESSION SPRINKLER SYSTEMS | | | \$10,700,000 |
| | | | | | |
| | | | | | |
| | | | | | |
| | - | | | | |
| | 1 | | | | |


\$ 1,130,500,000

Permit Packages

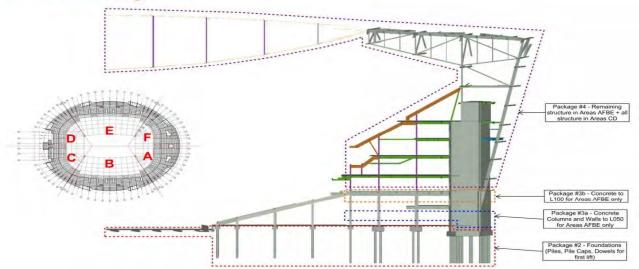

Permit Tracker

| Activity ID | Activity Name | Finish | Called to lead to |
|-------------|---|-------------|-------------------------|
| Summary and | Milestones | | Oct Nov Dec Jan Feb Mar |
| S000-8D | Design Summary - Stadium Design to 62.5% GMP | 01-Oct-17 A | |
| S000-8D1 | Design Summary - Stadium Design to 100% GMP Pricing | 25-Feb-18 A | |
| S000-8N1 | Construction Summary - Deep Foundations | 30-Apr-18 A | |
| S000-8N2C | Construction Summary - FRP Spread Footings | 09-Aug-18 A | |
| S000-8N2B | Construction Summary - FRP Wall/Mat Foundations | 16-Aug-18 A | |
| S000-8N5A | Construction Summary - FRP Elev/Esc Pits | 17-Aug-18 A | |
| S000-8D2 | Design Summary - Stadium Design to 100% CD | 27-Aug-18 A | |
| S000-8P2C | Construction Summary - FRP Columns | 28-Sep-18 A | |
| S000-8N3B | Construction Summary - Foundation Walls | 17-Oct-18 A | |
| S000-8P2B | Construction Summary - FRP Concrete Core Walls | 11-Jan-19 A | |
| S000-8P2G | Construction Summary - Pan & Joist Decks | 14-Jan-19 A | |
| S000-8P1 | Construction Summary - Underground Mech/Plumbing & Elec | 01-Mar-19 A | |
| S000-8M4 | Construction Summary - Mass Excavation | 26-Apr-19 A | |
| S000-8P4B | Construction Summary - Structural Steel (Long Span at Field Tray) | 26-Apr-19 A | |
| S000-8P4J | Construction Summary - Misc Structural Supports | 28-May-19 A | |
| S000-8P4D | Construction Summary - Steel Roof Truss Columns | 20-Jul-19 A | |
| S001-8P4D | Construction Summary - Steel Roof Canopy | 13-Sep-19 A | |
| S000-8P4F2 | Construction Summary - FRP Slab on Metal Deck | 13-Sep-19 A | |
| S000-8P4 | Construction Summary - Steel Structure (Bowl Steel) | 18-Oct-19 A | |
| S000-8T1B | Construction Summary - Mechanical Equipment | 05-Nov-19 A | |
| S000-8P5G | Construction Summary - Precast Stadia | 13-Jan-20 | |
| SXXN-8Q3C5 | Construction Summary - Storefront Glazing System | 13-Jan-20 | |
| S000-8R3 | Construction Summary - Escalators | 13-Jan-20 | |
| S1AB1-8S53 | Construction Summary - Interior Rough-in | 13-Jan-20 | |
| S000-8Q3S | Construction Summary - Specialty Entrances Op Doors | 07-Feb-20 | |
| S000-8P1E | Construction Summary - Slab on Grade | 12-Feb-20 | |
| S000-8Q5 | Construction Summary - Roof Systems | 24-Feb-20 | |
| S000-8Q2A | Construction Summary - Curtainwall | 26-Feb-20 | |
| S000-8D3 | Design Summary - Design Construction Administration | 02-Mar-20 | |
| S000-8Q1F | Construction Summary - Metal Wall Panels | 20-Mar-20 | |
| SRA0-8Q52 | Construction Summary - Membrane Roof Systems | 05-May-20 | |
| S000-8Q5J | Construction Summary - Roof Specialties & Accessories | 20-May-20 | |
| S000-8T7P1 | Construction Summary - Sports Equipment | 12-Jun-20 | |
| S000-8U9 | Construction Summary - Seating | 26-Jun-20 | |
| S1B48R13 | Construction Summary - Elevators | 08-Jul-20 | |
| S000-8U | Construction Summary - Drywall and Interior Finishes | 08-Jul-20 | |
| S000-8U8 | Construction Summary - Specialties | 17-Jul-20 | |
| L001-1A50 | Substantial Completion | 31-Jul-20* | |
| S000-8X31 | Construction Summary - Project Close-out | 14-Aug-20 | |

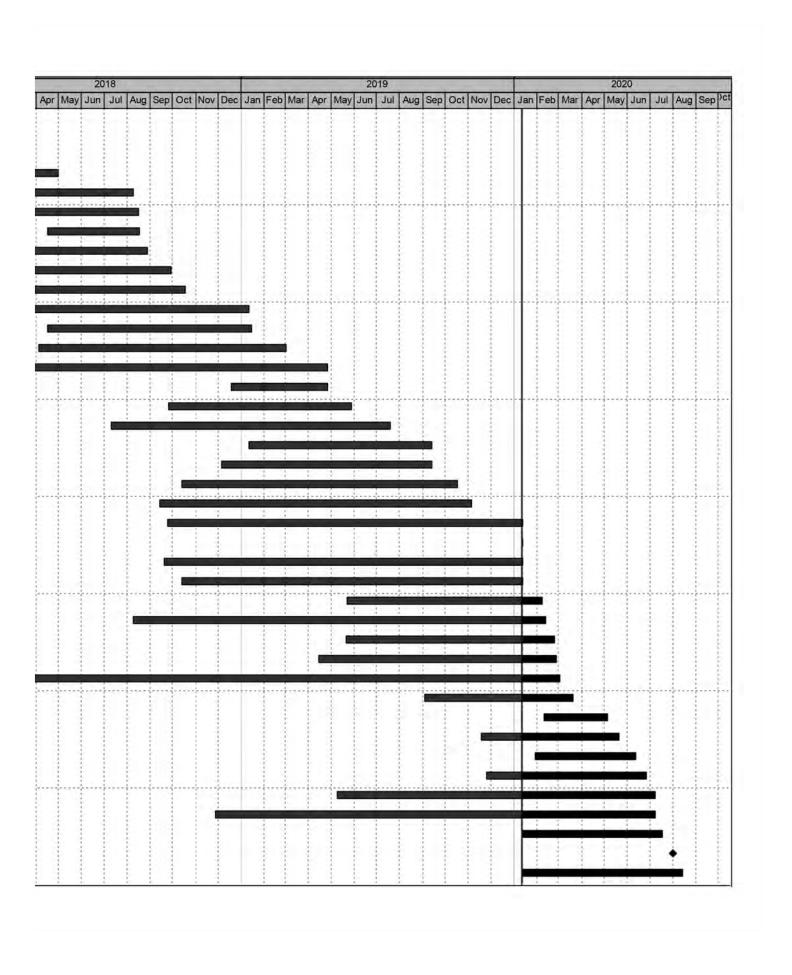

COMPLIANCE / SBE

In accordance with Section 31.5-6 of the Southern Nevada Tourism Improvement Act, Mortenson | McCarthy Las Vegas Stadium, A Joint Venture ("MMcJV") is following the process described below for verification of SBE Contractors.

SBE Contractors apply through the mmcjvlv.com website under the vendors tab. Those seeking certification as a qualified SBE contractor will then fill out and submit a self-certification form, whereas they attest to meeting the criteria for small local business classification denoted in the Senate Bill. The MMcJV Community Benefits Coordinator then reviews the information provided and utilizes the Nevada Secretary of State website: https://www.nvsos.gov/sos to verify the Act's requirements 31.5-2 section a, b, & c in regards to principal place of business, duration of business license, and that the required business license is current. Upon approval of these criteria, MMcJV will then give the contractor the designation of SBE. If firms do not meet the criteria or don't complete the process, they are not classified as SBE. A listing of all approved SBE's, or any of the above records can be provided upon request.









DATE: March 25, 2020

FROM: Lynn R. Littlejohn

RE: Allegiant Stadium

Community Benefits Plan Report – February 2020

SBE Program

• The SBE project goal is 15%.

- The current SBE participation is 24%.
- Approximately \$1.2 billion dollars of work has been awarded with \$301.1 million committed to SBE firms.
- 156 different SBE firms have been awarded work on the project; 45 with multiple contracts.
- 34 different WMBE firms have been awarded work on the project totaling \$68.7 million dollars.
- 76% of all firms awarded work on the project are Nevada based.

Workforce Diversity

- The workforce goal is 38% minority and female.
- The workforce participation is 62% minority/female and 2% veteran with approximately 4,278,869 hours worked through February
- 78% of the project workforce is Nevada residents.

Community Engagement and Outreach

 The project team participated in the Goodie Two Shoes program at William K Moore Elementary School where we outfitted approximately 450 disadvantaged children with new shoes and socks.

Attached are the SBE and workforce participation reports.



| cc | State | Subcontractor | Scope of Work | SBE/Other | Orig Contract \$ Amount | Original SBE \$ Commitment |
|----|-------|------------------------|--------------------------------------|-----------|----------------------------|-------------------------------|
| | NV | Lewis K. Construction | Fencing Repairs | SBE | \$ 19,360 | \$ 19,360 |
| | NV | Nevada Water Trucks | Track Out Pad Installation | SBE | \$ 10,000 | \$ 10,000 |
| | NV | Amazon Masonry | Dust Control | SBE/MBE | \$ 10,000 | \$ 10,000 |
| | NV | Tab Contractors, Inc. | Trailer Set-up & Geotech Fault Study | Other | \$ 748,450 | \$ 490,567 |
| | NV | Boulder Sand & Gravel | Aggregates | SBE | | |
| | NV | JS & S Surveying | Surveying | SBE/MBE | | |
| | NV | M Con | Utilities | SBE/MBE | | |
| | NV | Olson Precast Co. | Concrete Manhole | SBE | | |
| | NV | Acme Electric | Street Light Repairs | Other | | |
| | NV | Nevada Tap Master | Hot Taps | SBE | | |
| | NV | Merli Concrete Pumping | Box Culvert - Concrete Pump | SBE | | |
| | NV | National Trench Safety | Traffic Control | Other | | |
| | NV | Wells Cargo | Cold Mix, Reject Sand, Rock | Other | | |
| | NV | HD White Cap | Equipment Rental | Other | | |
| | NV | Cashman Equipment | Equipment Rental | Other | | |
| | NV | Sunstate | Sewer & Water Materials | Other | | |
| | NV | Ferguson Waterworks | Equipment Rental | Other | | |
| | NV | United Rentals | Concrete | Other | | |
| | NV | Nevada Ready Mix | Equipment Rental | Other | | |
| | NV | Ahern Rentals | Trucking Materials | Other | | |
| | NV | Werdco | Trucking Materials | Other | | |
| | NV | Diaz Trucking | Trucking Materials | Other | | |

| Original SBE Commitment % | Current Contract \$ Amount | SBE % | Awarded SBE \$Participation | Other \$Participation | Actual SBE \$ Paid | Actual Other \$ Paid |
|------------------------------|-------------------------------|-------|--------------------------------|-----------------------|-----------------------|-------------------------|
| 100% | \$ 21,838 | 100% | \$ 21,838 | | \$ 21,838 | \$ - |
| 100% | \$ 9,903 | 100% | \$ 9,903 | | \$ 9,903 | \$ - |
| 100% | \$ 11,495 | 100% | \$ 11,495 | | \$ 11,495 | \$ - |
| 66% | \$ 908,200 | 60% | | | | \$ 862,790 |
| | | | \$ 10,900 | | \$ 9,815 | |
| | | | \$ 28,190 | | \$ 20,088 | |
| | | | \$ 402,693 | | \$ 401,133 | |
| | | | \$ 14,738 | | \$ 14,738 | |
| | | | | \$ 4,033 | \$ - | \$ 4,033 |
| | | | \$ 1,560 | | \$ 1,560 | |
| | | | \$ 595 | | \$ 595 | |
| | | | | \$ 11,767 | | \$ 11,767 |
| | | | | \$ 3,090 | | \$ 3,090 |
| | | | | \$ 9,536 | | \$ 9,536 |
| | | | | \$ 5,016 | | \$ 5,016 |
| | | | | \$ 1,793 | | \$ 1,793 |
| | | | | \$ 84,388 | | \$ 84,388 |
| | | | | \$ 20,386 | | \$ 20,386 |
| | | | | \$ 7,954 | | \$ 7,954 |
| | | | | \$ 2,474 | | \$ 2,474 |
| | | | | \$ 2,764 | | \$ 2,764 |
| | | | | \$ 385 | | \$ 385 |



| cc | State | Subcontractor | Scope of Work | SBE/Other | Orig Contract \$ Amount | Original SBE \$ Commitment |
|------|-------|------------------------------|-----------------------------------|-----------|----------------------------|-------------------------------|
| | NV | Boulder Sand & Gravel | Type II | SBE | | |
| | NV | Hernandez Trucking | Trucking Materials | Other | | |
| | NV | HD Barricade | Traffic Control | Other | | |
| | NV | MMC, Inc. | Vactoring | Other | | |
| | NV | A-1 Concrete Cutting | Saw Cutting/Core Drilling/Demo | SBE/MBE | | |
| | NV | Wells Cargo, Inc. | Asphalt Paving | Other | | |
| | NV | Nevada Water Trucks | SWPPP & Dust Control Services | SBE | \$ 494,460 | \$ 494,460 |
| | NV | Cashman Professional | Photography | SBE | \$ 37,800 | \$ 37,800 |
| | NV | Eros Environmental | SWPPP Inspections | SBE | \$ 18,195 | \$ 18,195 |
| | NV | Preventive Measures | Site Security | SBE | \$ 100,000 | \$ 100,000 |
| | MN | Danny's Construction | Field Tray Mock-up | WBE | \$ 147,000 | \$ - |
| | NV | Trinity Land Survey | Surveying | SBE/WBE | | |
| 1.01 | TX | Derr & Isbell Construction | Personnel Hoist | Other | \$ 2,799,134 | \$ 419,870 |
| | NV | A&N Custom Fabrication | Misc. Metals | SBE | | |
| | TX | Beck Steel | Misc. Steel | Other | | |
| | NY | Extra Mile Transportation | Misc. Steel Items | Other | | |
| | NV | Fastenal | Mast Tools & Fasteners | Other | | |
| | NV | Hershberger Bros Welding | Mast Installation | SBE | | |
| | NV | Steel Partners | Fabrication of Bracing/Bridges | SBE | | |
| | TX | Walter P Moore | Construction Engineering & Design | Other | | |
| 1.01 | NV | Southwest Specialty Coatings | High Performance Coatings - Steel | SBE | \$ 1,000,000 | \$ 1,000,000 |
| | NV | Commercial Scaffolding of NV | Erect Scaffolding | SBE | | |
| | | | | | | |

| Original SBE Commitment % | Current Contract \$ Amount | SBE % | Awarded SB \$Participatio | | Actual SBE \$ Paid | Actual Other \$ Paid |
|------------------------------|-------------------------------|-------|------------------------------|------------------------|-----------------------|-------------------------|
| | | | \$ 7,7 | 17 | \$ 7,717 | \$ - |
| | | | | \$ 2,026 | | \$ 2,026 |
| | | | | \$ 8,575 | | \$ 8,575 |
| | | | | \$ 10,000 | | \$ 1,950 |
| | | | \$ 75,0 | 00 | \$ 360 | |
| | | | | \$ 31,200 | | \$ 29,710 |
| 100% | \$ 3,391,252 | 100% | \$ 3,391,2 | 52 | \$ 3,017,352 | |
| 100% | \$ 37,800 | 100% | \$ 37,8 | 00 | \$ 14,738 | |
| 100% | \$ 18,195 | 100% | \$ 18,1 | 95 | \$ 13,395 | |
| 100% | \$ 204,959 | 100% | \$ 204,9 | 59 | \$ 215,859 | |
| | \$ 2,768,830 | 100% | \$ 2,696,0 | 52 | \$ 2,576,952 | |
| | | | \$ 72,7 | 78 | | \$ 72,778 |
| 15% | \$ 2,764,797 | 25% | | | | \$ 2,626,557 |
| | | | \$ 5 | 68 | \$ 568 | 47.000 |
| | | | | \$ 17,963 \$ 30,000 | | \$ 17,963 \$ - |
| | | | | \$ 8,099 | | \$ 8,099 |
| | | | \$ 9 | 14 | \$ 944 | , ,,,,,, |
| | | | \$ 680,6 |)4 | \$ 680,604 | |
| | | | | \$ 104,235 | | \$ 104,235 |
| 100% | \$ 1,790,177 | 100% | \$ 1,778,9 | 10 | \$ 1,448,972 | \$ - |
| | | | \$ 11,2 | 57 | | |
| | | | | | | |



| СС | State | Subcontractor | Scope of Work | SBE/Other | Orig Contract \$ Amount | Original SBE \$ Commitment | |
|------|-------|--------------------------------|-------------------------------|-----------|----------------------------|-------------------------------|--|
| 1.01 | MI | Niles Industrial Coatings | Misc. Steel Painting | Other | \$ 165,000 | \$ 24,750 | |
| 1.01 | WI | Merrill Iron & Steel | Structural Steel | Other | \$ 179,413,551 | \$ 26,912,032 | |
| | TX | Derr & Isbell Construction | Steel Erection | Other | | | |
| | NV | Reliable Crane Service | Crane Operation & Maintenance | SBE | | | |
| | NV | Trinity Land Survey | Box Culvert - Survey | SBE/WBE | | | |
| | NV | Union Erectors, LLC | Steel Erection | SBE | | | |
| | СО | Derr & Gruenewald Construction | Steel Erection | Other | | | |
| | CA | The Herrick Corporation | Steel Erection | Other | | | |
| | NV | Ahern Rentals, Inc. | Equipment Rental | Other | | | |
| | CA | Barnhart Crane & Rigging | Rigging Equipment Rental | Other | | | |
| | NV | All-Star Building Services | Office Cleaning Services | Other | | | |
| | IN | Aarbee Structures | Detailing Services | Other | | | |
| | MT | ADF International | Various Fabrication Scope | Other | | | |
| | OR | Albina Pipe Bending | Bending Service | Other | | | |
| | MI | Alro Steel Corporation | Raw Material Supply | Other | | | |
| | WI | Amston Supply | Trailer Rental | Other | | | |
| | DE | Arcelormittal International | Raw Material Supply | Other | | | |
| | IL | Arcelormittal USA | Raw Material Supply | Other | | | |
| | NC | Armstrong Transport Group | Freight | Other | | | |
| | IL | Atlas Tube | HSS Tube & Pipe | Other | | | |
| | TN | Avenger Logistics | Freight | Other | | | |
| | со | AZZ Galvanizing Denver | Galvanizing | Other | | | |
| | WI | Baum Machine | Machining | Other | | | |
| | TX | Bedrock Logistics | Freight | Other | | | |
| | AZ | Bell Street | Fabrication Subcontractor | Other | | | |
| | | Black Diamond Pipe & Tube | Raw Material Supply | Other | | | |

| Original SBE Commitment % | Current Contract \$ Amount | SBE % | Awarded SBE \$Participation | Other \$Participation | Actual SBE \$ Paid | Actual Other \$ Paid |
|------------------------------|-------------------------------|-------|--------------------------------|-----------------------|-----------------------|-------------------------|
| 15% | \$ 184,200 | 15% | \$ 27,630 | | | |
| | | | | | | |
| 15% | \$ 237,741,213 | 22% | | | | \$ 223,035,925 |
| | | | | \$ 95,840,872 | | \$ 88,308,636 |
| | | | \$ 9,900,000 | | \$ 5,320,460 | |
| | | | \$ 1,000,000 | | \$ 990,668 | |
| | | | \$ 2,500,000 | | \$ 2,084,743 | |
| | | | | \$ 1,000,000 | | |
| | | | | \$ 500,000 | | |
| | | | | \$ 5,000,000 | | \$ 2,298,009 |
| | | | | \$ 212,007 | | \$ 212,007 |
| | | | | \$ 10,000 | | |
| | | | | \$ 7,111,619 | | \$ 7,111,619 |
| | | | | \$ 8,195,718 | | \$ 6,741,695 |
| | | | | \$ 28,708 | | \$ 28,708 |
| | | | | \$ 21,253 | | \$ 21,253 |
| | | | | \$ 234,362 | | \$ 234,362 |
| | | | | \$ 573,987 | | \$ 573,987 |
| | | | | \$ 187,422 | | \$ 187,422 |
| | | | | \$ 409,283 | | \$ 409,283 |
| | | | | \$ 1,847,527 | | \$ 1,847,527 |
| | | | | \$ 941,517 | | \$ 941,517 |
| | | | | \$ 26,809 | | \$ 26,809 |
| | | | | \$ 301,703 | | \$ 301,703 |
| | | | | \$ 530,876 | | \$ 530,876 |
| | | | | \$ 1,369,600 | | \$ 1,369,600 |
| | | | | \$ 141,790 | | \$ 141,790 |



| СС | State | Subcontractor | Scope of Work | SBE/Other | Orig Contract \$ Amount | Original SBE \$ Commitment |
|----|-------|--------------------------------|--|-----------|----------------------------|-------------------------------|
| | МО | Bourne Logistics Management | Freight | Other | | |
| | СО | Brown Strauss Co. | Raw Material Supply | Other | | |
| | IL | Chapel Steel | Material Supply | Other | | |
| | IL | Chicago Metal Rolled Products | Rolled Materials | Other | | |
| | VA | Cives Corporation | Fabrication Subcontractor | Other | | |
| | WI | Computerized Structural Design | Connection Design Services | Other | | |
| | SC | Con-Serv Inc. | Raw Material Supply | Other | | |
| | WA | Corona Stud & Deck | Deck Supply & Installation | Other | | |
| | IL | Custom Fab & Coatings | Fabrication Subcontractor | Other | | |
| | WI | D&S Machine Service, Inc. | Machining | Other | | |
| | SC | Erico International Corp. | Fasteners | Other | | |
| | NV | Expansion Specialties | Furnish & Install Expansion Joints at Stairs | SBE | | |
| | NV | Fasco | Fastener Supply & Delivery | SBE | | |
| | IL | FHS Consulting | Testing Service | Other | | |
| | MN | Gephart Morse | Temp Power | Other | | |
| | PA | Global Rope Access | Touch-up Field Painting & Cleaning | Other | | |
| | MT | HCA Transport | Freight | Other | | |
| | CA | The Herrick Corp. | Fabrication Subcontractor | Other | | |
| | NV | Hershberger Bros Welding | Misc. Fabrication Services | SBE | | |
| | МО | Hillsdale Fabricators | Fabrication Subcontractor | Other | | |
| | OK | Hilti | Anchors/Anchor Rods | Other | | |
| | AL | Independence Tube Corp. | Material Supplier | Other | | |
| | IL | Infra Metals | W, HSS, Plate, Raw Materials | Other | | |
| | UT | Interstate Gratings | Grating Supply | Other | | |
| | UT | Intsel Steel West | Raw Material Supply | Other | | |
| | AZ | JV Driver | Fabrication Subcontractor | Other | | |
| | ОН | Kenilworth Steel Co. | Raw Material Supply | Other | | |
| | KS | King of Freight LLC | Freight | Other | | |

| Original SBE Commitment % | Current Contract \$ Amount | SBE % | arded SBE articipation | Other \$Participation | Actual SBE \$ Paid | <i>A</i> | Actual Other \$ Paid |
|------------------------------|-------------------------------|-------|---------------------------|-----------------------|-----------------------|----------|-------------------------|
| | | | | \$ 17,035 | | \$ | 17,035 |
| | | | | \$ 585,914 | | \$ | 585,914 |
| | | | | \$ 134,748 | | \$ | 134,748 |
| | | | | \$ 22,420 | | \$ | 22,420 |
| | | | | \$ 874,701 | | \$ | 874,701 |
| | | | | \$ 163,195 | | \$ | 163,195 |
| | | | | \$ 257,022 | | \$ | 257,022 |
| | | | | \$ 5,952,613 | | \$ | 5,063,651 |
| | | | | \$ 992,542 | | \$ | 942,915 |
| | | | | \$ 115,766 | | \$ | 115,766 |
| | | | | \$ 17,399 | | \$ | 17,399 |
| | | | \$ 35,275 | | | | |
| | | | \$ 3,036,876 | | \$ 3,036,876 | 6 | |
| | | | | \$ 16,245 | | \$ | 16,245 |
| | | | | \$ 46,318 | | \$ | 46,318 |
| | | | | \$ 1,099,422 | | \$ | 321,182 |
| | | | | \$ 384,997 | | \$ | 384,997 |
| | | | | \$ 3,198,845 | | \$ | 3,198,845 |
| | | | \$ 2,882,882 | | \$ 2,882,882 | 2 | |
| | | | | \$ 265,388 | | \$ | 265,388 |
| | | | | \$ 82,431 | | \$ | 82,431 |
| | | | | \$ 91,438 | | \$ | 91,438 |
| | | | | \$ 221,158 | | \$ | 221,158 |
| | | | | \$ 408,459 | | \$ | 408,459 |
| | | | | \$ 321,877 | | \$ | 321,877 |
| | | | | \$ 2,780,813 | | \$ | 2,558,168 |
| | | | | \$ 134,898 | | \$ | 134,898 |
| | | | | \$ 607,773 | | \$ | 607,773 |



| СС | State | Subcontractor | Scope of Work | SBE/Other | Orig Contract \$ Amount | Original SBE \$ Commitment |
|----|-------|----------------------------|------------------------------------|-----------|----------------------------|-------------------------------|
| | IL | Kloeckner Metals - Chicago | Material Supplier | Other | | |
| | IA | Kloeckner Metals - Dubuque | Material Supplier | Other | | |
| | IL | Leeco Steel, LLC | Raw Material Supply | Other | | |
| | MN | LeJeune Steel Company | Fabrication Subcontractor | Other | | |
| | ОК | Love's Solutions | Freight | Other | | |
| | TX | Madden Bolt Corp. | Anchor Rod Assemblies | Other | | |
| | WI | Max Weiss | Rolled Materials | Other | | |
| | CA | McKinney Trailer Rentals | Trailer Rental | Other | | |
| | FL | Metals USA | Raw Material Supply | Other | | |
| | NV | Metro Trailer Leasing | Trailer Rental | Other | | |
| | МО | Milestone Trailer Leasing | Trailer Rental | Other | | |
| | NV | Mori Consulting | Raw Material Procurement | SBE/MBE | | |
| | WI | Monarch LLC | Machining | Other | | |
| | МО | Murphy Hoffman | Freight | Other | | |
| | AL | NAFCO | Fabrication Subcontractor | Other | | |
| | ОН | Nelson Stud Welding | Weld Studs | Other | | |
| | MI | Niles Industrial Coatings | Touch-up Field Painting & Cleaning | Other | | |
| | NV | NP Tropicana LLC | Lot Rentals | Other | | |
| | SC | Nucor Steel Berkeley | Raw Material | Other | | |
| | AR | Nucor Yamato Steel | WF Beams, Raw Material | Other | | |
| | AL | NuSteel Fabricators | Fabrication Subcontractor | Other | | |
| | IL | O'Brian Steel Service Co. | Raw Material | Other | | |
| | NC | Old Dominion Freight Line | Freight | Other | | |
| | IL | Olympic Steel | Material Supply | Other | | |
| | CA | PDM Steel Services | Material Supply | Other | | |
| | KS | PKM Steel Service | Fabrication Subcontractor | Other | | |
| | PA | PPG Industries | Raw Material | Other | | |
| | МО | Proenergy Crafts | Tradesmen | Other | | |

| Original SBE Commitment % | Current Contract \$ Amount | SBE % | Awarded SBE \$Participation | Other \$Participation | Actual SBE \$ Paid | Actual Other \$ Paid |
|------------------------------|-------------------------------|-------|--------------------------------|-----------------------|-----------------------|-------------------------|
| | | | | \$ 384,352 | | \$ 384,352 |
| | | | | \$ 110,840 | | \$ 110,840 |
| | | | | \$ 948,552 | | \$ 948,552 |
| | | | | \$ 520,577 | | \$ 520,577 |
| | | | | \$ 53,098 | | \$ 53,098 |
| | | | | \$ 4,992 | | \$ 4,992 |
| | | | | \$ 123,400 | | \$ 123,400 |
| | | | | \$ 243,068 | | \$ 243,068 |
| | | | | \$ 40,508 | | \$ 40,508 |
| | | | | \$ 118,511 | | \$ 118,511 |
| | | | | \$ 87,697 | | \$ 87,697 |
| | | | \$ 14,208,499 | | \$ 14,208,499 | |
| | | | | \$ 14,770 | | \$ 14,770 |
| | | | | \$ 301,820 | | \$ 301,820 |
| | | | | \$ 2,396,994 | | \$ 2,396,994 |
| | | | | \$ 8,961 | | \$ 8,961 |
| | | | | \$ 2,863,556 | | \$ 1,148,665 |
| | | | | \$ 253,000 | | \$ 253,000 |
| | | | | \$ 120,133 | | \$ 120,133 |
| | | | | \$ 1,520,127 | | \$ 1,520,127 |
| | | | | \$ 1,011,718 | | \$ 1,011,718 |
| | | | | \$ 276,744 | | \$ 276,744 |
| | | | | \$ 44,080 | | \$ 44,080 |
| | | | | \$ 155,736 | | \$ 155,736 |
| | | | | \$ 212,263 | | \$ 212,263 |
| | | | | \$ 737,467 | | \$ 737,467 |
| | | | | \$ 1,285,185 | | \$ 1,285,185 |
| | | | | \$ 263,399 | | \$ 263,399 |



| СС | State | Subcontractor | Scope of Work | SBE/Other | Orig Contract \$ Amount | Original SBE \$ Commitment |
|----|-------|---------------------------------|--|-----------|----------------------------|-------------------------------|
| | CA | RBC Lubron Bearing Systems | Bearing Supplier | Other | | |
| | NV | Rigging International Group | Primary Rope Access - Touch-up Field Painting & Cleaning | SBE | | |
| | WI | Russell Metals Williams Bahcall | Material Supply | Other | | |
| | NV | Ryan Transportation | Freight | Other | | |
| | AL | Saginaw Pipe Company | Raw Material Supply | Other | | |
| | TX | Service Steel Warehouse | Raw Material Supply | Other | | |
| | МО | South Side Machine Works | Machining | Other | | |
| | WI | SPE, Inc. | Tradesmen | Other | | |
| | SE | SSAB/IPSCO | Material Supplier | Other | | |
| | NV | Southwest Specialty Coatings | Touch-up Field Painting & Cleaning | SBE | | |
| | NV | Rigging International Group | Rigging - Rope Access | SBE | | |
| | KS | Steel & Pipe Supply | W, HSS, Plate, Raw Materials | Other | | |
| | IN | Steel Dynamics | W, C, L, Raw Materials | Other | | |
| | LA | Steel Fabricators of Monroe | Fabrication | Other | | |
| | NV | Steel Partners | Stair Supply | SBE | | |
| | МО | Steelman Transportation | Freight | Other | | |
| | TX | STI Group, Inc. | Fabrication Subcontractor | Other | | |
| | WI | Strohwig Industries | Machining | Other | | |
| | ОН | TQL | Freight | Other | | |
| | NV | Tradesmen International | Tradesmen | Other | | |
| | IN | Triad Metals International | Raw Material Supply | Other | | |
| | МО | Tubular Steel | HSS Tube & Raw Materials | Other | | |
| | NV | Union Erectors | Field Repairs | SBE | | |
| | KS | Unique Metal Fabrications | Fabrication Subcontractor | Other | | |
| | TX | Universal Steel America | Material Supplier | Other | | |
| | ОН | US Logistics LLC | Freight | Other | | |
| | AZ | VDS West | Fabrication Subcontractor | Other | | |
| | CA | West Coast Inspections | Shop Inspection Services | Other | | |

| Original SBE Commitment % | Current Contract \$ Amount | SBE % | varded SBE articipation | Ot | her \$Participation | А | ctual SBE \$ Paid | A | ctual Other \$ Paid |
|------------------------------|-------------------------------|-------|----------------------------|----|---------------------|----|----------------------|----|------------------------|
| | | | | \$ | 201,219 | | | \$ | 201,219 |
| | | | \$ 1,267,511 | | | \$ | 389,451 | | |
| | | | | \$ | 207,874 | | | \$ | 207,874 |
| | | | | \$ | 34,891 | | | \$ | 34,891 |
| | | | | \$ | 207,297 | | | \$ | 207,297 |
| | | | | \$ | 63,419 | | | \$ | 63,419 |
| | | | | \$ | 21,050 | | | \$ | 21,050 |
| | | | | \$ | 154,203 | | | \$ | 154,203 |
| | | | | \$ | 2,291,647 | | | \$ | 2,291,647 |
| | | | \$ 6,000,175 | | | \$ | 5,215,082 | | |
| | | | \$ 1,300,000 | | | | | | |
| | | | | \$ | 133,645 | | | \$ | 133,645 |
| | | | | \$ | 117,455 | | | \$ | 117,455 |
| | | | | \$ | 987,492 | | | \$ | 987,492 |
| | | | \$ 1,264,228 | | | \$ | 1,203,534 | | |
| | | | | \$ | 37,498 | | | \$ | 37,498 |
| | | | | \$ | 4,251,206 | | | \$ | 4,251,206 |
| | | | | \$ | 1,116,364 | | | \$ | 1,100,778 |
| | | | | \$ | 315,520 | | | \$ | 315,520 |
| | | | | \$ | 43,832 | | | \$ | 43,832 |
| | | | | \$ | 108,589 | | | \$ | 108,589 |
| | | | | \$ | 3,385,010 | | | \$ | 3,385,010 |
| | | | \$ 3,258,179 | | | \$ | 3,180,571 | | |
| | | | | \$ | 2,383,104 | | | \$ | 2,383,104 |
| | | | | \$ | 13,118 | | | \$ | 13,118 |
| | | | | \$ | 253,804 | | | \$ | 253,804 |
| | | | | \$ | 2,776,461 | | | \$ | 2,776,461 |
| | | | | \$ | 2,338,911 | | | \$ | 2,338,911 |



| СС | State | Subcontractor | Scope of Work | SBE/Other | Orig Contract \$ Amount | Original SBE \$ Commitment |
|-------|-------|------------------------------------|---|-----------|---|-------------------------------|
| | FL | Worldwide Specialty Logistics | Freight | Other | | |
| | NV | Xtra Lease LLC | Trailer Rental | Other | | |
| | WI | Zalk Josephs Fabricators | Fabrication | Other | | |
| | WI | ZMAC Transportation Solutions | Freight | Other | | |
| 1.02a | NJ | Vector Foiltec | ETF Roofing System | Other | \$ 29,701,944 | \$ 4,455,292 |
| | CA | Walter P Moore | Professional Engineering | Other | | |
| | IT | Cimolai S.P.A. | Material Supplies | Other | | |
| | NV | Union Erectors | Material Supplies | SBE | | |
| | NV | Reliable Crane Services | Equipment & Storage | SBE | | |
| | NV | General Design & Const. Co., Inc. | Plenum Material | SBE/MBE | | |
| | NV | TV Transport | Warehouse | SBE | | |
| | MN | Danny's Construction Co | ETFE Secondary Steel Erection | WBE | | |
| | NV | Dielco Crane | Crane Work | Other | | |
| | NV | Unforgettable Coatings | Painting | SBE | | |
| | PA | Global Mountain Solutions | Labor to Install EFTE Air Supply Units | Other | | |
| | MN | Harris Mechanical | Install EFTE Plenum Duct | Other | | |
| 1.02b | VA | Freyssinet, Inc. | Cable Net Roof Support | Other | \$ 31,600,000 | \$ 4,740,000 |
| | СН | Fatzer AG | Manufacture & Supply of Fully Locked coil Ropes | Other | , ,,,,,,,,,,,,,,,,,,,,,,,,,,,,,,,,,,,,, | , , , , , |
| | DE | Bollinger & Grohmann International | Design Services | Other | | |
| | MO | Thornton Tomasetti | Structural Engineering | Other | | |
| | NV | Kordt Engineering | PE Services of Permanent Works | SBE | | |
| | IT | CAVE S.R.L. | Manufacture & Supply of Cable Clamps | Other | | |
| | СН | HFE | Manufacture & Supply of Cable Struts | Other | | |
| | СН | CHINA Grand Engineering | Manufacture & Supply of Temporary Work Steel | Other | | |
| | NV | TV Transport | Yard - Rental, Security & Storage | SBE | | |
| | NV | Vision Construction Services | Crane Rental | SBE | | |
| | NV | Steel Partners, LLC | Installation | SBE | | |
| | NV | Rigging International Group | Rope Access | SBE | | |
| | NV | Southwest Specialty Coatings | Painting Struts | SBE | | |
| | LA | Aggreko, LLC | Electrical Supply | Other | | |

| Original SBE Commitment % | Current Contract \$ Amount | SBE % | arded SBE articipation | Other \$Participation | Actual SBE \$ Paid | A | Actual Other \$ Paid |
|------------------------------|-------------------------------|-------|---------------------------|-----------------------|-----------------------|----|-------------------------|
| | | | | \$ 1,364,893 | | \$ | 1,364,893 |
| | | | | \$ 1,343,323 | | \$ | 1,343,323 |
| | | | | \$ 115,532 | | \$ | 115,532 |
| | | | | \$ 18,625 | | \$ | 18,625 |
| | | | | | | | |
| 15% | \$ 36,295,005 | 15% | | | | \$ | 23,645,529 |
| | | | | \$ 840,325 | | \$ | 871,745 |
| | | | | \$ 7,325,193 | | \$ | 7,325,193 |
| | | | \$ 12,611 | | \$ 12,611 | | |
| | | | \$ 8,490 | | \$ 8,490 | | |
| | | | \$ 20,367 | | \$ 20,367 | | |
| | | | \$ 1,000,000 | | \$ 1,044,267 | | |
| | | | \$ 4,252,000 | | \$ 794,260 | | |
| | | | | \$ 700,000 | | | |
| | | | \$ 250,000 | | | | |
| | | | | \$ 89,000 | | | |
| | | | | \$ 50,000 | | | |
| | | | | | | | |
| 15% | \$ 34,988,541 | 22% | | | | \$ | 31,188,230 |
| | | | | \$ 3,848,988 | | \$ | 3,841,043 |
| | | | | \$ 431,332 | | \$ | 371,800 |
| | | | | \$ 175,831 | | \$ | 175,831 |
| | | | \$ 84,400 | | 84,400 | | |
| | | | | \$ 284,881 | | \$ | 272,919 |
| | | | | \$ 476,084 | | \$ | 476,084 |
| | | | | \$ 894,626 | | \$ | 847,516 |
| | | | \$ 473,070 | | 454,062 | | |
| | | | \$ 1,615,000 | | 1,397,354 | | |
| | | | \$ 4,721,256 | | 4,721,256 | | |
| | | | \$ 506,656 | | 221,534 | | |
| | | | \$ 180,705 | | 180,705 | | |
| | | | | \$ 140,000 | | | |



| CC | State | Subcontractor | Scope of Work | SBE/Other | Orig Contract \$ Amount | Original SBE \$ Commitment |
|------|-------|---------------------------------------|----------------------------------|-----------|----------------------------|-------------------------------|
| | TX | Roll-Lift USA, Inc. | Provide Equipment | Other | | |
| | NV | Desert Lumber | Supply Lumber | Other | | |
| | NV | Trinity Land Surveying, Inc. | Land Surveyor | SBE/WBE | | |
| | TX | Layher, Inc. | Tower Bare Rental | Other | | |
| | NV | Mojave Electric | On-Call Electrician | Other | | |
| | NV | Border Construction Specialties | Safety Supplier | Other | | |
| | NV | HD Supply Constuction Supply/WhiteCap | Safety Supplier | Other | | |
| 1.03 | NV | Sunstate Companies, LLC | PreCast | Other | \$ 25,129,767 | \$ 3,769,465 |
| | NV | Expansion Specialties | Caulking of PreCast | SBE/VBE | | |
| | NV | GM Construction, LLC | Erection of PreCast - Prior | Other | | |
| | NV | GM Construction, LLC | Erection of PreCast | SBE | | |
| | NV | GM Construction, LLC | Erection of PreCast - Lower Bowl | SBE | | |
| | NV | Westside Building Materials | Supplier | Other | | |
| | NV | Lowe's | Supplier | Other | | |
| | NV | Reliable Steel | Stud & Shield Welding | SBE | | |
| | CA | United Rentals Northwest | Rental | Other | | |
| | ОН | Tru-Fit Products of Utah | Field Supplies | Other | | |
| | NV | Fasteners | Field Supplies | Other | | |
| | UT | DJB Gas Service | Fuel | Other | | |
| | NV | Curtis Steel | Material | Other | | |
| | CA | California Tool Welding | Weld Supplies | Other | | |
| | NV | CES | Field Supplies | Other | | |
| | NV | AXT Transportation | Fuel | Other | | |
| | CA | Airgas West | Welding Gas | Other | | |
| | NV | Ahern Rentals | Rental | Other | | |
| | СТ | CS Unitec, Inc. | Field Supplies | Other | | |
| | NV | Home Depot | Field Supplies | Other | | |
| | NV | Red-O-Arc Welding | Field Equipment | Other | | |
| | NV | Southern Nevada Welding | Field Supplies | Other | | |
| | NV | PR Diamond Products | Field Small Tools | Other | | |
| | NV | Dielco Crane Services | Crane Services & Hydraulic Lifts | Other | | |
| | NV | Abatix | Supplier | Other | | |
| | WA | Amazon | Supplier | Other | | |
| | NV | Concrete Accessories | Supplier | SBE | | |
| | NV | BC Rope & Rigging | Supplier | SBE | | |
| | NV | Copper State Bolt & Nut Co. | Supplier | Other | | |

| Original SBE Commitment % | Current Contract \$ Amount | SBE % | varded SBE articipation | Other \$Participation | Actual SBE \$ Paid | A | Actual Other \$ Paid |
|------------------------------|-------------------------------|-------|----------------------------|-----------------------|-----------------------|----|-------------------------|
| | | | | \$ 234,535 | | | 234,535.00 |
| | | | | \$ 75,000 | | | 62,915.00 |
| | | | \$ 30,000 | | 25,337 | | |
| | | | | \$ 290,000 | | | 250,565.00 |
| | | | | \$ 55,000 | | | 43,225.00 |
| | | | | \$ 35,000 | | | 24,608.00 |
| | | | | \$ 30,000 | | | 29,011.00 |
| 15% | \$ 34,440,170 | 28% | | | | \$ | 31,432,591 |
| | | | \$ 205,000 | | \$ 158,175 | | |
| | | | | \$ 2,253,992 | | \$ | 2,253,992 |
| | | | \$ 4,945,867 | | \$ 4,169,781 | | |
| | | | \$ 3,674,876 | | \$ 3,674,876 | | |
| | | | | \$ 1,000 | | \$ | 36 |
| | | | | \$ 1,500 | | \$ | 1,332 |
| | | | \$ 550,000 | | \$ 536,310 | | |
| | | | | \$ 5,603 | | \$ | 5,603 |
| | | | | \$ 36,886 | | \$ | 36,886 |
| | | | | \$ 10,550 | | \$ | 10,550 |
| | | | | \$ 637 | | \$ | 637 |
| | | | | \$ 619 | | \$ | 619 |
| | | | | \$ 9,671 | | \$ | 9,671 |
| | | | | \$ 959 | | \$ | 959 |
| | | | | \$ 1,533 | | \$ | 1,533 |
| | | | | \$ 541 | | \$ | 541 |
| | | | | \$ 20,530 | | \$ | 20,530 |
| | | | | \$ 555 | | \$ | 555 |
| | | | | \$ 698 | | \$ | 698 |
| | | | | \$ 16,549 | | \$ | 16,549 |
| | | | | \$ 241 | | \$ | 241 |
| | | | | \$ 724 | | \$ | 724 |
| | | | | \$ 1,850,000 | | \$ | 1,824,523 |
| | | | | \$ 63,000 | | \$ | 62,045 |
| | | | | \$ 20,000 | | \$ | 16,800 |
| | | | \$ 50,000 | | \$ 26,395 | | |
| | | | \$ 3,000 | | \$ 2,542 | | |
| | | | | \$ 5,000 | | \$ | 350 |



| СС | State | Subcontractor | Scope of Work | SBE/Other | Orig Contract \$ Amount | Original SBE \$ Commitment |
|----|-------|------------------------------------|-----------------------------|-----------|----------------------------|-------------------------------|
| | NV | Core T Trucking | Supplier | Other | | |
| | NV | Fasteners, Inc. | Supplier | Other | | |
| | NV | Cutting Edge | Supplier | Other | | |
| | NV | Harbor Freight Tools | Supplier | Other | | |
| | NV | HD Supply Waterworks | Supplier | Other | | |
| | NV | McFadden-Dale Hardware | Supplier | Other | | |
| | MN | M.A. Mortenson Co. | Supplier | Other | | |
| | NV | Kuker Ranken Vegas | Supplier | Other | | |
| | NV | McIntosh Communications | Supplier | Other | | |
| | NV | Mobile Mini | Supplier | Other | | |
| | NV | Mobile Materials | Supplier | Other | | |
| | NV | Senergy Petroleum | Supplier | Other | | |
| | NV | Silver State Rope & Rigging | Supplier | Other | | |
| | NV | Steel Edge | Supplier | SBE | | |
| | NV | Precision Aggregate Products | Supplier | SBE | | |
| | OK | Hilti, Inc. | Supplier | Other | | |
| | NV | JS&S Surveying, Inc. | Suveying | SBE/MBE | | |
| | NV | Home Depot | Supplier | Other | | |
| | IL | U-Line | Supplier | Other | | |
| | NV | Monsen Engineering | Supplying Engineering Equip | Other | | |
| | IL | Reddaway, Inc. | Freight Charges | Other | | |
| | NV | JLB Land Surveying, LLC | Supplier | Other | | |
| | GA | Conac - Concrete Product Solutions | Supplier | Other | | |
| | NV | Standard Steel, LTD | Welding | Other | | |
| | NV | Commercial Hardward | Consumables | Other | | |
| | NV | Fasteners, Inc. | Consumables | Other | | |
| | NV | Terrible Herbst | Water/Ice | Other | | |
| | NV | Home Depot | Small Tools | Other | | |
| | NV | McFadden Dale Hardware | Consumables | Other | | |
| | NV | Praxair, Inc. | Consumables | Other | | |
| | NV | Walmart | Ice/Water | Other | | |
| | NV | Ahern Rentals | Equipment Rental | Other | | |
| | NV | Harbor Freight | Consumables | Other | | |
| | NV | Lowe's | Consumables | Other | | |
| | NV | Hilti | Small Tools | Other | | |
| | NV | United Rentals | Equipment Rental | Other | | |
| | NV | Dirtworks Positioning LLC | Supplier | Other | | |
| | NV | Border Construction | Supplier | Other | | |

| Original SBE Commitment % | Current Contract \$ Amount | SBE % | rded SBE ticipation | Other \$Participation | Actual SBE \$ Paid | Δ | Actual Other \$ Paid |
|------------------------------|-------------------------------|-------|------------------------|-----------------------|-----------------------|----|-------------------------|
| | | | | \$ 350 | | \$ | 350 |
| | | | | \$ 50,000 | | \$ | 35,064 |
| | | | | \$ 1,000 | | \$ | 455 |
| | | | | \$ 1,000 | | \$ | 594 |
| | | | | \$ 6,000 | | \$ | 5,250 |
| | | | | \$ 500 | | \$ | 213 |
| | | | | \$ 300,000 | | \$ | 299,703 |
| | | | | \$ 500 | | \$ | 182 |
| | | | | \$ 10,000 | | \$ | 9,138 |
| | | | | \$ 15,000 | | \$ | 10,159 |
| | | | | \$ 10,000 | | \$ | 4,967 |
| | | | | \$ 100,000 | | \$ | 41,064 |
| | | | | \$ 225,000 | | \$ | 222,488 |
| | | | \$ 150,000 | | \$ 80,752 | | |
| | | | \$ 40,000 | | \$ 11,661 | | |
| | | | | \$ 1,000 | | \$ | 196 |
| | | | \$ 177,408 | | \$ 46,680 | | |
| | | | | \$ 3,000 | | \$ | 2,641 |
| | | | | \$ 5,000 | | \$ | 4,001 |
| | | | | \$ 30,000 | | \$ | 28,678 |
| | | | | \$ 2,000 | | \$ | 435 |
| | | | | \$ 14,000 | | \$ | 13,215 |
| | | | | \$ 3,000 | | \$ | 2,387 |
| | | | | \$ 1,100,000 | | \$ | 1,096,665 |
| | | | | \$ 500 | | \$ | 36 |
| | | | | \$ 7,000 | | \$ | 4,940 |
| | | | | \$ 3,106 | | \$ | 3,106 |
| | | | | \$ 3,361 | | \$ | 1,347 |
| | | | | \$ 2,500 | | \$ | 1,226 |
| | | | | \$ 50,000 | | \$ | 38,773 |
| | | | | \$ 500 | | \$ | 96 |
| | | | | \$ 5,000 | | \$ | 3,101 |
| | | | | \$ 1,500 | | \$ | 53 |
| | | | | \$ 1,500 | | \$ | 208 |
| | | | | \$ 5,000 | | \$ | 4,984 |
| | | | | \$ 12,000 | | \$ | 11,864 |
| | | | | \$ 1,000 | | \$ | 244 |
| | | | | \$ 10,000 | | \$ | 436 |



| СС | State | Subcontractor | Scope of Work | SBE/Other | Orig Contract \$ Amount | Original SBE \$ Commitment |
|-----------|-------|--------------------------------------|--|-----------|----------------------------|-------------------------------|
| | NV | American Eagle Ready Mix | Supplier | Other | | |
| | NV | Ahern | Supplier | Other | | |
| | FL | Jim & Slims Tool Supply | Supplier | Other | | |
| | NM | Heatly Engineering | Design/Engineering of PreCast | Other | | |
| | NV | Western Pacific Precast, LLC | Precast Elements | Other | | |
| | NV | Mountain West Excavation & Utilities | Core Drilling | SBE/WBE | | |
| 1.04/1.05 | MN | Harris Companies | Mechanical & Plumbing | Other | \$ 121,500,000 | \$ 18,225,000 |
| | NV | Maui One Excavating | Trenching, Excating & Hauling | SBE/MBE | | |
| | NV | Lone Mountain Excavation | Site Prep | Other | | |
| | NV | Trinity Land Survey | Box Culvert - Survey | SBE/WBE | | |
| | NV | C-Los Industries | Warehouse Lease to Erect Oval Mock-up | SBE/MBE | | |
| | NV | Mechanical Equipment Reps | Provide Computer Room AC Units | SBE/MBE | | |
| | NV | Corporate Air Mechanical Services | Furnish 3 Pump Skids, 2 Head Exhcangers, 6 Domestic Heat Exchangers, 1 Triplex Booster Pump Package, 2 Rolairtrols | SBE | | |
| | NV | Corporate Air Mechanical Services | Furnish 6 Cell Stainless Cooling Tower w/Free Cooling and Single Flange Inlet | SBE | | |
| | NV | Corporate Air Mechanical Services | 7 Boilers | SBE | | |
| | NV | Corporate Air Mechanical Services | Supplies - Fans & PCU's | SBE | | |
| | NV | Corporate Air Mechanical Services | Furnish 35 Electric Water Heaters & 7 ASME 125# Storage Tanks | SBE | | |
| | NV | Corporate Air Mechanical Services | Provide 1 Lot Fabric Duct (Ductsox) & Associated hangers | SBE | | |
| | NV | Corporate Air Mechanical Services | Provide 26 Fire Smoke Dampers, 48 Fire Dampers & 6 Silencers | SBE | | |
| | NV | Corporate Air Mechanical Services | Provide 1 Lot Metal-Fab UL Listed Grease Duct, 1 Lot Metal-Fab UL Listed General Exhaust Flue, & 1 Lot Metal Fab UL Listed boiler Exhaust Flue | SBE | | |
| | NV | LTSA, LLC | Furnish air Handling Units;VAV's & BCU's | SBE | | |
| | NV | LTSA, LLC | Provide 26 Variable Frequency Drives with 3% Line Reactors & 20 Passive Harmonic Filters | SBE | | |
| | MN | Trane U.S., Inc. | Furnish & Install BAS Mechanical Control System | Other | | |
| | NV | Lawyer Mechanical Services | HVAC Controls Installation | SBE | | |
| | NV | Precision Automation | Low Voltage Controls HVAC Controls Installation | SBE | | |

| Original SBE Commitment % | Current Contract \$ Amount | SBE % | Awarded SBE \$Participation | Other \$Participation | Actual SBE \$ Paid | Actual Other \$ Paid |
|------------------------------|-------------------------------|-------|--------------------------------|-----------------------|-----------------------|-------------------------|
| | | | | \$ 20,000 | | \$ 16,800 |
| | | | | \$ 100,000 | | \$ 58,267 |
| | | | | \$ 500 | | \$ 55 |
| | | | | \$ 1,768,710 | | \$ 1,714,805 |
| | | | | \$ 18,591,763 | | \$ 18,238,039 |
| | | | \$ 10,000 | | | |
| | | | | | | |
| 15% | \$ 135,591,693 | 21% | | | | \$ 111,660,950 |
| | | | \$ 2,859,399 | | \$ 2,540,220 | |
| | | | | \$ 2,098,170 | | \$ 1,617,235 |
| | | | \$ 50,000 | | \$ 13,065 | |
| | | | \$ 5,412 | | \$ 5,412 | |
| | | | \$ 372,194 | | \$ 372,194 | |
| | | | 072,101 | | Ψ 072,104 | |
| | | | \$ 954,100 | | \$ 924,199 | |
| | | | | | | |
| | | | \$ 613,779 | | ¢ 507.274 | |
| | | | \$ 013,779 | | \$ 597,274 | |
| | | | \$ 403,133 | | \$ 372,690 | |
| | | | \$ 1,810,938 | | \$ 1,810,938 | |
| | | | A 407.070 | | ф 470 F00 | |
| | | | \$ 187,079 | | \$ 179,508 | |
| | | | \$ 1,021,488 | | | |
| | | | | | | |
| | | | \$ 87,400 | | | |
| | | | | | | |
| | | | | | | |
| | | | \$ 2,444,744 | | | |
| | | | | | | |
| | | | \$ 6,927,372 | | \$ 6,851,295 | |
| | | | ф 245.024 | | ф 200.702 | |
| | | | \$ 315,024 | | \$ 306,762 | |
| | | | | \$ 3,106,583 | | \$ 1,655,617 |
| | | | \$ 1,715,296 | | | |
| | | | | | | |
| | | | \$ 900,551 | | \$ 648,000 | |



| СС | State | Subcontractor | Scope of Work | SBE/Other | Orig Contract \$ Amount | Original SBE \$ Commitment |
|-------------|-------|------------------------------|--|-----------|----------------------------|-------------------------------|
| | NV | Advanced Controls & Electric | Low Voltage HVAC Controls Installation | SBE | | |
| | NV | Ideal Supply Company | Provide all Galvanized Victaulic Fittings Supplies | SBE | | |
| | NV | Energy Mechanical Insulation | Furnish & Install Plumbing Insulation | SBE/WBE | | |
| | NV | Energy Mechanical Insulation | Furnish & Install Piping Insulation | SBE/WBE | | |
| | NV | Energy Mechanical Insulation | Furnish & Install Mechanical Insulation | SBE/WBE | | |
| | NV | Energy Mechanical Insulation | Furnish & Install All Fire-Stopping on all Plumbing, Piping & Mechanical Systems | SBE/WBE | | |
| | NV | BrandSafway | Scaffolding erection & rental | Other | | |
| | NV | Superior Duct Fabrication | Fabricate & Supply all round ductwork Fittings | Other | | |
| | NV | Mesa Mechanical | Beverage Conduite & CO2 Branch Lines | SBE/WBE | | |
| | IL | BevStream Corp. | Beverage Conduit System & CO2 Branch lines | Other | | |
| | NV | Spider | Swing Stages | Other | | |
| | NV | Jcord, LLC | Saw Cutting and Core Drilling | SBE | | |
| | NV | MMC, Inc. | Vacuum Truck for Cleaning Sump Basins & Interceptors | Other | | |
| | NV | Tabitt | HVAC & Plumbing Testing, Adjusting & Balancing | Other | | |
| | NV | Commercial Scaffolding, Inc. | Provide Rental, Erection & Dismantle Scaffold | SBE | | |
| | ВС | Global Rope Access | Furnish, Install & Remove Rigging | Other | | |
| | NV | Rigging International | Furnish, Install & Remove Rigging | SBE | | |
| 1.06 & 4.08 | NV | Gephart/Morse | Electrical & Low Voltage | Other | \$ 85,793,108 | \$ 13,087,750 |
| | NV | Morse Electric | | | | |
| | NV | A-1 Concrete | Concrete & Excavation | SBE/MBE | | |
| | NV | MMC | Hydro Excavating | Other | | |
| | NV | Pyrocom | Sprinkler Monitoring Dialer | SBE/WBE | | |
| | NV | Hampton Tedder Electric | Electrical Testing | Other | | |
| | NV | Lone Mountain Excavation | Excavation | Other | | |
| | NV | Live Electric | Electrical | SBE/WBE | | |
| | NV | Westland State | Parking | Other | | |
| | NV | The Tiberti Fence Company | Drilling | SBE | | |
| | NV | Main Electric | Electrical Supplier | Other | | |
| | NV | Codale Energy | Electrical Supplier | Other | | |
| | CA | Industrial Electric Mftg | Electrical Distribution | Other | | |

| Original SBE Commitment % | Current Contract \$ Amount | SBE % | Awarded SBE \$Participation | Other \$Participation | Actual SBE \$ Paid | Actual Other \$ Paid |
|------------------------------|-------------------------------|-------|--------------------------------|-----------------------|-----------------------|-------------------------|
| | | | \$ 500,000 | | \$ 468,930 | |
| | | | \$ 2,868,918 | | \$ 2,797,425 | |
| | | | \$ 655,368 | | \$ 469,824 | |
| | | | \$ 1,456,925 | | \$ 907,998 | |
| | | | \$ 785,253 | | \$ 448,902 | |
| | | | \$ 736,959 | | \$ 530,683 | |
| | | | | \$ 38,563 | | \$ 38,563 |
| | | | | \$ 1,449,381 | | \$ 1,443,746 |
| | | | \$ 700,000 | | | |
| | | | | \$ 1,717,000 | | |
| | | | | \$ 38,278 | | |
| | | | \$ 160,000 | | | |
| | | | | \$ 20,000 | | |
| | | | | \$ 567,000 | | |
| | | | \$ 61,450 | | | |
| | | | | \$ 7,888 | | |
| | | | \$ 36,000 | | | |
| | | | | | | |
| 15% | \$ 152,205,738 | 15% | \$ 2,582,774 | | | \$ 107,941,444 |
| | | | \$ 127,418 | | \$ 127,418 | |
| | | | | \$ 10,450 | | \$ 10,450 |
| | | | \$ 8,860 | | \$ 8,860 | |
| | | | | \$ 1,250 | | \$ 1,250 |
| | | | | \$ 2,043,115 | | \$ 2,037,936 |
| | | | \$ 71,700 | ф 004 C27 | \$ 71,700 | ¢ 004.027 |
| | | | ¢ 27,002 | \$ 991,637 | ¢ 26.722 | \$ 991,637 |
| | | | \$ 27,003 | \$ 3,396,590 | \$ 26,722 | \$ 2,516,092 |
| | | | | \$ 2,119,434 | | \$ 995,439 |
| | | | | \$ 6,294,033 | | \$ 6,138,956 |



| СС | State | Subcontractor | Scope of Work | SBE/Other | Orig Contract \$ Amount | Original SBE \$ Commitment |
|----|-------|----------------------------------|--|-----------|----------------------------|-------------------------------|
| | NV | CESS | Generator/PDV's/Transfer Switches & Show Power, Broadcast Truck Power, Pedestals | SBE/MBE | | |
| | NV | National Field Services | Electrical Acceptance Testing & Studies | Other | | |
| | NV | General Design & Const. | Fabrication | SBE/MBE | | |
| | NV | Valley Steel | Unload and set Electrical Gear | SBE/WBE | | |
| | NV | Coherent Design | AV Design Assist, Testing & Commissioning | SBE | | |
| | NV | Johnson Controls Fire Protection | Fire Alarm System | Other | | |
| | PA | Tait Towers Manufacturing, LLC | Design Development for Speaker Array Rigging | Other | | |
| | NV | Clinton Nevada, LLC | Supply Commscope Cable | SBE | | |
| | NV | Well Equipment, Inc. | Supply Low Voltage Cabling Materials & Equipment | SBE | | |
| | ВС | Global Rope Access | Speaker Install, Infill speakers, Array speaker, cable pull | Other | | |
| | NV | Simply Connected, Inc. | Harman Order | Other | | |
| | NV | Jcord, LLC | Scanning/coredrilling | SBE | | |
| | NV | MD Electric | Torch Interior Electrical Fit Out | SBE/WBE | | |
| | MN | Gephart Electric, Inc. | | | | |
| | MN | Border States Supply | Electrical Supplies | Other | | |
| | NV | CESS | Cable Tray/Interior & Sports Lighting | SBE/MBE | | |
| | NV | Fastener & Supply Co., Inc | Electrical Supplies | Other | | |
| | IL | Global Equipment Company, Inc. | Electrical Supplies | Other | | |
| | MN | Graybar Electric Supply | Electrical Supplies | Other | | |
| | NV | Las Vegas Lighting | Feeder Cable & Branch Wire | SBE/MBE | | |
| | NV | Live Electric | Generator Distribution Feeds - Quad A, B, C & D | SBE/WBE | | |
| | MN | MA Mortenson | Equipment Rental | Other | | |
| | СО | National Lightning Protection | Lightning Protection System | Other | | |
| | NV | Nedco Supply | Electrical Supplies | Other | | |
| | MN | Povolny Specialties | Electrical Supplies | Other | | |
| | NV | Rosendin | Install MV Cables, Install & Terminate 600V Cables | Other | | |
| | MN | Total Tool Supply, Inc. | Electrical Material | Other | | |
| | MN | Viking Electric Supply | Electrical Supplies | Other | | |
| | NV | Brandsafeway Services | Level 350 Electrical Installation | Other | | |

| Original SBE Commitment % | Current Contract \$ Amount | SBE % | Awarded SBE \$Participation | Other \$Participation | Actual SBE \$ Paid | Actual Other \$ Paid |
|------------------------------|-------------------------------|-------|--------------------------------|-----------------------|-----------------------|-------------------------|
| | | | \$ 2,603,176 | | \$ 1,967,234 | |
| | | | | \$ 313,815 | | \$ 206,940 |
| | | | \$ 60,888 | | \$ 60,888 | |
| | | | \$ 31,350 | | \$ 31,350 | |
| | | | \$ 197,750 | | \$ 56,000 | |
| | | | | \$ 4,605,755 | | \$ 3,528,893 |
| | | | | \$ 24,150 | | |
| | | | \$ 2,155,174 | | \$ 1,264,601 | |
| | | | \$ 1,608,321 | | \$ 1,540,298 | |
| | | | | \$ 349,780 | | \$ 10,280 |
| | | | | \$ 3,045,759 | | \$ 2,778,849 |
| | | | \$ 2,800 | | | |
| | | | \$ 1,144,011 | | \$ 459,947 | |
| | | | | | | |
| | | | | \$ 79,595 | | \$ 78,928 |
| | | | \$ 9,541,033 | | \$ 3,015,251 | |
| | | | | \$ 121,319 | | \$ 121,319 |
| | | | | \$ 16,861 | | \$ 16,861 |
| | | | | \$ 67,504 | | \$ 46,613 |
| | | | \$ 1,343,141 | | \$ 613,239 | |
| | | | \$ 657,731 | | \$ 657,731 | |
| | | | | \$ 801,684 | | \$ 607,754 |
| | | | | \$ 127,040 | | |
| | | | | \$ 63,669 | | \$ 63,571 |
| | | | | \$ 37,478 | | \$ 36,610 |
| | | | | \$ 740,289 | | \$ 525,603 |
| | | | | \$ 21,262 | | \$ 19,551 |
| | | | | \$ 12,257 | | \$ 12,174 |
| | | | | \$ 39,456 | | \$ 39,456 |



| СС | State | Subcontractor | Scope of Work | SBE/Other | Orig Contract \$ Amount | Original S \$ Commite | |
|-----------|-------|--------------------------------|---|-----------|----------------------------|--------------------------|--------|
| | AZ | Communications Integrators | Electrical Supplies | Other | | | |
| | MN | Gopher Stage Lighting | Electrical Supplies | Other | | | |
| | NV | Jcord Construction Services | Pole Bases | SBE | | | |
| | NV | Merli Concrete Pumping | Concrete Pumping | SBE | | | |
| | NV | R.E.B Construction | Drill Foundations | Other | | | |
| | NV | DIG 3, LLC | Excavation | Other | | | |
| | NV | MMC, Inc. | Hydro Excavation | Other | | | |
| | TX | Vahle Electrifications Systems | Electrical | Other | | | |
| | MS | Sequel Electric Supply | Electrical Supplies | Other | | | |
| | | | | | | | |
| 1.07 | NV | Desert Fire Protection, LP | Fire Protection | Other | \$ 14,200,000 | \$ 2,13 | 30,000 |
| | NV | TAB Contractors | Underground Fire Line | Other | | | |
| | NV | Jcord Construction | GPR & Core Drill | SBE | | | |
| | NV | JS&S Inc. | Fire Sprinkler Layout with Trimble | SBE/MBE | | | |
| | NV | Lucky Transportation | Transportation | SBE | | | |
| | NV | Energy Mechanical Insulation | Fire Caulking & Insulation of Pipe | SBE | | | |
| | NV | Monsen Engineering Services | Plotter & Printing Supplies | SBE | | | |
| | NV | Silver State Marketing Group | Supply bulk Fire Sprinkler Material & Pipe & Fittings | SBE | | | |
| | NV | Lone Mountain Excavation | South FDC Underground | Other | | | |
| | NV | Carefree Catering | Site Water Delivery | SBE | | | |
| | NV | Ice Now NV, LLC | Ice & Water | SBE | | | |
| | NV | World Wide Safety | Safety | SBE/WMBE | | | |
| | | | Futuring Ourtain wall/Dilator | | | | |
| 1.08/1.09 | NV | Enclos Corp. | Exterior Curtainwall/Ribbon Rainscreen | Other | \$ 97,194,122 | \$ 14,62 | 20,335 |
| | NV | Innova Technologies | Structural Engineering/Material Mock-up | SBE/MBE | | | |
| | NV | Union Erectors | Steel Structure & Install Material Mock-up | SBE | | | |
| | NV | Affordable Federal Services | Misc. Construction Services | SBE | | | |
| | NV | Walters & Wolf | Storefront | Other | | | |
| | NC | Assa Abloy Entrance Systems | Door Auto Operators Supply & Install | Other | | | |
| | NV | Hershberger Bros Welding | Curtainwall Anchor & Steel Clips | SBE | | | |
| | NV | FASCO | Fasteners | SBE | | | |

| Original SBE Commitment % | Current Contract \$ Amount | SBE % | warded SBE Participation | Other \$Participation | Actual SBE \$ Paid | , | Actual Other \$ Paid |
|------------------------------|-------------------------------|-------|-----------------------------|-----------------------|-----------------------|----|-------------------------|
| | | | | \$ 199,118 | | \$ | 193,256 |
| | | | | \$ 1,620,383 | | \$ | 575,582 |
| | | | \$ 657,731 | | \$ 148,315 | | |
| | | | \$ 10,000 | | | | |
| | | | | \$ 60,000 | | | |
| | | | | \$ 70,000 | | | |
| | | | | \$ 5,000 | | | |
| | | | | \$ 26,745 | | | |
| | | | | \$ 15,799 | | \$ | 15,799 |
| | | | | | | | |
| 15% | \$ 15,075,987 | 16% | | | | \$ | 10,162,295 |
| | | | | \$ 115,655 | | \$ | 100,475 |
| | | | \$ 150,000 | | \$ 112,000 | + | |
| | | | \$ 6,312 | | \$ 6,312 | 1 | |
| | | | \$ 150,000 | | \$ 113,440 | + | |
| | | | \$ 100,000 | | \$ 74,256 | 1 | |
| | | | \$ 3,581 | | \$ 3,581 | | |
| | | | \$ 2,000,000 | | \$ 946,377 | | |
| | | | | \$ 92,394 | | \$ | 92,394 |
| | | | \$ 2,000 | | \$ 1,890 | | |
| | | | \$ 11,000 | | \$ 9,162 | | |
| | | | \$ 25,000 | | | | |
| | | | | | | | |
| 15% | \$ 101,585,116 | 18% | | | | \$ | 83,237,848 |
| | | | \$ 14,618 | | \$ 14,618 | | |
| | | | \$ 20,717 | | \$ 20,717 | | |
| | | | \$ 10,268,326 | | \$ 10,228,424 | | |
| | | | | \$ 2,041,571 | | | |
| | | | | \$ 47,250 | | | |
| | | | \$ 1,553,054 | | \$ 1,553,054 | | |
| | | | \$ 650,000 | | \$ 625,462 | | |



| СС | State | Subcontractor | Scope of Work | SBE/Other | Orig Contract \$ Amount | Original SBE \$ Commitment |
|-------|-------|----------------------------------|--|-----------|----------------------------|-------------------------------|
| | TX | Baker Metal | CW Metal Panels | Other | | |
| | NV | Expansion Specialties | Exterior Expansion Joint System | SBE/VBE | | |
| | NV | Gephart/Morse Electrical | Operable Door | Other | | |
| | NV | Union Erectors | Operable Door | SBE | | |
| | CA | Railworks Track Service | Welding on back for Operable Doors | Other | | |
| | NV | Team Construction | Grouting - operable door | Other | | |
| | NV | Reliable Crane Services | Crane Services | SBE | | |
| | CA | Construction Consulting Lab West | Field Testing | Other | | |
| | CA | Intertek-ATI | Field Testing | Other | | |
| 1.10 | NV | KONE | Elevator & Lifts | Other | \$ 17,942,010 | \$ 1,435,361 |
| | NV | Hightower Trucking, Inc. | Warehouse/Logistics Support | SBE/MBE | | |
| | NV | Storage on Wheels, Inc. | Jobsite Trailer | Other | | |
| | NV | CESS | Misc. Electrical Supplies | SBE/MBE | | |
| | TX | Platinum Specialty Services | Scaffolding | Other | | |
| | NV | Codale Electric Supply | Electrical Supplies | Other | | |
| | TX | Hutcherson Elevator Co. | Freight Elevator - D5, Install 6 hatch doors, 1 car gate | Other | | |
| | TX | Hutcherson Elevator Co. | Freight Elevator - C3, Install 7 hatch doors, 1 car gate | Other | | |
| | NV | Union Erectors | Furnish Material | SBE | | |
| | NV | Energy Mechanical Insulation | Firestopping | SBE/WBE | | |
| | NV | Jcord LLc | Drill holes to hang rigging to hoist escalator | SBE | | |
| | NV | Dielco Crane | Craning of the Escalators | Other | | |
| | NV | Ameripro Service Systems, Inc. | On-Site Fuel & Lube | Other | | |
| | MN | MA Mortenson Company | Equipment Rentals | Other | | |
| | NV | Fasco | Vendor/Bin Stak | SBE | | |
| | OK | Travertine | 17 - Elevator Cab Interiors | Other | | |
| | WA | Hankin Specialty Elevators | ADA Lifts | Other | | |
| 2.01a | NV | Trinity Land Survey | Box Culvert - Survey | SBE/WBE | \$ 38,770 | \$ 38,770 |

| Original SBE Commitment % | Current Contract \$ Amount | SBE % | A ¹ | warded SBE Participation | 0 | ther \$Participation | | Actual SBE \$ Paid | Α | ctual Other \$ Paid |
|------------------------------|-------------------------------|-------|----------------|-----------------------------|----|----------------------|----|-----------------------|----|------------------------|
| | | | | | \$ | 6,421,181 | | | \$ | 6,296,491 |
| | | | \$ | 725,570 | | | \$ | 237,738 | | |
| | | | | | \$ | 143,111 | | | | |
| | | | \$ | 4,502,176 | | | \$ | 4,264,639 | | |
| | | | | | \$ | 50,400 | | | \$ | 50,400 |
| | | | | | \$ | 103,777 | | | \$ | 103,777 |
| | | | \$ | 251,782 | | | \$ | 251,782 | | |
| | | | | | \$ | 15,000 | | | | |
| | | | | | \$ | 15,000 | | | | |
| 00/ | Ф 40.4C4.4C4 | 00/ | Φ. | 207.422 | | | | | Φ. | 44 000 074 |
| 8% | \$ 19,164,161 | 8% | \$ | 327,133 955,000 | | | \$ | 934,326 | \$ | 14,382,371 |
| | | | Ψ | 933,000 | ¢ | 15,000 | Ψ | 954,520 | ¢. | 4,249 |
| | | | | 74 500 | \$ | 15,000 | _ | 50.705 | \$ | 4,249 |
| | | | \$ | 71,500 | | | \$ | 59,705 | | |
| | | | | | \$ | 79,994 | | | \$ | 79,994 |
| | | | | | \$ | 15,000 | | | \$ | 11,898 |
| | | | | | \$ | 62,900 | | | | |
| | | | | | \$ | 70,100 | | | | |
| | | | \$ | 80,000 | | | \$ | 70,421 | | |
| | | | \$ | 75,000 | | | \$ | 16,787 | | |
| | | | \$ | 16,500 | | | \$ | 14,335 | | |
| | | | | | \$ | 6,500 | | | \$ | 4,250 |
| | | | | | \$ | 20,000 | | | \$ | 11,250 |
| | | | | | \$ | 260,000 | | | \$ | 77,440 |
| | | | \$ | 8,000 | | | \$ | 4,561 | | |
| | | | | | \$ | 463,741 | | | \$ | 218,769 |
| | | | | | \$ | 175,000 | | | | |
| | | | | | | | | | | |
| 100% | \$ 71,251 | 100% | \$ | 71,251 | | | \$ | 71,251 | | |
| | | | | | | | | | | |



| СС | State | Subcontractor | Scope of Work | SBE/Other | O | Orig Contract \$ Amount | | riginal SBE Commitment |
|-----------|-------|---------------------------|---|-----------|----|----------------------------|----|---------------------------|
| 2.01f | NV | Marnell Masonry | Box Culvert - Masonry | SBE | \$ | 33,198 | \$ | 33,198 |
| 2.01h | NV | Sahara Concrete | Box Culvert - Site Concrete, Paving & Hardscapes | SBE | \$ | 3,678,883 | \$ | 3,678,883 |
| | NV | CMC Rebar | Box Culvert - Reinforcing (Supply & Install) | Other | | | | |
| | NV | Dielco Crane Services | Box Culvert - Crane Work | Other | | | | |
| | NV | Merli Concrete Pumping | Box Culvert - Concrete Pump | SBE | | | | |
| | NV | A-1 Concrete | Demolition | SBE/MBE | | | | |
| 2.01k | NV | The Tiberti Fence Company | Box Culvert - Fence | SBE | \$ | 256,862 | \$ | 256,862 |
| | NV | Flippen's Trenching | 143 Holes | SBE | | | | |
| 2.02/2.03 | NV | Tab Contractors | Box Culvert /Earthwork/Site Utilities | Other | \$ | 15,258,168 | \$ | 10,707,010 |
| | NV | Brightview Landscape | Box Culvert - Landscape & Irrigation | Other | | | | |
| | NV | Sanders Construction | Drilling & Blasting | SBE | | | | |
| | NV | JS & S Surveying | Land Survey & Construction Staking | SBE/MBE | | | | |
| | NV | A-1 Concrete Cutting | Core Drilling/Concrete Cutting/Demolition | SBE/MBE | | | | |
| | NV | M Con, Inc. | Utility Work Installation | SBE/MBE | | | | |
| | NV | MMC, Inc. | Hydro Excavating/Vactor | Other | | | | |
| | NV | Nevada Ready Mix | Concrete | Other | | | | |
| | NV | Nelson Hiniker Striping | Traffic Control | SBE | | | | |
| | NV | Sticha Inc. | Trucking Materials | Other | | | | |
| | NV | National Trench Safety | Steel Plates & Shoring | Other | | | | |
| | МО | Core & Main | Water Materials | Other | | | | |
| | NV | Wells Cargo, Inc. | Asphalt Paving | Other | | | | |
| | NV | Merli Concrete Pumping | Pump Concrete | SBE | | | | |
| | NV | MMC, Inc. | Hydro Excavating/Pot Holing | Other | | | | |
| | NV | TAB Contractors | Excavating | Other | | | | |

| Original SBE Commitment % | Current Contract \$ Amount | SBE % | varded SBE articipation | Other \$Participation | | Actual SBE \$ Paid | Δ | actual Other \$ Paid |
|------------------------------|-------------------------------|-------|----------------------------|-----------------------|----|-----------------------|----|-------------------------|
| 100% | \$ 33,198 | 100% | \$ 33,198 | | \$ | 33,198 | | |
| | | | | | | | | |
| 100% | \$ 4,180,022 | 100% | \$ 3,919,506 | | \$ | 4,180,022 | | |
| | | | | \$ 794,604 | | | \$ | 794,604 |
| | | | | \$ 107,725 | | | \$ | 107,725 |
| | | | \$ 78,642 | - | \$ | 78,642 | | |
| | | | \$ 181,874 | | \$ | 181,874 | | |
| 1000/ | Φ 004.000 | 4000/ | 202.452 | | _ | 050.740 | | |
| 100% | \$ 294,882 | 100% | \$ 286,159 | | \$ | 259,719 | | |
| | | | \$ 8,723 | | \$ | 8,723 | | |
| 70% | \$ 29,058,644 | 45% | | | | | \$ | 26,443,959 |
| | | | | \$ 21,550 | | | \$ | 21,550 |
| | | | \$ 2,309,326 | | \$ | 2,193,860 | | |
| | | | \$ 409,688 | | \$ | 260,896 | | |
| | | | \$ 75,000 | | \$ | 73,635 | | |
| | | | \$ 435,993 | | \$ | 414,193 | | |
| | | | | \$ 18,550 | | | \$ | 18,550 |
| | | | | \$ 20,000 | | | \$ | 19,423 |
| | | | \$ 3,240 | | \$ | 3,240 | | |
| | | | | \$ 1,080 | | | \$ | 1,080 |
| | | | | \$ 285,000 | | | \$ | 522,277 |
| | | | | \$ 29,790 | | | \$ | 27,992 |
| | | | | \$ 77,527 | | | \$ | 68,555 |
| | | | \$ 639 | | \$ | 639 | | |
| | | | | \$ 866,257 | | | \$ | 866,257 |
| | | | | \$ 5,000 | | | \$ | 291 |



| сс | State | s procurement activity through Febr Subcontractor | Scope of Work | SBE/Other | Orig Contract \$ Amount | Original SBE \$ Commitment |
|----|-------|--|--|-----------|----------------------------|-------------------------------|
| | CA | Viking Drillers, Inc. | Abandonment (4) Monitoring Wells | Other | | |
| | NV | Acme Electric | Remove/Replace Street Lights | Other | | |
| | NV | Boulder Sand & Gravel | Gravel base for concrete & asphalt disposal | SBE | | |
| | NV | Elkhorn Environmental | Trucking/Street Sweeping | SBE | | |
| | NV | Donovan Brothers Trucking | Trucking/Haul-Off | SBE | | |
| | NV | Merli Concrete Pumping | Box Culvert - Concrete Pump | SBE | | |
| | NV | Olson PreCast Company | Install Storm Drain & Sewer MH & Drop Inlets | SBE | | |
| | NV | Armorock, LLC | Manhole Materials | Other | | |
| | NV | Nevada Tap Master | Wet Tap | SBE | | |
| | NV | Nevada Water Trucks | Water Truck | SBE | | |
| | NV | Enco Southwest, Inc. | Pump Controls | SBE | | |
| | NV | M Con, Inc. | Main Water Line | SBE/MBE | | |
| | NV | Ahern Rentals | Equipment Rental | Other | | |
| | NV | MMc Inc. | Vactor/Pothole Services | Other | | |
| | CA | Cashman Equipment Co. | Equipment Rental | Other | | |
| | TX | Aggregate Industries | Type II Supplier | Other | | |
| | МО | Core & Main | Material Supplier | Other | | |
| | NV | National Trench Safety | Shoring/Trench Plates | Other | | |
| | NV | Nevada Ready Mix | Concrete Supplier | Other | | |
| | NV | Rinker Materials | RPC Onsite/Offsite | Other | | |
| | NV | HD Barricade, Inc. | Traffic Control | Other | | |
| | NV | Sticha Inc. | Trucking | Other | | |
| | NV | Las Vegas Paving | Cold Mix | Other | | |
| | CA | HD White Cap | Safety Supplies | Other | | |

| Original SBE Commitment % | Current Contract \$ Amount | SBE % | Aw \$Pa | arded SBE articipation | Other \$Participation | Actual SBE \$ Paid | A | ctual Other \$ Paid |
|------------------------------|-------------------------------|-------|------------|---------------------------|-----------------------|-----------------------|----|------------------------|
| | | | | | \$ 8,800 | | \$ | 8,800 |
| | | | | | \$ 362,556 | | \$ | 362,556 |
| | | | \$ | 357,361 | | \$ 325,114 | | |
| | | | \$ | 2,384,021 | | \$ 2,384,021 | | |
| | | | \$ | 2,801,398 | | \$ 2,801,398 | | |
| | | | \$ | 10,000 | | \$ 2,979 | | |
| | | | \$ | 478,911 | | \$ 276,976 | | |
| | | | | | \$ 326,659 | | \$ | 326,659 |
| | | | \$ | 49,895 | | \$ 48,765 | | |
| | | | \$ | 265,877 | | \$ 265,877 | | |
| | | | \$ | 208,780 | | \$ 208,780 | | |
| | | | \$ | 3,060,201 | | \$ 2,283,025 | | |
| | | | | | \$ 12,000 | | \$ | 11,744 |
| | | | | | \$ 15,000 | | \$ | 13,825 |
| | | | | | \$ 4,478 | | \$ | 4,478 |
| | | | | | \$ 50,000 | | \$ | 45,089 |
| | | | | | \$ 675,000 | | \$ | 519,374 |
| | | | | | \$ 25,000 | | \$ | 19,019 |
| | | | | | \$ 20,000 | | \$ | 18,499 |
| | | | | | \$ 150,000 | | \$ | 132,896 |
| | | | | | \$ 2,500 | | \$ | 2,400 |
| | | | | | \$ 1,394 | | \$ | 1,338 |
| | | | | | \$ 2,500 | | \$ | 500 |
| | | | | | \$ 5,000 | | \$ | 5,131 |



| СС | State | Subcontractor | Scope of Work | SBE/Other | rig Contract \$ Amount | riginal SBE commitment |
|-----------|-------|-------------------------------|--|-----------|---------------------------|---------------------------|
| | NV | Olson Precast Company | 8" Meter Vaults | SBE | | |
| | NV | Nevada Tap Master | Hot Tap on Domestic Water Line | Other | | |
| | NV | Las Vegas Paving | Flaggers | Other | | |
| | NV | Wells Cargo, Inc. | Asphalt Patching | Other | | |
| | NV | Nelson Hiniker Striping | Striping/Traffic Control | SBE | | |
| | NV | Sahara Concrete | Concrete Repair | SBE | | |
| | | | | | | |
| 2.05 | CA | Malcolm Drilling | Deep Foundations | Other | \$ 8,630,311 | \$ 1,588,177 |
| | NV | CMC Steel | Reinforcing Steel | Other | | |
| | NV | Steel Edge, Inc. | Piles | SBE | | |
| | NV | Precision aggregate Products | Supply Grout for Deep Foundations | SBE | | |
| | NV | Trinity Land Survey | Box Culvert - Survey | SBE/WBE | | |
| | NV | Dielco Crane Service | Crane Lift Services | Other | | |
| | NV | TAB Contractors | Load Haul-off & Dispose ACIP Spoils | Other | | |
| | NV | Fugro USA Land | Osterberg Cell load testing equipment & services | Other | | |
| | NV | Clark Welding & Fabricating | Welding | Other | | |
| | NV | White Cap | General Building Materials | Other | | |
| | NV | United Rentals | Rental Equipment | Other | | |
| | NV | ммс | Potholing/Vac Truck Work | Other | | |
| | | | | | | |
| 2.99/3.99 | NV | Mortenson/McCarthy | Structural Concrete | Other | \$ 128,419,469 | \$ 19,262,920 |
| 3.99a | WI | Gateway Forming Systems | Horizontal Formwork | Other | | |
| | NV | Region 9 Safety | Safety Director | SBE/MBE | | |
| | NV | Pacific Construction Services | Shoring Rental/Lumber | SBE | | |
| 3.99b | NV | CMC Rebar | Reinforcing | Other | | |

| Original SBE Commitment % | Current Contract \$ Amount | SBE % | warded SBE Participation | Other \$Participation | Actual SBE \$ Paid | , | Actual Other \$ Paid |
|------------------------------|-------------------------------|-------|-----------------------------|-----------------------|-----------------------|----|-------------------------|
| | | | \$ 62,997 | | \$ 55,686 | | |
| | | | | \$ 1,500 | | | |
| | | | | \$ 692,289 | | \$ | 692,289 |
| | | | | \$ 160,565 | | \$ | 160,565 |
| | | | \$ 151,578 | | \$ 119,507 | | |
| | | | \$ 2,836 | | \$ 2,836 | | |
| | | | | | | | |
| 18% | \$ 10,729,892 | 26% | | | | \$ | 10,729,892 |
| | | | | \$ 2,200,385 | | \$ | 2,096,926 |
| | | | \$ 457,446 | | \$ 457,446 | | |
| | | | \$ 2,133,225 | | \$ 2,133,225 | | |
| | | | \$ 187,619 | | \$ 187,619 | \$ | - |
| | | | | \$ 20,353 | | \$ | 20,353 |
| | | | | \$ 221,790 | | \$ | 210,700 |
| | | | | \$ 205,817 | | \$ | 205,817 |
| | | | | \$ 51,702 | | \$ | 51,702 |
| | | | | \$ 44,503 | | \$ | 44,503 |
| | | | | \$ 20,791 | | \$ | 20,791 |
| | | | | \$ 1,125 | | \$ | 1,125 |
| | | | | | | | |
| 15% | \$ 142,926,934 | 25% | | | | \$ | 122,747,095 |
| | | | | \$ 15,128,319 | | \$ | 15,128,319 |
| | | | \$ 168,341 | | \$ 168,341 | | |
| | | | \$ 1,000,000 | | \$ 934,987 | | |
| | | | | \$ 21,337,720 | | \$ | 19,511,124 |



| CC | State | Subcontractor | Scope of Work | SBE/Other | Orig Contract \$ Amount | Original SBE \$ Commitment |
|----|-------|-------------------------------|-------------------------------------|-----------|----------------------------|-------------------------------|
| | NV | Steel Edge, Inc. | Reinforcing Steel | SBE | | |
| | NV | Precision Aggregate Products | Concrete | SBE | | |
| | NV | Merli Concrete | Concrete Pumping | SBE | | |
| | NV | Penhall Co. | Demolition | Other | | |
| | NV | Copper State Bolt & Nut Co. | Materials | Other | | |
| | NV | Jcord | Demolition | SBE | | |
| | NV | Ahern Rentals | Equipment Rental | Other | | |
| | AZ | Sunstate Equipment | Equipment Rental | Other | | |
| | CA | HD Supply | Supplies & Materials | Other | | |
| | NJ | Hilti | Small Tools , Materials & Equipment | Other | | |
| | TX | H & E Equipment | Equipment Rental | Other | | |
| | GA | Herc Rentals | Equipment Rental | Other | | |
| | NV | Lynco Associates | Epoxy & Rebar Enbeds | Other | | |
| | IL | CDW Direct, LLC | Technology Equipment | Other | | |
| | NV | Atlas Construction Supply | Column Formwork - Supplies | Other | | |
| | NV | BC Wire Rope & Rigging | Rigging Supplies | SBE | | |
| | NV | Pacific Construction Services | Lumber - Supplier | SBE | | |
| | NV | Construction Testing Services | Professional Services | Other | | |
| | NV | Concrete Accessories | Grout/Concrete - Supplier | SBE | | |
| | MN | Curtis 1000 Inc. | Materials | Other | | |
| | MN | ESCH Construction Supply | Materials | Other | | |
| | NV | FASCO | Materials | SBE | | |
| | NV | Fastenal Company | Materials | Other | | |
| | NV | Fasteners Inc. | Thread Supplier | Other | | |
| | NV | Glove Connection | Safety Equipment & Small Tools | SBE | | |

| Original SBE Commitment % | Current Contract \$ Amount | SBE % | | warded SBE Participation | Other \$Participation | | Actual SBE \$ Paid | A | Actual Other \$ Paid |
|------------------------------|-------------------------------|-------|----|-----------------------------|-----------------------|----|-----------------------|----|-------------------------|
| | | | \$ | 5,358,109 | | \$ | 5,358,109 | | |
| | | | \$ | 15,373,190 | | \$ | 14,776,088 | | |
| | | | \$ | 722,421 | | \$ | 719,911 | | |
| | | | | | \$ 80,648 | | | \$ | 80,648 |
| | | | | | \$ 10,000 | | | \$ | 6,052 |
| | | | \$ | 1,895,195 | | \$ | 1,759,127 | | |
| | | | | | \$ 40,000 | | | \$ | 22,512 |
| | | | | | \$ 5,000 | | | \$ | 3,694 |
| | | | | | \$ 40,000 | | | \$ | 25,480 |
| | | | | | \$ 91,329 | | | \$ | 91,329 |
| | | | | | \$ 20,000 | | | \$ | 6,934 |
| | | | | | \$ 30,000 | | | \$ | 15,116 |
| | | | | | \$ 54,000 | | | \$ | 46,420 |
| | | | | | \$ 35,000 | | | \$ | 10,933 |
| | | | | | \$ 1,500,000 | | | \$ | 354,037 |
| | | | \$ | 650,000 | | \$ | 355,214 | | |
| | | | \$ | 1,500,000 | | \$ | 1,108,614 | | |
| | | | | | \$ 100,000 | | | \$ | 88,076 |
| | | | \$ | 200,000 | | \$ | 169,806 | | |
| | | | | | \$ 3,450 | | | \$ | 1,205 |
| | | | | | \$ 5,000 | | | \$ | 2,573 |
| | | | \$ | 100,000 | | \$ | 55,765 | | |
| | | | | | \$ 2,450 | | | \$ | 348 |
| | | | | | \$ 200,000 | | | \$ | 160,735 |
| | | | \$ | 300,000 | | \$ | 252,140 | | |
| | | | ļΨ | - 550,000 | | Ψ | 202, 140 | | |



| СС | State | Subcontractor | Scope of Work | SBE/Other | Orig Contract \$ Amount | Original SBE \$ Commitment |
|----|-------|----------------------------------|-------------------------------|-----------|----------------------------|-------------------------------|
| | IL | Grainger | Construction Supplies | Other | | |
| | NJ | Hilti | Small Tools & Epoxy | Other | | |
| | WA | KR | Materials | Other | | |
| | СО | Smalley & Company | Water Stop Supplies | Other | | |
| | NV | HD Supply White Cap | Materials | Other | | |
| | NV | New Life Office LLC | Workstation Materials | Other | | |
| | PA | Norcen Industries | Materials | Other | | |
| | NV | NOVA Geotechnical & Inspection | Professional Services | Other | | |
| | МО | Office Essentials | Office Supplies | Other | | |
| | NV | Staples | Office Supplies | Other | | |
| | NV | William Vollmer | Materials | Other | | |
| | СО | RMD KWIKform North America | Materials | Other | | |
| | NV | M.J. Dean Construction | Concrete Forming | Other | | |
| | AZ | UFP Chandler, LLC | Materials | Other | | |
| | IL | Uline, Inc. | Materials | Other | | |
| | NV | Reliable Crane | Crane Rental | SBE | | |
| | NV | Eberhard SW Roofing | Water Stop Supplies | SBE | | |
| | NV | IQC Southwest, LLC | Quality Control - Inspections | Other | | |
| | NV | Artkore LLC | Materials | SBE | | |
| | NV | Commercial Scaffolding of Nevada | Stair Tower & Scaffolding | SBE | | |
| | NV | Union Erectors | Steel Corrections | SBE | | |
| | SD | Dakota Riggers & Tool Supply | Materials | Other | | |
| | NV | Fiber Tech Lifting Products | Materials | Other | | |
| | NV | Hershberger Bros Welding | Materials | SBE | | |
| | | June Rose, LLC | Materials | SBE | | |

| Original SBE Commitment % | Current Contract \$ Amount | SBE % | warded SBE Participation | Ot | her \$Participation | Actual SBE \$ Paid | A | Actual Other \$ Paid |
|------------------------------|-------------------------------|-------|-----------------------------|----|---------------------|-----------------------|----|-------------------------|
| | | | | \$ | 10,000 | | \$ | 5,944 |
| | | | | \$ | 500,000 | | \$ | 426,184 |
| | | | | \$ | 20,000 | | \$ | 8,248 |
| | | | | \$ | 10,500 | | \$ | 1,505 |
| | | | | \$ | 1,500,000 | | \$ | 1,337,457 |
| | | | | \$ | 42,000 | | \$ | 2,944 |
| | | | | \$ | 20,000 | | \$ | 1,826 |
| | | | | \$ | 20,000 | | \$ | 3,779 |
| | | | | \$ | 2,000 | | \$ | 380 |
| | | | | \$ | 10,000 | | \$ | 3,012 |
| | | | | \$ | 20,000 | | \$ | 2,756 |
| | | | | \$ | 2,500,000 | | \$ | 1,645,321 |
| | | | | \$ | 1,500,000 | | \$ | 1,143,842 |
| | | | | \$ | 25,500 | | \$ | 8,499 |
| | | | | \$ | 10,000 | | \$ | 3,269 |
| | | | \$ 7,000,000 | | | \$ 1,844,856 | | |
| | | | \$ 50,000 | | | \$ 43,434 | | |
| | | | | \$ | 500,000 | | \$ | 394,193 |
| | | | \$ 1,500 | | | \$ 602 | | |
| | | | \$ 500,000 | | | \$ 219,442 | | |
| | | | \$ 861,388 | | | \$ 861,388 | | |
| | | | | \$ | 3,450 | | \$ | 122 |
| | | | | \$ | 2,000 | | \$ | 217 |
| | | | \$ 10,000 | | | \$ 4,528 | | |
| | | | \$ 30,000 | | | \$ 9,434 | | |



| СС | State | Subcontractor | Scope of Work | SBE/Other | Orig Contract \$ Amount | Original SBE \$ Commitment |
|------|----------|--|---|--------------|----------------------------|-------------------------------|
| | MN | Mars Supply | Materials | Other | | |
| | NV | RGR Training Center | Safety Training | Other | | |
| | NV | Border Construction Specialties | Materials | Other | | |
| | GA | Global Equipment Co. | Materials | Other | | |
| | NV | Go2 Partners | Materials | Other | | |
| | MD | Canam Steel Corporation | Materials | Other | | |
| | NV | Mobile Materials, LLC | Materials | Other | | |
| | WA | Safeworks Holding, Inc. | Materials | Other | | |
| | NV | BrandSafway Services, LLC | Scaffolding | Other | | |
| | MN | Acme Tools | Small Tools | Other | | |
| | WA | Amazon Business | Misc. Supplies | Other | | |
| | NV | Ice Now | Ice & Water | SBE | | |
| | IL | Deslauries, Inc. | Equipment Rental | Other | | |
| | MN | Tforce Final Mile LLC | Materials | Other | | |
| | NV | GM Construction | Professional Services | SBE | | |
| | NV | ORR Safety Corp. | Safety Supplies | Other | | |
| | PA | Traffic Safety Store | Materials | Other | | |
| | NV | Silver Star Ready Mix | Site Concrete | Other | | |
| | NV | 84 Lumber Company | Materials | Other | | |
| | | | | | | |
| 3.01 | WA | Corona Stud & Deck, LLC | Scoreboard | Other | \$ 2,671,201 | \$ 400,680 |
| | NV | Crown Fabricators | Supply & Fabricate Misc. Steel & Handrail | SBE | | |
| | CA | EW Corporation Industrial Fabricators | Steel Fabrication | Other | | |
| 2.00 | T\/ | Compatio Continue In- | Fixed Section | Oth c :- | ¢ 0.005.404 | ¢ 4.000.700 |
| 3.02 | TX FL | Camatic Seating, Inc. Seating Installation Group | Fixed Seating Seating Installation | Other WBE | \$ 8,225,124 | \$ 1,233,769 |

| Original SBE Commitment % | Current Contract \$ Amount | SBE % | arded SBE articipation | Other \$Participation | Actual SBE \$ Paid | A | ctual Other \$ Paid |
|------------------------------|-------------------------------|-------|---------------------------|-----------------------|-----------------------|----|------------------------|
| | | | | \$ 5,000 | | \$ | 1,038 |
| | | | | \$ 20,000 | | \$ | 3,360 |
| | | | | \$ 30,000 | | \$ | 20,541 |
| | | | | \$ 10,000 | | \$ | 1,044 |
| | | | | \$ 5,000 | | \$ | 1,312 |
| | | | | \$ 10,000 | | \$ | 2,336 |
| | | | | \$ 20,000 | | \$ | 9,540 |
| | | | | \$ 200,000 | | \$ | 172,026 |
| | | | | \$ 392,092 | | \$ | 369,748 |
| | | | | \$ 5,000 | | \$ | 222 |
| | | | | \$ 5,000 | | \$ | 2,614 |
| | | | \$ 20,000 | | \$ 12,339 | | |
| | | | | \$ 20,000 | | \$ | 5,311 |
| | | | | \$ 5,000 | | \$ | 886 |
| | | | \$ 30,000 | | \$ 18,103 | | |
| | | | | \$ 20,364 | | \$ | 20,364 |
| | | | | \$ 5,000 | | \$ | 1,109 |
| | | | | \$ 1,200,000 | | \$ | 90,000 |
| | | | | \$ 15,000 | | \$ | 4,854 |
| | | | | | | | |
| 15% | \$ 3,120,981 | 15% | \$ 307,820 | | | \$ | 2,159,184 |
| | | | \$ 160,327 | | \$ 160,327 | | |
| | | | | \$ 683,830 | | \$ | 555,342 |
| 15% | \$ 8,225,124 | 17% | | | | \$ | 3,326,901 |
| 1070 | 0,220,124 | . 770 | \$ 1,372,383 | | \$ 185,521 | ۳ | 0,020,001 |



| СС | State | Subcontractor | Scope of Work | SBE/Other | rig Contract \$ Amount | riginal SBE Commitment |
|-----------|-------|-----------------------------------|---|-----------|---------------------------|---------------------------|
| | | | | | | |
| 3.03 | CA | Seda Seating Ltd. | Retractable Seating | Other | \$ 6,448,586 | \$ 967,288 |
| | NV | Union Erectors | Installation Labor on Retractable Seating Units | SBE | | |
| 3.04/3.10 | NV | Eberhard Southwest Roofing | Roofing & Waterproofing | SBE | \$ 4,259,219 | \$ 4,259,219 |
| | СО | Smalley & Company | Waterproofing Materials | Other | | |
| | NV | Construction Sealants Supply | Waterproofing Materials | SBE | | |
| | TX | StarFoam Manufacturing | Waterproofing Materials | Other | | |
| | CA | Sika Sarnafil | Roofing Materials | Other | | |
| | NV | Dielco Crane | Crane Service | Other | | |
| | | | | | | |
| 3.05 | NV | Union Erectors | Misc. Metals - Stairs | SBE | \$ 974,144 | \$ 974,144 |
| | IN | American Stairs Corp. | Stair Material Supplier | Other | | |
| | NV | Commercial Scaffolding | Provide Scaffold | SBE | | |
| | NV | Jcord, LLC | Drill Holes | SBE | | |
| | | | | | | |
| 3.06 | KS | Dimensional Innovations | Signature Tower | Other | \$ 580,823 | \$ 87,123 |
| | NV | Valley Steel, LLC | Fabrication & Installation for Al Davis Signature Tower | SBE/WBE | | |
| | NV | MD Electric | Torch Interior Electrical Fit Out | SBE/WBE | | |
| | NV | P1 Group | Torch Plumbing | Other | | |
| | NV | Gephart/Morse | Torch Interior Electrical Fit Out Supervision | Other | | |
| | NV | GM Construction | Grout for Torch Base | SBE | | |
| | NV | Casas Electric | Electrical Engineering of Signature Tower | SBE | | |
| | | | | | | |
| 3.08a | TN | Industrial Door Contractors (IDC) | Operable Field Mechanization | Other | \$ 17,160,597 | \$ 2,600,000 |
| | MN | Danny's Construction Co., LLC | Installation of Field Tray | WBE | | |
| | NV | Dielco Crane | Crane Work | Other | | |
| | NV | Trinity Land Surveying | Field Survey & Layout | SBE/WBE | | |

| Original SBE Commitment % | Current Contract \$ Amount | SBE % | | warded SBE Participation | Oth | er \$Participation | | Actual SBE \$ Paid | Α | Actual Other \$ Paid |
|------------------------------|-------------------------------|-------|----|-----------------------------|-----|--------------------|----|-----------------------|----|-------------------------|
| | | | | | | | | | | |
| 15% | \$ 6,815,659 | 15% | \$ | 1,022,349 | | | | | \$ | 4,078,911 |
| | | | \$ | 328,495 | | | | | | |
| | | | | | | | | | | |
| 100% | \$ 5,826,932 | 100% | \$ | 5,361,932 | | | \$ | 2,561,733 | | |
| | | | | | \$ | 60,000 | | | \$ | 52,700 |
| | | | \$ | 465,000 | | | \$ | 460,735 | | |
| | | | · | , | Φ. | 07.000 | Ť | | Φ. | 04.507 |
| | | | | | \$ | 67,000 | | | \$ | 64,527 |
| | | | | | \$ | 1,400,000 | | | \$ | 809,519 |
| | | | | | \$ | 80,000 | | | \$ | 56,217 |
| | | | | | | | | | | |
| 100% | \$ 8,364,766 | 100% | \$ | 8,355,282 | | | \$ | 6,494,578 | | |
| | | | | | \$ | 663,039 | | | \$ | 527,419 |
| | | | \$ | 6,784 | | | \$ | 2,731 | | |
| | | | \$ | 2,700 | | | \$ | 2,700 | | |
| | | | Ψ | 2,700 | | | Ψ | 2,700 | | |
| 15% | \$ 15,201,880 | 15% | \$ | 469,343 | | | | | \$ | 8,212,593 |
| | | .07 | | | | | | | | |
| | | | \$ | 1,730,853 | | | \$ | 521,107 | | |
| | | | \$ | 65,000 | | | | | | |
| | | | | | \$ | 81,300 | | | | |
| | | | | | \$ | 10,010 | | | | |
| | | | \$ | 7,836 | | | | | | |
| | | | | | | | | | | |
| | | | \$ | 7,250 | | | \$ | 7,250 | | |
| | | 4 | | | | | | | | |
| 15% | \$ 17,702,221 | 17% | | | | | | | \$ | 15,641,624 |
| | | | | | \$ | 3,536,483 | | | \$ | 3,336,737 |
| | | | | | \$ | 38,550 | | | | |
| | | | \$ | 72,779 | | | \$ | 72,779 | | |



| CC | State | Subcontractor | Scope of Work | SBE/Other | Orig Contract \$ Amount | Original SBE \$ Commitment |
|-------|-------|------------------------------------|--|-----------|----------------------------|-------------------------------|
| | PA | Gantrex Inc. | Thermite Welding | Other | | |
| | NV | Mori Consulting | Supplier | SBE/MBE | | |
| | NV | Gephart/Morse | Mechanized Field Tray Wiring | Other | | |
| | | | | | | |
| | NV | FSI/Flooring Solutions of NV, Inc. | Mondo for mock-up plus field tray | SBE | | |
| | MN | Harris | Drainage System for the Field Tray | Other | | |
| | NV | Southwest Specialty Coatings | Surface preparation and coating of field tray | SBE | | |
| 3.08b | NV | McKeon Door of Nevada, Inc. | Operable Field Door Mechanization | Other | \$ 475,967 | \$ 126,735 |
| | NV | Mojave Electric | Electrical | Other | | |
| | NV | Clear Solutions Group | Material (glass) Supplier | SBE | | |
| | NV | MJDean/Southwest Door & Hardware | Doors, Frames & Hardware | Other | | |
| | CA | Moderco Inc. | Panel Operable Wall - Supplier | Other | | |
| 3.08c | CA | Show Canada Industries | Retractable Columns | Other | \$ 1,701,160 | \$ 255,174 |
| | NV | Daniel K Sobel | Project Management | SBE | | |
| | NV | JS & S Surveying | Survey for Retractable Columns | SBE/MBE | | |
| | NV | MD Electric Inc. | Low Voltage Installation For Retractable Columns | SBE/WBE | | |
| | NV | Union Erectors | Installation Labor for Retractable Columns | SBE | | |
| 3.09 | NV | Gephart/Morse | Distributed Antenna System (DAS) | Other | \$ 3,000,000 | \$ 450,000 |
| | | Morse Electric | | | | |
| | NV | MD Electric | DAS Conduit | SBE/WBE | | |
| | NV | CESS | DAS Generator, ATS, PDU | SBE/MBE | | |
| | NV | General Design & Construction | Multi Brackets & Compression Plates | SBE/MBE | | |
| | NV | Clinton Nevada | Cabling Supplier/Distributor | SBE | | |
| | CA | Industrial Electric Mfg. | Electrical Switchgear | Other | | |
| | NY | JMA Wireless | Wireless Components | Other | | |
| | NV | Well Equipment, Inc. | Electrical Material | SBE | | |
| | | | | | | |

| Original SBE Commitment % | Current Contract \$ Amount | SBE % | | varded SBE articipation | Other \$Participation | Actual SBE \$ Paid | A | Actual Other \$ Paid |
|------------------------------|-------------------------------|-------|----------|-------------------------|-----------------------|-----------------------|----|-------------------------|
| | | | | | \$ 172,459 | | \$ | 172,459 |
| | | | \$ | 2,703,105 | | \$ 2,703,105 | | |
| | | | | | \$ 328,225 | | \$ | 135,000 |
| | | | \$ | 99,075 | | | | |
| | | | | | \$ 44,831 | | \$ | 35,599 |
| | | | \$ | 66,193 | | | | |
| | | | | | | | | |
| 27% | \$ 483,316 | 26% | | | | | \$ | 300,342 |
| | | | | | \$ 29,210 | | | |
| | | | \$ | 126,735 | | \$ 126,735 | | |
| | | | | | \$ 60,186 | | | |
| | | | | | \$ 22,043 | | | |
| 15% | \$ 1,900,939 | 15% | Ф. | 92,141 | | | \$ | 1 420 924 |
| 1070 | \$ 1,900,939 | 1070 | \$ \$ | 163,000 | | \$ 108,000 | Φ | 1,439,824 |
| | | | \$ | 10,000 | | | | |
| | | | \$ | 10,000 | | | | |
| | | | \$ | 10,000 | | | | |
| | | | | | | | | |
| 15% | \$ 28,422,299 | 15% | | | | | \$ | 11,850,758 |
| | | | | | | | | |
| | | | \$ | 1,212,257 | | \$ 1,127,107 | | |
| | | | \$ | 16,593 | | | | |
| | | | \$ | 98,310 | | \$ 30,836 | | |
| | | | \$ | 2,500,835 | | \$ 737,454 | | |
| | | | | | \$ 99,160 | | \$ | 99,073 |
| | | | | | \$ 2,015,565 | | \$ | 1,971,344 |
| | | | \$ | 495,244 | | | | |
| | | | | | | | | |



| СС | State | Subcontractor | Scope of Work | SBE/Other | Orig Contract \$ Amount | Original SBE \$ Commitment |
|-----------|-------|-----------------------------------|--|-----------|----------------------------|-------------------------------|
| 3.11/4.01 | NV | Performance Contracting, Inc. | Exterior & Interior Framing/Drywall | Other | \$ 40,095,890 | \$ 6,025,279 |
| | NV | Commercial Scaffolding | Erection/dismantle of Scaffold | SBE | | |
| | NV | Gale Building Products | Insulation and Firestopping | Other | | |
| | NV | Lochsa Engineering | Engineering Services | Other | | |
| | NV | R&P Supply | Framing, Drywall, Taping | SBE | | |
| | NV | Technicoat Management | Interior Moisture Barrier | SBE | | |
| | NV | Tomarco Fastening Systems, Inc. | Fasteners | Other | | |
| | NV | Legacy Cast & Stone & Composites | Ceiling Shapes | SBE | | |
| | NV | Herman Truck Lines, LLC | Metal Decking/Trucking | SBE | | |
| | NV | MPS Plastic Wall Products | FRP | SBE | | |
| 4.02 | NV | CEDCO, Inc. | Masonry | Other | \$ 5,258,412 | \$ 861,346 |
| | NV | A Track-Out Solutions | Material Purchasing Delivery | SBE/WBE | | |
| | NV | JS & S Surveying | Survey - CMU Wall Control Layout | SBE/MBE | | |
| | NV | Technicoat Management | Fire Stop/Joint Sealants | SBE | | |
| | NV | Region 9 Safety Compliance | Safety Coordinator | SBE/MBE | | |
| | CA | Epic CAD Solutions | Providing 3D Modeling | Other | | |
| | NV | Silver Star Ready Mix | Supplying of Masonry Grout | Other | | |
| | NV | JCord Construction | CMU Wall Demolition | SBE | | |
| 4.03 | NV | American Door Installation, LP | Frames, Doors & Hardware | SBE | \$ 595,725 | \$ 595,725 |
| | NV | The Hallgren Co. | Supply Frames, Doors & Hardware | Other | | |
| 4.03 | NV | The Hallgren Company of Las Vegas | Door Hardware | Other | \$ 348,030 | |
| 4.04 | NV | Giroux Glass, Inc. | Decorative Glazing & Mirrors | Other | \$ 2,161,805 | \$ 324,271 |
| | NV | Glass Supply, Inc. | Supplying Architectural Mirror Fabricated to size | SBE | | |
| 4.04 | NV | Davis Glass & Mirror | Storefront Curtain Wall Entrances | SBE | \$ 1,850,406 | \$ 1,850,406 |
| | | Tepco Glass | Level 400 Motorized Windows | Other | | |
| | | | | | | |

| Original SBE Commitment % | Current Contract \$ Amount | SBE % | Awarded SBE \$Participation | Other \$Participation | Actual SBE \$ Paid | Actual Other \$ Paid |
|------------------------------|-------------------------------|-------|--------------------------------|-----------------------|-----------------------|-------------------------|
| 15% | \$ 48,221,605 | 15% | | | | \$ 33,698,738 |
| | | | \$ 1,367,818 | | \$ 331,674 | |
| | | | | \$ 1,926,360 | | \$ 899,122 |
| | | | | \$ 113,600 | | \$ 113,600 |
| | | | \$ 4,300,000 | | \$ 692,707 | |
| | | | \$ 359,710 | | \$ 189,687 | |
| | | | | \$ 117,527 | | \$ 117,527 |
| | | | \$ 35,856 | | \$ 35,856 | |
| | | | \$ 200,000 | | \$ 170,472 | |
| | | | \$ 900,000 | | | |
| 16% | \$ 4,907,004 | 24% | | | | \$ 4,581,328 |
| | | | \$ 855,500 | | \$ 502,990 | |
| | | | \$ 30,000 | | \$ 27,472 | |
| | | | \$ 158,710 | | \$ 75,157 | |
| | | | \$ 115,000 | | \$ 113,453 | |
| | | | | \$ 50,000 | | \$ 46,695 |
| | | | | \$ 280,000 | | \$ 136,093 |
| | | | \$ 41,610 | | \$ 41,610 | |
| 100% | \$ 3,090,198 | 100% | \$ 3,090,198 | | \$ 1,946,899 | |
| | | | | \$ 1,905,191 | | \$ 1,556,476 |
| | | | | | | |
| | \$ 348,030 | | | \$ 348,030 | | \$ 330,629 |
| 15% | \$ 3,438,557 | 15% | \$ 186,181 | | | \$ 421,893 |
| | | | \$ 329,603 | | | |
| 4000/ | C 4.044.040 | 4000/ | 6 4.040.004 | | ¢ 400.400 | |
| 100% | \$ 1,341,210 | 100% | \$ 1,316,284 | \$ 442.045 | \$ 192,122 | |
| | | | | \$ 113,845 | | |



| СС | State | Subcontractor | Scope of Work | SBE/Other | Orig Contract \$ Amount | | riginal SBE Commitment |
|-------|-------|---|---|-----------|----------------------------|------|---------------------------|
| | NV | Sunstone Building Specialties | TV Booth Operable Windows | SBE | | | |
| | | | | | | | |
| 4.05 | GA | Raydeo Enterprises, Inc. | Stadium Railings | Other | \$ 11,524,35 | 8 \$ | 2,751,947 |
| | GA | East Gate Pallets | Pallets | Other | | | |
| | GA | G&F Southeast Distributors Inc. | Stainless Steel Cable & Hardware | Other | | | |
| | NV | Innova Technologies | Engineering | SBE | | | |
| | IL | McMaster Carr | Misc. Hardware | Other | | | |
| | WI | R&B Wagner | Core Cups, Cladding Tape, End Caps, Panel Grip, Handrail Brackets | Other | | | |
| | TX | Ryerson | Steal Flat & Steal Tube | Other | | | |
| | NV | Steel Partners | Panel Grip, Gaskets & Glass Shoe | SBE | | | |
| | GA | Stewart Stainless Supply | Stainless Steel Pipe & Sheets | Other | | | |
| | CA | Glassworks LA, Inc. | Glass | Other | | | |
| | NV | Expansion Specialties | Caulk & Grout | SBE/VBE | | | |
| | NV | Standard Steel | Installation | Other | | | |
| | NV | Trinity Land Surveying | Field Survey & Layout | SBE/WBE | | | |
| 4.06 | NV | Creative Play Recreation | Shade Canopies | SBE | \$ 1,206,09 | 7 \$ | 1,206,09 |
| 4.06 | NV | Valley Steel LLC | North End Zone Camera Platform at Catwalk | SBE/WBE | \$ 123,48 | 7 \$ | 123,48 |
| 4.07 | NV | Expansion Specialties | Expansion Joints | SBE/VBE | \$ 1,640,55 | 0 \$ | 1,640,55 |
| | KS | Balco, Inc. | Material Supplier | Other | ψ 1,010,00 | • • | .,0.0,00 |
| | MA | Emseal Joint System, Ltd. | Material Supplier | Other | | | |
| | WI | Inpro Corporation | Material Supplier | Other | | | |
| 4.08f | MN | Alpha Video Sports & Entertaiment Group | Video Production Systems | Other | \$ 7,499,81 | 5 \$ | 74,99 |
| | IL | Clark Wire and Cable | Control Room Equipment Supplier | Other | | | |
| | CA | Bittree In. | Control Room Equipment Supplier | Other | | | |
| | NY | Tecnec Distributing | Control Room Equipment Supplier | Other | | | |
| | СО | Wesco Broadcast & Entertainment | Control Room Equipment Supplier | Other | | | |
| | MA | Superlogics Inc. | Control Room Equipment Supplier | Other | | | |
| | NY | Dale Electronics | Control Room Equipment Supplier | Other | | | |

| Original SBE Commitment % | Current Contract \$ Amount | SBE % | varded SBE Participation | Other \$Participation | Actual SBE \$ Paid | А | ctual Other \$ Paid |
|------------------------------|-------------------------------|-------|-----------------------------|-----------------------|-----------------------|----|------------------------|
| | | | \$ 24,926 | | | | |
| | | | | | | | |
| 24% | \$ 12,379,319 | 15% | \$ 353,178 | | | \$ | 6,158,525 |
| | | | | \$ 40,000 | | \$ | 11,306 |
| | | | | \$ 198,000 | | \$ | 165,360 |
| | | | \$ 65,000 | | \$ 60,219 | | |
| | | | | \$ 20,000 | | \$ | 13,539 |
| | | | | \$ 337,308 | | \$ | 8,689 |
| | | | | \$ 200,000 | | \$ | 143,289 |
| | | | \$ 1,264,070 | | \$ 1,264,070 | | |
| | | | | \$ 325,000 | | \$ | 232,219 |
| | | | | \$ 456,860 | | \$ | 296,110 |
| | | | \$ 152,650 | | \$ 36,480 | | |
| | | | | \$ 1,000,000 | | | |
| | | | \$ 22,000 | | | | |
| | | | | | | | |
| 100% | \$ 1,528,170 | 100% | \$ 1,528,170 | | \$ 269,332 | | |
| | | | | | | | |
| 100% | \$ 125,081 | 100% | \$ 125,081 | | \$ 37,697 | | |
| 100% | \$ 1,913,486 | 100% | \$ 1,913,486 | | \$ 1,412,280 | | |
| | , , | | <u> </u> | \$ 100,000 | , , , | \$ | 104,186 |
| | | | | \$ 600,000 | | \$ | 546,062 |
| | | | | \$ 60,000 | | \$ | 51,891 |
| | | | | | | | |
| 1% | \$ 7,499,815 | 1% | | | | \$ | 3,914,679 |
| | | | | \$ 15,479 | | | |
| | | | | \$ 3,854 | | | |
| | | | | \$ 1,139 | | | |
| | | | | \$ 8,105 | | | |
| | | | | \$ 3,240 | | | |
| | | | | \$ 5,450 | | | |



| СС | State | Subcontractor | Scope of Work | SBE/Other | Orig Contract \$ Amount | Original SBE \$ Commitment |
|----|-------|---------------------------------------|---------------------------------|-----------|----------------------------|-------------------------------|
| | MN | Bosch Security Systems | Control Room Equipment Supplier | Other | | |
| | IL | Studio Technologies | Control Room Equipment Supplier | Other | | |
| | CA | Wohler Technology | Control Room Equipment Supplier | Other | | |
| | NM | Lectronsonics | Control Room Equipment Supplier | Other | | |
| | NY | American Music & Sound | Control Room Equipment Supplier | Other | | |
| | UT | Harmon Music Group | Control Room Equipment Supplier | Other | | |
| | CA | Yamaha Corp of America | Control Room Equipment Supplier | Other | | |
| | NY | EEG Enterprises | Control Room Equipment Supplier | Other | | |
| | CA | Barco Volsom, LLC | Control Room Equipment Supplier | Other | | |
| | PA | Simplylive, Inc. | Control Room Equipment Supplier | Other | | |
| | CA | AJA Video Systems | Control Room Equipment Supplier | Other | | |
| | NJ | IHSE USA, LLC | Control Room Equipment Supplier | Other | | |
| | NY | Multidune Video & Fiber Optics System | Control Room Equipment Supplier | Other | | |
| | CA | IDX Technology | Control Room Equipment Supplier | Other | | |
| | NJ | Panasonic Corp of NA | Control Room Equipment Supplier | Other | | |
| | OR | Tektronix, Inc. | Control Room Equipment Supplier | Other | | |
| | NJ | Sony Electronics, Inc. | Control Room Equipment Supplier | Other | | |
| | NY | Ross Video Inc. | Control Room Equipment Supplier | Other | | |
| | NJ | Evs Broadcast Equipment, Inc. | Control Room Equipment Supplier | Other | | |
| | CA | Riedel Communications | Control Room Equipment Supplier | Other | | |
| | ON | Evertz Microsystems, Inc. | Control Room Equipment Supplier | Other | | |
| | NV | Titan Systems, Inc. | Low Voltage Installers | Other | | |
| | NV | MD Electric | Installation of Racks and Base | SBE/WBE | | |
| | NV | MD Electric | High Voltage Installers | SBE/WBE | | |

| Original SBE Commitment % | Current Contract \$ Amount | SBE % | Awarded SBE \$Participation | Other \$Participation | Actual SBE \$ Paid | Actual Other \$ Paid |
|------------------------------|-------------------------------|-------|--------------------------------|-----------------------|-----------------------|-------------------------|
| | | | | \$ 11,042 | | |
| | | | | \$ 5,112 | | |
| | | | | \$ 19,271 | | |
| | | | | \$ 4,376 | | |
| | | | | \$ 10,710 | | |
| | | | | \$ 3,563 | | |
| | | | | \$ 1,680 | | |
| | | | | \$ 7,727 | | |
| | | | | \$ 4,748 | | |
| | | | | \$ 6,022 | | |
| | | | | \$ 152,505 | | |
| | | | | \$ 347,769 | | |
| | | | | \$ 17,823 | | |
| | | | | \$ 226 | | |
| | | | | \$ 36,717 | | |
| | | | | \$ 119,067 | | |
| | | | | \$ 159,917 | | |
| | | | | \$ 533,814 | | |
| | | | | \$ 436,782 | | |
| | | | | \$ 300,280 | | |
| | | | | \$ 808,747 | | |
| | | | | \$ 270,000 | | |
| | | | \$ 15,222 | | | |
| | | | \$ 55,442 | | | |



| СС | State | Subcontractor | Scope of Work | SBE/Other | Orig Contract \$ Amount | Original SBE \$ Commitment |
|-------|-------|-------------------------------------|--|-----------|----------------------------|-------------------------------|
| | TX | Bedrock Logistics | Freight | Other | | |
| | NV | Ice Now | Water | SBE | | |
| | NV | Vision Control Associates of Nevada | Misc. Camera Products | SBE/WBE | | |
| 4.09 | NV | Aggregate Industries | Bituminous Pavement | Other | \$ 4,408,062 | \$ 661,20 |
| 4.03 | NV | MC4 Construction | Traffic Signals & Streetlights | SBE | Ψ,400,002 | Ψ 001,20 |
| | NV | JS&S Survey | Land Surveying | SBE/MBE | | |
| | NV | Affordable Striping and Sealing | Striping and Signs | SBE | | |
| | NV | Stewart & Sundell Concrete | Concrete Island & Barrier Rail | SBE | | |
| | NV | A-1 Concrete Cutting & Demolition | Core Drilling/Saw Cutting | SBE/MBE | | |
| | NV | Flippins Trenching Inc. | Sawcutting | SBE | | |
| | NV | HD Barricade, Inc. | Traffic Barricade Rental | Other | | |
| | NV | JS&S, Inc. | Survey | SBE/MBE | | |
| | NV | A Affordable Striping & Sealing | Asphalt Striping & Signs | SBE | | |
| | | | | | | |
| 4.10a | NV | Sahara Concrete | Decorative Site Concrete | SBE | \$ 14,216,220 | \$ 14,216,22 |
| | NV | T.B. Penick & Sons | Decorative Concrete | Other | | |
| | CA | Triton Structural Concrete, Inc. | Site Concrete - Labor | Other | | |
| | NV | Merli Concrete Pumping of Nevada | Concrete Pump | SBE | | |
| | NV | Penhall Company | Concrete Core Drilling | Other | | |
| | NV | TAB Contractors Inc. | Excavation/Grading | Other | | |
| | NV | Merli Concrete Inc. | Concrete Pump | SBE | | |
| | CA | CMC Rebar | Rebar Install | Other | | |
| 4.10a | NV | Stewart & Sundell Concrete | Curbs, Gutters & Sidewalk | SBE | \$ 2,295,788 | \$ 2,295,78 |
| 4.10a | NV | Nevada Ready Mix | Concrete Supplier | Other | φ 2,295,766 | \$ 2,295,76 |
| | INV | Nevaua Neauy Wiix | Concrete Supplier | Other | | |
| 4.10b | NV | Aggregate Industries | MSE Retaining Walls | Other | \$ 5,132,049 | \$ 793,79 |
| | CA | The Reinforced Earth Company | Design/Provide MSE Wall Material | Other | | |
| | NV | Stewart & Sundell | CIP Concrete for MSE Walls | SBE | | |
| | NV | Harris Rebar Las Vegas, Inc. | Reinforcing Steel | Other | | |
| | NV | Sunbelts of Nevada, LLC | Type II Placement over CMU walls with belted equipment | SBE | | |
| | NV | JS&S, Inc. | Survey as pertains to MSE Walls | SBE/MBE | | |
| | | | | | | |
| 4.11 | NV | Brightview Landscape Development | Landscape & Irrigation | Other | \$ 2,799,991 | \$ 447,67 |
| | | | | | | |

| Commitment % | Current Contract \$ Amount | SBE % | Awarded SBE \$Participation | Other \$Participation | Actual SBE \$ Paid | Actual Other \$ Paid |
|--------------|---|-------|---|-----------------------|-----------------------|-------------------------|
| | | | | \$ 13,095 | | |
| | | | \$ 461 | | | |
| | | | \$ 4,000 | | | |
| | | | | | | |
| 15% | \$ 6,217,282 | 27% | | | | \$ 1,552,631 |
| | | | \$ 1,275,330 | | \$ 352,532 | |
| | | | \$ 2,224 | | | |
| | | | \$ 165,630 | | | |
| | | | \$ 29,948 | | | |
| | | | \$ 5,000 | | \$ 2,268 | |
| | | | \$ 5,000 | | | |
| | | | | \$ 96,900 | | \$ 96,900 |
| | | | \$ 8,500 | | \$ 422 | |
| | | | \$ 165,630 | | | |
| 100% | \$ 12,663,783 | 100% | \$ 12,538,783 | | \$ 3,278,295 | |
| | , ,,,,,,,,,,,,,,,,,,,,,,,,,,,,,,,,,,,,, | | , ,,,,,,,,,,,,,,,,,,,,,,,,,,,,,,,,,,,,, | \$ 3,942,800 | , , , , , | \$ 236,664 |
| | | | | \$ 1,522,428 | | \$ 160,000 |
| | | | \$ 25,000 | | \$ 5,662 | |
| | | | | \$ 7,000 | | |
| | | | | \$ 1,865,286 | | \$ 185,890 |
| | | | \$ 100,000 | | \$ 9,733 | |
| | | | | \$ 720,492 | | \$ 195,349 |
| | | | | | | |
| 100% | \$ 1,996,103 | 100% | \$ 1,996,103 | | \$ 493,609 | |
| | | | | \$ 390,000 | | |
| 15% | \$ 5,654,924 | 18% | | | | \$ 5,372,178 |
| | | | | \$ 864,421 | | \$ 853,971 |
| | | | \$ 942,022 | | \$ 941,202 | |
| | | | | \$ 72,394 | | \$ 68,774 |
| | | | \$ 58,750 | | \$ 45,372 | |
| | | | \$ 40,192 | | \$ 41,918 | |
| | | | ,, | | | |
| 16% | \$ 2,806,971 | 15% | | | | \$ 352,403 |



| CC | State | Subcontractor | Scope of Work | SBE/Other | Orig Contract \$ Amount | | Original SBE \$ Commitment |
|-----------|-------|---|---|-----------|----------------------------|-------|-------------------------------|
| | NV | Amazon Masonry | Trucking & Hauling of Material along with Trenching | SBE | | | |
| | NV | Synthetic Turf Products dba Green Living Services | Site Amenities | SBE | | | |
| | NV | Sunbelts of Nevada | Placement of Conveyored Equipment | SBE | | | |
| | | | | | | | |
| 4.12 | СО | Rolling Plains Construction | Fireproofing | Other | \$ 4,378,32 | 22 \$ | 667,494 |
| | NV | Quinette King Consulting | Material Supplier | SBE/MBE | | | |
| | NV | United Rentals | Equipment Rentals | Other | | | |
| 5.01/5.19 | NV | Southwest Specialty Contractors | Acoustical Ceilings & Bowl Acoustical Treatment | Other | \$ 11,842,08 | 39 \$ | 1,780,000 |
| | NV | AMS | Misc. Grid | Other | | | |
| | NV | T3 Distributors LLC | Ceiling/Fabric Supplier | SBE | | | |
| | NV | Affordable Federal Services | Acoustical Sound absorbing Ceiling Units | SBE | | | |
| | NV | Construction Sealants Supply | Concrete Sealer | SBE | | | |
| | NV | Mori Consulting LLC | Acoustical Sound Absorbing Ceiling Units & Sound absorbing Wall Units | SBE/MBE | | | |
| | NV | N & P Services Company, LLC | Acoustical Ceiling Material Supplier | SBE | | | |
| 5.02 | NV | Architectural Southwest Stone Co. | Ceramic Tile | SBE | \$ 3,273,83 | 80 \$ | 3,273,830 |
| | NV | Technicoat Management Inc. | Installation of Mapei Mapelastic AquaDefense in Designated Areas | SBE | | | |
| | | | | | | | |
| 5.02 | NV | T. Nickolas Company | Ceramic Tile & Quartz | Other | \$ 5,911,12 | 21 \$ | 886,668 |
| | NV | Marble Tec | Install Quartz Tops | SBE | | | |
| | NV | Technicoat | Waterproofing | SBE | | | |
| 5.03 | NV | Master Craft Carpet Services | Carpet/Flooring | Other | \$ 1,712,86 | 60 \$ | 256,929 |
| | NV | Desired Space | Material Procurement | SBE | | | |
| | | | | | | | |
| 5.04 | | Technicoat Management, Inc. | Resinous Flooring | SBE | \$ 850,17 | '0 \$ | 850,170 |

| Original SBE Commitment % | Current Contract \$ Amount | SBE % | Awarded SBE \$Participation | Other \$Participation | Actual SBE \$ Paid | Actual Other \$ Paid |
|------------------------------|-------------------------------|-------|--------------------------------|-----------------------|-----------------------|-------------------------|
| | | | \$ 329,496 | | | |
| | | | \$ 50,400 | | | |
| | | | \$ 42,920 | | \$ 33,190 | |
| | | | | | | |
| 15% | \$ 5,890,754 | 19% | | | | \$ 5,003,546 |
| | | | \$ 1,105,910 | | \$ 1,105,910 | |
| | | | | \$ 250,000 | | \$ 41,425 |
| | | | | | | |
| 15% | \$ 13,724,598 | 15% | \$ 121,463 | | | \$ 4,330,353 |
| | | | | \$ 15,000 | | \$ 12,858 |
| | | | \$ 293,650 | | \$ 145,713 | |
| | | | \$ 758,143 | | \$ 403,805 | |
| | | | \$ 90,000 | | \$ 18,397 | |
| | | | \$ 168,808 | | | |
| | | | \$ 626,626 | | \$ 283,992 | |
| 100% | \$ 3,301,940 | 100% | \$ 3,286,340 | | ф 2.25C.0.42 | |
| 100% | \$ 3,301,940 | 100% | \$ 3,286,340 | | \$ 2,256,843 | |
| | | | \$ 15,600 | | \$ 7,932 | |
| 15% | \$ 7,941,285 | 15% | \$ 150,043 | | | \$ 934,228 |
| 1370 | Ψ 7,341,200 | 1370 | \$ 950,000 | | \$ 204,696 | ψ 334,220 |
| | | | \$ 91,150 | | \$ 65,360 | |
| | | | 01,100 | | 00,000 | |
| 15% | \$ 1,891,787 | 20% | | | | \$ 79,538 |
| | | | \$ 380,156 | | \$ 380,156 | |
| | | | | | | |
| 100% | \$ 907,497 | 100% | \$ 907,497 | | \$ 302,993 | |



| СС | State | Subcontractor | Scope of Work | SBE/Other | rig Contract \$ Amount | ginal SBE ommitment |
|---------------------|-------|--------------------------------------|---|-----------|---------------------------|------------------------|
| | СТ | Dur-A-Flex, Inc. | Resinous Flooring Material Supplier | Other | | |
| 5.05 | NV | Midwest Pro Painting | Paint & Wallcovering | Other | \$ 4,015,702 | \$ 973,035 |
| | NV | Quinette King Consulting | Supplier | SBE/MBE | | |
| | | | Toilet Compartments & Toilet | | | |
| 5.08/5.09 | NV | ISEC | Accessories | Other | \$ 2,286,410 | \$ 342,962 |
| | NV | Sunstone Building Specialties | Metal Toilet Compartments, Adult Changing Stations & AED's | SBE | | |
| | MN | Activar, Inc. | Fire Extinguisher, AED & AED Cabinet Samples | Other | | |
| | NY | American Specialties, Inc. | TRA Samples | Other | | |
| | CO | Buck Engineering | Engineering Shop Drawings | Other | | |
| | WI | InPro | Cubical Curtain Samples | Other | | |
| | NV | Nevada Precision | DM1 Aluminum Base & Steel Plate Shelves | SBE/MBE | | |
| | NV | Woodstock Architectural Products | Column Covers & Escalator Panels | SBE | | |
| | FL | Access-Able Designs | Folding Dressing Benches | Other | | |
| | TX | Allied Hand Dryer | VERDEdri Hand Dryers | Other | | |
| | LA | Gordon Architectural & Eng Solutions | Column Covers | Other | | |
| | FL | American Sanitary Partition | Toilet Partitions | Other | | |
| | NY | Sportsfield Specialties, Inc. | Sports Equipment & Goal Post Padding | Other | | |
| | CA | Bobrick Washroom Equipment | Shower Curtain | Other | | |
| | | | | | | |
| 5.11 | NV | YESCO | Signage & Graphics | Other | \$ 4,793,199 | \$ 718,980 |
| | NV | Flippin's Trenching, Inc. | Locate Utilities | SBE | | |
| | NV | Eberhard Southwest Roofing, Inc. | Rooftop Logo Signage | SBE | | |
| | NV | Union Erectors | Steel & Catwalks Interior Bowl NRP Signs | SBE | | |
| 5.12/5.20/5 .22a | NV | Spilker Pacific, LLC | Overhead Doors, Loading Dock Equipment & Coiling Smoke Doors | Other | \$ 641,879 | \$ 285,805 |
| .228 | NV | The Smith Overhead Door | Ovehead Doors & Loading Dock Equipment | SBE | | |

| Original SBE Commitment % | Current Contract \$ Amount | SBE % | warded SBE Participation | Other \$Participation | Actual SBE \$ Paid | A | Actual Other \$ Paid |
|------------------------------|-------------------------------|-------|-----------------------------|-----------------------|-----------------------|----|-------------------------|
| | | | | \$ 332,638 | | \$ | 174,457 |
| | | | | | | | |
| 24% | \$ 4,234,884 | 23% | | | | \$ | 1,969,289 |
| | | | \$ 973,035 | | \$ 363,180 | | |
| | | | | | | | |
| 15% | \$ 5,631,836 | 18% | | | | \$ | 3,047,251 |
| | | | \$ 399,392 | | \$ 61,215 | | |
| | | | | \$ 64,673 | | \$ | 64,673 |
| | | | | \$ 68,942 | | \$ | 64,736 |
| | | | | \$ 13,740 | | \$ | 13,740 |
| | | | | \$ 2,764 | | \$ | 2,760 |
| | | | \$ 36,215 | | \$ 20,953 | | |
| | | | \$ 600,820 | | \$ 492,853 | | |
| | | | | \$ 14,250 | | \$ | 14,250 |
| | | | | \$ 98,862 | | \$ | 98,862 |
| | | | | \$ 78,437 | | \$ | 2,144 |
| | | | | \$ 226,310 | | \$ | 124,508 |
| | | | | \$ 85,743 | | | |
| | | | | \$ 751 | | \$ | 751 |
| | | | | | | | |
| 15% | \$ 9,645,852 | 15% | \$ 247,259 | | | \$ | 3,079,524 |
| | | | \$ 7,595 | | | | |
| | | | \$ 187,164 | | | | |
| | | | \$ 1,004,860 | | | | |
| | | | | | | | |
| 45% | \$ 771,955 | 57% | | | | \$ | 692,949 |
| | | | \$ 437,740 | | \$ 437,740 | | |



| СС | State | Subcontractor | Scope of Work | SBE/Other | Orig Contract \$ Amount | Original SBE \$ Commitment |
|-------------------|-------|----------------------------------|---|-----------|----------------------------|-------------------------------|
| | | | | | | |
| 5.14/5.10b & c | CA | Golden Bay Fence Plus Iron Works | Fence, Gates, Bollards & Wedge Barrier | Other | \$ 2,297,856 | \$ 344,678 |
| | NV | R.E.B. Construction Co. | Foundation Drilling | Other | | |
| | NV | Harris Rebar | Bollard Cage reinforced steel tied & delivered to the jobsite | Other | | |
| | NV | Fencing Specialties Inc. | Marerials | SBE/MBE | | |
| 5.14b | WI | Jones Sign Company | Decorative Site Railings | Other | \$ 549,340 | \$ 82,401 |
| | CA | Walmsley Safety Consulting, LLC | Safety Professional | Other | | |
| | NV | Region 9 Safety | Safety Director | SBE/MBE | | |
| | NV | Gilberts Precision Machine Co. | Materials | SBE | | |
| | NV | TV Transport | Freight Transport | SBE | | |
| | NV | The Tiberti Fence | Fencing Materials | SBE | | |
| | NV | Southwest Specialty Coating | Onsite Touch-up Painting | SBE | | |
| | NV | Fasco | Materials | SBE | | |
| | NV | General Design | Materials | SBE/MBE | | |
| | ВС | Global Rope Access | Scoreboard Installation | Other | | |
| | NV | House of Signs | Installation | SBE | | |
| | NV | Ahern Rentals | Install Equipment | Other | | |
| 5.15 | AZ | Western Millwork | Millwork | Other | \$ 9,676,392 | \$ 1,451,459 |
| | NV | Plus Studios | Architectural Millwork | SBE | | |
| | | | | | | |
| 5.15 | NV | Austin Millwork & Cabinetry | Millwork NEZ (North End Zone Club) | Other | \$ 937,328 | \$ 191,154 |
| 5.17b | GA | Sports Field, Inc. dba Fields | Heat System for Operable Field | Other | \$ 1,716,348 | \$ 257,452 |
| | UT | Cache Valley Electric | Electrical Installation | Other | | |
| | СО | The RMH Group | Electrical Engineering | Other | | |
| | ОН | Rovisys Building Technologies | Control Panel Design & Fabrication | Other | | |

| Original SBE Commitment % | Current Contract \$ Amount | SBE % | Awarded SBE \$Participation | Other \$Participation | Actual SBE \$ Paid | Actual Other \$ Paid |
|------------------------------|-------------------------------|-------|--------------------------------|-----------------------|-----------------------|-------------------------|
| | | | | | | |
| 15% | \$ 5,327,079 | 15% | \$ 199,062 | | | \$ 1,613,079 |
| | | | | \$ 75,000 | | \$ 13,600 |
| | | | | \$ 374,390 | | \$ 49,311 |
| | | | \$ 600,000 | | \$ 159,966 | |
| | | | | | | |
| 15% | \$ 4,132,104 | 15% | \$ 284,748 | | | \$ 1,152,057 |
| | | | | \$ 10,163 | | \$ 10,163 |
| | | | \$ 17,077 | | \$ 12,917 | |
| | | | \$ 12,061 | | \$ 12,061 | |
| | | | \$ 96,100 | | \$ 1,600 | |
| | | | \$ 45,044 | | \$ 45,044 | |
| | | | \$ 48,000 | | \$ 48,000 | |
| | | | \$ 1,842 | | \$ 1,842 | |
| | | | \$ 19,904 | | \$ 19,904 | |
| | | | | \$ 182,210 | | |
| | | | \$ 95,040 | | \$ 13,494 | |
| | | | | \$ 80,398 | | \$ 55,550 |
| | | | | | | |
| 15% | \$ 9,657,862 | 100% | \$ 9,050,562 | | | \$ 1,978,256 |
| | | | \$ 607,300 | | | |
| | | | | | | |
| 20% | \$ 1,237,145 | 15% | \$ 191,154 | | | \$ 26,714 |
| | | | | | | |
| 15% | \$ 3,336,722 | 15% | \$ 103,699 | | | \$ 1,093,368 |
| | | | | \$ 320,124 | | \$ 18,732 |
| | | | | \$ 68,960 | | \$ 64,849 |
| | | | | \$ 109,892 | | \$ 109,892 |



| сс | State | Subcontractor | Scope of Work | SBE/Other | | rig Contract \$ Amount | | Original SBE Commitment |
|-------|-------|--|--------------------------------------|-----------|----|---------------------------|----|----------------------------|
| | NV | Construction Sealants Supply | Furnish Drain Board & Filter Fabric | SBE | | | | |
| | NV | 3 QTD Technologies | Panel Construction | SBE | | | | |
| | AQ | Heating Solutions International | Furnish Heating Ribbons | Other | | | | |
| 5.00 | NIV/ | Marillan Ourstone Oak in street Maria Is | Ladar | ODE | Φ. | 4 000 750 | Φ. | 4 000 750 |
| 5.22 | NV | Mueller Custom Cabinetry of Nevada | Lockers | SBE | \$ | 1,606,750 | \$ | 1,606,750 |
| | TX | Hollman, Inc. | Locker Fabrication | Other | | | | |
| 5.22b | NV | Arcon Global, Inc. | Access Flooring | SBE | \$ | 36,060 | \$ | 36,060 |
| 5.22d | NV | Sunstone Building Specialties | Operable Partitions | SBE | \$ | 198,426 | \$ | 198,426 |
| | | | | | | | | |
| 5.22e | AZ | Luminous Egress | Photoluminescent | MBE | \$ | 297,842 | \$ | 44,676 |
| 5.22g | NV | Custom Hearth Distributors dba Custom Specialties Group | Trash Chutes | SBE | \$ | 128,408 | \$ | 128,408 |
| | NV | Energy Mechanical Insulation | Trash Chutes Insulation fire wrap | SBE/WBE | | | | |
| 5.24 | CA | Contract Décor, Inc. | Window Treatment (Curtains & Drapes) | Other | \$ | 32,236 | \$ | 4,835 |
| 6.00 | NV | Cleaning Services, Inc. | Final Clean | SBE/MBE | \$ | 1,524,491 | \$ | 1,524,491 |
| | | | Totals | | \$ | 969,700,127 | \$ | 188,695,639 |
| | | | Goal | | Ψ | 303,700,127 | ψ | 100,093,039 |

| Original SBE Commitment % | Current Contract \$ Amount | SBE % | warded SBE Participation | Other \$Participation | Actual SBE \$ Paid | A | Actual Other \$ Paid |
|------------------------------|-------------------------------|-------|-----------------------------|-----------------------|-----------------------|----|-------------------------|
| | | | \$ 188,524 | | \$ 271 | | |
| | | | \$ 208,285 | | \$ 208,285 | | |
| | | | | \$ 203,260 | | \$ | 203,260 |
| | | | | | | | |
| 100% | \$ 1,606,750 | 100% | \$ 1,606,750 | | \$ 457,985 | | |
| | | | | \$ 1,019,141 | | \$ | 364,710 |
| | | | | | | | |
| 100% | \$ 36,060 | 100% | \$ 36,060 | | | | |
| | | | | | | | |
| 100% | \$ 267,608 | 100% | \$ 267,608 | | \$ 49,396 | | |
| | | | | | | | |
| 15% | \$ 297,842 | 15% | \$ 44,676 | | | | |
| | | | | | | | |
| 100% | \$ 336,267 | 100% | \$ 176,864 | | \$ 282,560 | | |
| | | | \$ 159,403 | | \$ 145,764 | | |
| | | | | | | | |
| 15% | \$ 222,657 | 15% | \$ 33,399 | | | | |
| | | | | | | | |
| 100% | \$ 1,524,491 | 100% | \$ 1,524,491 | | | | |
| | | | | | | | |
| 19% | \$ 1,258,614,723 | 24% | \$ 301,130,183 | \$ 360,271,074 | \$ 198,414,946 | \$ | 1,232,270,026 |
| 15% | | | | | | | |



This report reflects the cumulative hours worked through February 2020

| This report reflects the cumulative hours worked through February 20 |
|--|
| Subcontractor |
| |
| |
| |
| La da Maranta anta a |
| Lewis K Construction |
| Modern Demo & Services |
| Total for Lewis K Construction |
| |
| Geotechnical & Environmental Services |
| Eagle Drilling Services |
| Total for Geotecnical & Environmental Svs |
| Total for Geolecincal & Environmental 3v3 |
| Nevede Weter Truck |
| Nevada Water Truck |
| Total for Nevada Water Truck |
| |
| Amazon Masonry |
| Total for Amazon Masonry |
| |
| TAB Contractors - Trailer City |
| Mcon |
| Acme Electric - Mcon TC |
| Olson Precast - Mcon TC |
| Nevada Tap Master - Mcon TC |
| Merli - Mcon TC |
| MMC, Inc. |
| |
| A-1 Concrete |
| Wells Cargo |
| Total for TAB Contractors - Trailer City |
| |
| Sahara Concrete |
| CMC Rebar |
| Dielco Crane Service |
| Merli Concrete |
| A-1 Concrete |
| Total for Sahara Concrete |
| Total for Saliara Concrete |
| Marrall Macanny |
| Marnell Masonry |
| Total for Marnell Masonry |
| |
| TAB Contractors - Main |
| Brightview Landscape |
| Nelson Hiniker Striping |
| Sanders Construction |
| A-1 Concrete |
| MMC |
| TAB-MMC |
| |
| Mcon |
| MMC - Mcon |
| Wells Cargo - Mcon |
| Merli - Mcon BC |
| Viking Drillers, Inc. |
| Acme Electric |
| Merli Concrete |
| Olson Precast |
| Las Vegas Paving |
| Nevada Tap Master |
| |
| Wells Cargo - TAB |
| The Tiberti Fence - TAB |
| Total for TAD Confrontors Main |
| Total for TAB Contractors - Main |
| |
| Southland - TC |
| |
| Southland - TC |

| | Cumulative hours through February 2020 | | | | | | | |
|---------|--|-----------------|-----------------------|------------|--|--|--|--|
| Total | Total | Total | Total | Total | | | | |
| Hours | Minority/Female | Veteran | Minority/Female % | Veteran % | | | | |
| Hours | illinority/i omalo | Veteran | Milliority/i emale /0 | Veteran 70 | | | | |
| 30 | 30 | 0 | 100% | 0% | | | | |
| 198 | 198 | 0 | 100% | 0% | | | | |
| 228 | 228 | 0 | 100% | 0% | | | | |
| | | | 10070 | 0,0 | | | | |
| 0 | 0 | 0 | 0% | 0% | | | | |
| 110 | 33 | 0 | 30% | 0% | | | | |
| 110 | 33 | 0 | 30% | 0% | | | | |
| | | | | | | | | |
| 30,727 | 24,301 | 0 | 79% | 0% | | | | |
| 30,727 | 24,301 | 0 | 79% | 0% | | | | |
| | | | | | | | | |
| 99 | 99 | 0 | 100% | 0% | | | | |
| 99 | 99 | 0 | 100% | 0% | | | | |
| | | | | | | | | |
| 2,439 | 605 | 0 | 25% | 0% | | | | |
| 2,333 | 2,076 | 0 | 89% | 0% | | | | |
| 27 | 12 | 0 | 44% | 0% | | | | |
| 91 | 91 | 0 | 100% | 0% | | | | |
| 2 | 2 | 0 | 100% | 0% | | | | |
| 4 | 0 | 0 | 0% | 0% | | | | |
| 7 | 7 | 0 | 100% | 0% | | | | |
| 4 | 4 | 0 | 100% | 0% | | | | |
| 88 | 44 | 0 | 50% | 0% | | | | |
| 4,993 | 2,838 | 0 | 57% | 0% | | | | |
| 20,805 | 19,858 | 0 | 95% | 0% | | | | |
| 4,450 | 3,363 | 0 | 76% | 0% | | | | |
| 379 | 0 | 0 | 0% | 0% | | | | |
| 297 | 0 | 0 | 0% | 0% | | | | |
| 1,346 | 719 | 0 | 53% | 0% | | | | |
| 27,277 | 23,940 | 0 | 88% | 0% | | | | |
| 21,211 | 25,540 | · | 0070 | 070 | | | | |
| 139 | 47 | 0 | 34% | 0% | | | | |
| 139 | 47 | 0 | 34% | 0% | | | | |
| | | | - | | | | | |
| 151,937 | 67,532 | 119 | 44% | 0% | | | | |
| 100 | 100 | 0 | 100% | 0% | | | | |
| 516 | 311 | 0 | 60% | 0% | | | | |
| 3,648 | 2,254 | 0 | 62% | 0% | | | | |
| 528 | 324 | 5 | 61% | 1% | | | | |
| 8,941 | 8,474 | 0 | 95% | 0% | | | | |
| 6 | 6 | 0 | 100% | 0% | | | | |
| 13,767 | 11,684 | 0 | 85% | 0% | | | | |
| 122 | 86 | 0 | 70% | 0% | | | | |
| 184 | 108 | 0 | 59% | 0% | | | | |
| 4 | 0 | 0 | 0% | 0% | | | | |
| 4 | 0 | 0 | 0% | 0% | | | | |
| 3,297 | 1,776 | 0 | 54% | 0% | | | | |
| 17 | 0 | 0 | 0% | 0% | | | | |
| 1,496 | 1,294 | 0 | 86% | 0% | | | | |
| 80 | 88 | 0 | 110% | 0% | | | | |
| 117 | 22 | 0 | 18% | 0% | | | | |
| 293 | 126 | 0 | 43% | 0% | | | | |
| 3 | 3 | 0 124 | 100% | 0% | | | | |
| 185,059 | 94,184 | 124 | 51% | 0% | | | | |
| 473 | 191 | 0 | 40% | 0% | | | | |
| 614 | 152 | 0 | 25% | 0% | | | | |
| 1,087 | 343 | 0 | 32% | 0% | | | | |
| 1,007 | U-7-U | | J£ /0 | U /0 | | | | |



| This report reflects the cumulative hours worked through February Subcontractor |
|--|
| |
| |
| Gephart-Morse, LLC Morse Electric - GM |
| A-1 Concrete - Morse |
| MMC - A-1 Morse |
| Lone Mountain - Morse |
| Joord |
| Live Electric - Morse Pyrocom |
| Valley Steel |
| Gephart Electric - GM |
| Jcord |
| Merli Concrete - Jcord REB Construction - Jcord |
| Dig 3 |
| Rosendin Electric |
| Total for Gephart-Morse, LLC |
| The Tiberti Fence |
| Flippins |
| Total for Tiberti Fence |
| |
| Malcolm Drilling |
| CMC Rebar Clark Welding & Fabricating |
| Dielco Crane |
| MMC |
| Total for Malcolm Drilling |
| MartanaaniMaCarthy |
| Mortenson McCarthy Merli Concrete Pumping |
| CMC Rebar |
| Gateway Concrete |
| Jcord |
| Silver Star Ready Mix Commercial Scaffolding |
| Union Erectors - MMc Concrete |
| Reliable Crane Service - MMc |
| Penhall Company |
| MJ Dean |
| Total for Mortenson McCarthy Joint Venture |
| EL - L LOW B C |
| Epernard SW Rooting |
| Eberhard SW Roofing Dielco Crane - Eberhard |
| |
| Dielco Crane - Eberhard Total for Eberhard Southwest Roofing |
| Dielco Crane - Eberhard Total for Eberhard Southwest Roofing Sunstate |
| Dielco Crane - Eberhard Total for Eberhard Southwest Roofing Sunstate Expansion Specialties - Sunstate |
| Dielco Crane - Eberhard Total for Eberhard Southwest Roofing Sunstate |
| Dielco Crane - Eberhard Total for Eberhard Southwest Roofing Sunstate Expansion Specialties - Sunstate Mountain West Excavation & Utilities GM Construction Reliable Steel - GM |
| Dielco Crane - Eberhard Total for Eberhard Southwest Roofing Sunstate Expansion Specialties - Sunstate Mountain West Excavation & Utilities GM Construction Reliable Steel - GM Standard Steel |
| Dielco Crane - Eberhard Total for Eberhard Southwest Roofing Sunstate Expansion Specialties - Sunstate Mountain West Excavation & Utilities GM Construction Reliable Steel - GM Standard Steel Dielco - GM |
| Dielco Crane - Eberhard Total for Eberhard Southwest Roofing Sunstate Expansion Specialties - Sunstate Mountain West Excavation & Utilities GM Construction Reliable Steel - GM Standard Steel |
| Dielco Crane - Eberhard Total for Eberhard Southwest Roofing Sunstate Expansion Specialties - Sunstate Mountain West Excavation & Utilities GM Construction Reliable Steel - GM Standard Steel Dielco - GM |
| Dielco Crane - Eberhard Total for Eberhard Southwest Roofing Sunstate Expansion Specialties - Sunstate Mountain West Excavation & Utilities GM Construction Reliable Steel - GM Standard Steel Dielco - GM Total for Sunstate Harris Energy Mechanical Insulation |
| Dielco Crane - Eberhard Total for Eberhard Southwest Roofing Sunstate Expansion Specialties - Sunstate Mountain West Excavation & Utilities GM Construction Reliable Steel - GM Standard Steel Dielco - GM Total for Sunstate Harris Energy Mechanical Insulation Mesa Mechanical Inc. |
| Dielco Crane - Eberhard Total for Eberhard Southwest Roofing Sunstate Expansion Specialties - Sunstate Mountain West Excavation & Utilities GM Construction Reliable Steel - GM Standard Steel Dielco - GM Total for Sunstate Harris Energy Mechanical Insulation Mesa Mechanical Inc. Advanced Controls & Electric |
| Dielco Crane - Eberhard Total for Eberhard Southwest Roofing Sunstate Expansion Specialties - Sunstate Mountain West Excavation & Utilities GM Construction Reliable Steel - GM Standard Steel Dielco - GM Total for Sunstate Harris Energy Mechanical Insulation Mesa Mechanical Inc. |
| Dielco Crane - Eberhard Total for Eberhard Southwest Roofing Sunstate Expansion Specialties - Sunstate Mountain West Excavation & Utilities GM Construction Reliable Steel - GM Standard Steel Dielco - GM Total for Sunstate Harris Energy Mechanical Insulation Mesa Mechanical Inc. Advanced Controls & Electric Rigging International Group JCord Bevstream |
| Dielco Crane - Eberhard Total for Eberhard Southwest Roofing Sunstate Expansion Specialties - Sunstate Mountain West Excavation & Utilities GM Construction Reliable Steel - GM Standard Steel Dielco - GM Total for Sunstate Harris Energy Mechanical Insulation Mesa Mechanical Inc. Advanced Controls & Electric Rigging International Group JCord Bevstream Mesa Mechanical Inc Bevstream |
| Dielco Crane - Eberhard Total for Eberhard Southwest Roofing Sunstate Expansion Specialties - Sunstate Mountain West Excavation & Utilities GM Construction Reliable Steel - GM Standard Steel Dielco - GM Total for Sunstate Harris Energy Mechanical Insulation Mesa Mechanical Inc. Advanced Controls & Electric Rigging International Group JCord Bevstream Mesa Mechanical Inc Bevstream Maui One |
| Dielco Crane - Eberhard Total for Eberhard Southwest Roofing Sunstate Expansion Specialties - Sunstate Mountain West Excavation & Utilities GM Construction Reliable Steel - GM Standard Steel Dielco - GM Total for Sunstate Harris Energy Mechanical Insulation Mesa Mechanical Inc. Advanced Controls & Electric Rigging International Group JCord Bevstream Mesa Mechanical Inc Bevstream Maui One Lone Mountain |
| Dielco Crane - Eberhard Total for Eberhard Southwest Roofing Sunstate Expansion Specialties - Sunstate Mountain West Excavation & Utilities GM Construction Reliable Steel - GM Standard Steel Dielco - GM Total for Sunstate Harris Energy Mechanical Insulation Mesa Mechanical Inc. Advanced Controls & Electric Rigging International Group JCord Bevstream Mesa Mechanical Inc Bevstream Maui One |
| Dielco Crane - Eberhard Total for Eberhard Southwest Roofing Sunstate Expansion Specialties - Sunstate Mountain West Excavation & Utilities GM Construction Reliable Steel - GM Standard Steel Dielco - GM Total for Sunstate Harris Energy Mechanical Insulation Mesa Mechanical Inc. Advanced Controls & Electric Rigging International Group JCord Bevstream Mesa Mechanical Inc Bevstream Maui One Lone Mountain |
| Dielco Crane - Eberhard Total for Eberhard Southwest Roofing Sunstate Expansion Specialties - Sunstate Mountain West Excavation & Utilities GM Construction Reliable Steel - GM Standard Steel Dielco - GM Total for Sunstate Harris Energy Mechanical Insulation Mesa Mechanical Inc. Advanced Controls & Electric Rigging International Group JCord Bevstream Mesa Mechanical Inc Bevstream Maui One Lone Mountain Total for Harris Merrill Steel Corona Stud & Deck |
| Dielco Crane - Eberhard Total for Eberhard Southwest Roofing Sunstate Expansion Specialties - Sunstate Mountain West Excavation & Utilities GM Construction Reliable Steel - GM Standard Steel Dielco - GM Total for Sunstate Harris Energy Mechanical Insulation Mesa Mechanical Inc. Advanced Controls & Electric Rigging International Group JCord Bevstream Mesa Mechanical Inc Bevstream Maui One Lone Mountain Total for Harris Merrill Steel Corona Stud & Deck Niles Industrial Coatings |
| Dielco Crane - Eberhard Total for Eberhard Southwest Roofing Sunstate Expansion Specialties - Sunstate Mountain West Excavation & Utilities GM Construction Reliable Steel - GM Standard Steel Dielco - GM Total for Sunstate Harris Energy Mechanical Insulation Mesa Mechanical Inc. Advanced Controls & Electric Rigging International Group JCord Bevstream Mesa Mechanical Inc Bevstream Maui One Lone Mountain Total for Harris Merrill Steel Corona Stud & Deck Niles Industrial Coatings Union Erectors |
| Dielco Crane - Eberhard Total for Eberhard Southwest Roofing Sunstate Expansion Specialties - Sunstate Mountain West Excavation & Utilities GM Construction Reliable Steel - GM Standard Steel Dielco - GM Total for Sunstate Harris Energy Mechanical Insulation Mesa Mechanical Inc. Advanced Controls & Electric Rigging International Group JCord Bevstream Mesa Mechanical Inc Bevstream Maui One Lone Mountain Total for Harris Merrill Steel Corona Stud & Deck Niles Industrial Coatings Union Erectors Global Rope Access |
| Dielco Crane - Eberhard Total for Eberhard Southwest Roofing Sunstate Expansion Specialties - Sunstate Mountain West Excavation & Utilities GM Construction Reliable Steel - GM Standard Steel Dielco - GM Total for Sunstate Harris Energy Mechanical Insulation Mesa Mechanical Inc. Advanced Controls & Electric Rigging International Group JCord Bevstream Mesa Mechanical Inc Bevstream Maui One Lone Mountain Total for Harris Merrill Steel Corona Stud & Deck Niles Industrial Coatings Union Erectors Global Rope Access Rigging International Group |
| Dielco Crane - Eberhard Total for Eberhard Southwest Roofing Sunstate Expansion Specialties - Sunstate Mountain West Excavation & Utilities GM Construction Reliable Steel - GM Standard Steel Dielco - GM Total for Sunstate Harris Energy Mechanical Insulation Mesa Mechanical Inc. Advanced Controls & Electric Rigging International Group JCord Bevstream Mesa Mechanical Inc Bevstream Maui One Lone Mountain Total for Harris Merrill Steel Corona Stud & Deck Niles Industrial Coatings Union Erectors Global Rope Access |
| Dielco Crane - Eberhard Total for Eberhard Southwest Roofing Sunstate Expansion Specialties - Sunstate Mountain West Excavation & Utilities GM Construction Reliable Steel - GM Standard Steel Dielco - GM Total for Sunstate Harris Energy Mechanical Insulation Mesa Mechanical Inc. Advanced Controls & Electric Rigging International Group JCord Bevstream Mesa Mechanical Inc Bevstream Maui One Lone Mountain Total for Harris Merrill Steel Corona Stud & Deck Niles Industrial Coatings Union Erectors Global Rope Access Rigging International Group Expansion Specialties Southwest Specialty Coatings Rigging Int- SW Specialty |
| Dielco Crane - Eberhard Total for Eberhard Southwest Roofing Sunstate Expansion Specialties - Sunstate Mountain West Excavation & Utilities GM Construction Reliable Steel - GM Standard Steel Dielco - GM Total for Sunstate Harris Energy Mechanical Insulation Mesa Mechanical Inc. Advanced Controls & Electric Rigging International Group JCord Bevstream Mesa Mechanical Inc Bevstream Maui One Lone Mountain Total for Harris Merrill Steel Corona Stud & Deck Niles Industrial Coatings Union Erectors Global Rope Access Rigging International Group Expansion Specialties Southwest Specialty Derr & Isbell |
| Dielco Crane - Eberhard Total for Eberhard Southwest Roofing Sunstate Expansion Specialties - Sunstate Mountain West Excavation & Utilities GM Construction Reliable Steel - GM Standard Steel Dielco - GM Total for Sunstate Harris Energy Mechanical Insulation Mesa Mechanical Inc. Advanced Controls & Electric Rigging International Group JCord Bevstream Mesa Mechanical Inc Bevstream Maui One Lone Mountain Total for Harris Merrill Steel Corona Stud & Deck Niles Industrial Coatings Union Erectors Global Rope Access Rigging International Group Expansion Specialties Southwest Specialty Coatings Rigging Int- SW Specialty |

| | Cumulative ho | | h February 2020 | |
|------------------|-----------------|------------|-------------------|-----------|
| Total | Total | Total | Total | Total |
| Hours | Minority/Female | Veteran | Minority/Female % | Veteran % |
| | | | | |
| 0 | 0 | 0 | 0% | 0% |
| 323,046 | 186,215 | 27,443 | 58% | 8% |
| 664 | 293 | 24 | 44% | 4% |
| 52 | 52 | 0 | 100% | 0% |
| 11,881 1,307 | 5,274 | 0 | 44% 72% | 0% 0% |
| 13,262 | 948 9,406 | 141 | 72% | 1% |
| | | 0 | 0% | 0% |
| 20 28 | 0 | 0 | 0% | 0% |
| ∠o 11,477 | 8,132 | 0 | 71% | 0% |
| 1,295 | 968 | 0 | 75% | 0% |
| 8 | 0 | 0 | 0% | 0% |
| 40 | 16 | 0 | 40% | 0% |
| 998 | 4 | 176 | 0% | 18% |
| 12,309 | 4,178 | 2,261 | 34% | 18% |
| 376,384 | 215,483 | 30,045 | 57% | 8% |
| 0.0,00. | 2.0,.00 | 00,010 | 0.70 | 370 |
| 1,991 | 1,663 | 142 | 84% | 7% |
| 77 | 25 | 0 | 32% | 0% |
| 2,068 | 1,688 | 142 | 82% | 7% |
| | | | | |
| 18,088 | 6,333 | 0 | 35% | 0% |
| 2,913 | 2,030 | 0 | 70% | 0% |
| 167 | 76 | 0 | 46% | 0% |
| 108 | 0 | 0 | 0% | 0% |
| 5 | 5 | 0 | 100% | 0% |
| 21,280 | 8,443 | 0 | 40% | 0% |
| | | | | |
| 616,044 | 507,057 | 14,044 | 82% | 2% |
| 2,487 | 539 | 0 | 22% | 0% |
| 297,094 | 257,574 | 0 | 87% | 0% |
| 157,670 | 115,629 | 6,926 | 73% | 4% |
| 14,670 | 11,549 | 0 | 79% | 0% |
| 23,116 | 9,204 | 0 | 40% | 0% |
| 4,298 | 4,298 | 0 | 100% | 0% |
| 2,310 | 584 | 0 | 25% | 0% |
| 28,401 | 1,321 | 0 | 5% | 0% |
| 631 | 562 | 0 | 89% | 0% |
| 9,516 | 7,724 | 0 | 81% | 0% |
| ,156,236 | 916,038 | 20,970 | 79% | 2% |
| 22.212 | 00.045 | | 000/ | 201 |
| 26,942 | 26,615 | 0 | 99% | 0% |
| 259 | 0 | 0 | 0% | 0% |
| 27,200 | 26,615 | 0 | 98% | 0% |
| 0 | 0 | 0 | 0% | 0% |
| | | 0 | 92% | 0% |
| 2,091 | 1,928 | 0 | | 0% |
| 127 | 127 | - | 100% | |
| 57,734 3,431 | 53,514 1,263 | 0 | 93% | 0% |
| 14,825 | 8,974 | 0 | 61% | 0% |
| 3,306 | 159 | 0 | 5% | 0% |
| 81,513 | 65,964 | 0 | 81% | 0% |
| 01,010 | 00,904 | U | 0170 | U 70 |
| 414,782 | 216,196 | 4,236 | 52% | 1% |
| 32,063 | 16,640 | 2,148 | 52% | 7% |
| 5,780 | 812 | 2,140 | 14% | 0% |
| 7,328 | 0 | 10 | 0% | 0% |
| 340 | 16 | 0 | 5% | 0% |
| 2,641 | 1,785 | 0 | 68% | 0% |
| 0 | 0 | 0 | 0% | 0% |
| 2,277 | 844 | 32 | 37% | 1% |
| 6,580 | 4,066 | 0 | 62% | 0% |
| 7,587 | 3,705 | 0 | 49% | 0% |
| 479,377 | 244,062 | 6,452 | 51% | 1% |
| - | , | | | |
| 0 | 0 | 0 | 0% | 0% |
| 58,637 | 18,667 | 854 | 32% | 1% |
| 45,144 | 16,462 | 1,200 | 36% | 3% |
| 20,600 | 7,637 | 1,812 | 37% | 9% |
| 14,641 | 4,285 | 0 | 29% | 0% |
| 8,272 | 1,267 | 0 | 16% | 0% |
| 103 | 80 | 0 | 78% | 0% |
| 32,182 | 21,858 | 80 | 68% | 0% |
| 11,740 | 635 | 0 | 5% | 0% |
| 507,367 | 266,826 | 1,912 | 53% | 0% |
| 100,100 | | | | |
| 28 711 | 11 680 | 1 1 4 1 1 | Δ1% | 5% |
| 28,711 12,939 | 11,689 8,785 | 1,411 0 | 41% 68% | 5% 0% |



| bcontractor | 1 1 | Commendation lead | | | |
|--|---|---|--|--|---|
| | | ī | | n February 2020 | |
| | Total | Total | Total | Total | Total |
| | Hours | Minority/Female | Veteran | Minority/Female % | Veteran % |
| | 1,808 | 932 | 0 | 52% | 0% |
| ice | 50,092 | 2,346 | 0 | 5% | 0% |
| | 792,235 | 361,467 | 7,268 | 46% | 1% |
| | | | | | |
| | 42,795 | 22,117 | 111 | 52% | 0% |
| es, Inc. | 540 | 286 | 0 | 53% | 0% |
| 1100, 1110. | 1,805 | 1,353 | 0 | 75% | 0% |
| | _ | · · · · · · · · · · · · · · · · · · · | 331 | | 9% |
| | 3,773 | 667 | | 18% | |
| on | 568 | 470 | 0 | 83% | 0% |
| | 49,480 | 24,893 | 442 | 52% | 0% |
| | | | | | |
| | 43,800 | 9,977 | 490 | 23% | 1% |
| | 19 | 0 | 0 | 0% | 0% |
| | 99 | 88 | 0 | 89% | 0% |
| r Co. | 198 | 0 | 0 | 0% | 0% |
| ılation | 112 | 62 | 0 | 55% | 0% |
| | 44,228 | 10,127 | 490 | 23% | 1% |
| | 44,220 | 10,121 | 730 | £U /0 | 1 /0 |
| | | 07.50 | 4.000 | 4.407 | 00/ |
| n | 63,280 | 27,567 | 4,990 | 44% | 8% |
| | 109 | 101 | 0 | 93% | 0% |
| sulation - Desert Fire | 974 | 670 | 56 | 69% | 6% |
| | 881 | 558 | 3 | 63% | 0% |
| ation | 473 | 210 | 0 | 44% | 0% |
| | 65,716 | 29,105 | 5,049 | 44% | 8% |
| | | | | | |
| w Voltage | 0 | 0 | 0 | 0% | 0% |
| Itage | 75,650 | 33,331 | 9,415 | 44% | 12% |
| oltage | 2,336 | 764 | 0 | 33% | 0% |
| orse - Low Voltage | 77,985 | 34,095 | 9,415 | 44% | 12% |
| ···• | | . , | , ·- | • • | |
| ting | 316,628 | 256,243 | 2,588 | 81% | 1% |
| - PCI | 15,300 | 15,300 | 0 | 100% | 0% |
| | 1,995 | 928 | 0 | 46% | 0% |
| ucts | 1,305 | 1,300 | 0 | 100% | 0% |
| | 11,994 | 10,917 | 0 | 91% | 0% |
| Contracting | _ | | | | |
| Contracting | 347,221 | 284,687 | 2,588 | 82% | 1% |
| | → | | | | |
| tries - MSE Retaining Wall | 36,922 | 16,533 | 990 | 45% | 0% |
| | 8,217 | 4,722 | 0 | 57% | 0% |
| 8&S | 348 | 169 | 0 | 49% | 0% |
| e Industries MSE Retaining Wall | 45,487 | 21,423 | 990 | 47% | 2% |
| <u> </u> | | | | | |
| LC | 24,093 | 17,993 | 0 | 75% | 0% |
| | 410 | 323 | 0 | 79% | 0% |
| Commoraid IIC | | 18,316 | | 79% 75% | |
| mmercial, LLC | 24,503 | | 0 | | |
| | | 10,510 | | 1370 | 0% |
| • | | | | | |
| ruction | 60,221 | 42,277 | 0 | 70% | 0% |
| uction | 60,221 60,221 | | | | |
| ction | _ | 42,277 | 0 | 70% | 0% |
| uction s Construction | _ | 42,277 | 0 | 70% | 0% |
| uction s Construction | 60,221 | 42,277 42,277 | 0 | 70% 70% 47% | 0% 0% |
| ction Construction | 60,221 26,201 40 | 42,277 42,277 12,270 | 0 0 256 0 | 70% 70% 47% 10% | 0% 0% 1% 0% |
| ruction ns Construction | 60,221 26,201 | 42,277 42,277 12,270 | 0 0 256 | 70% 70% 47% | 0% 0% 1% |
| etruction ains Construction are ctors - Core | 26,201 40 26,241 | 42,277 42,277 12,270 4 12,274 | 0 0 256 0 256 | 70% 70% 47% 10% 47% | 0% 0% 1% 0% 1% |
| rruction ins Construction re tors - Core | 26,201 40 26,241 8,761 | 42,277 42,277 12,270 4 12,274 3,547 | 0 0 256 0 256 | 70% 70% 47% 10% 47% | 0% 0% 1% 0% 1% |
| uction as Construction ors - Core | 26,201 40 26,241 | 42,277 42,277 12,270 4 12,274 | 0 0 256 0 256 | 70% 70% 47% 10% 47% | 0% 0% 1% 0% 1% |
| ruction ns Construction e tors - Core | 26,201 40 26,241 8,761 8,761 | 42,277 42,277 12,270 4 12,274 3,547 3,547 | 0 0 256 0 256 | 70% 70% 47% 10% 47% 40% | 0% 0% 1% 0% 1% 0% |
| rs - Core | 26,201 40 26,241 8,761 8,761 | 42,277 42,277 12,270 4 12,274 3,547 3,547 22,135 | 0 0 256 0 256 | 70% 70% 47% 10% 47% 40% 40% | 0% 0% 1% 0% 1% 0% |
| ction s Construction rs - Core - Hoist | 8,761 35,286 45,311 | 42,277 42,277 12,270 4 12,274 3,547 3,547 22,135 23,599 | 0 0 256 0 256 | 70% 70% 47% 10% 47% 40% 40% 63% 52% | 0% 0% 1% 0% 1% 0% 0% |
| ction Construction s - Core Hoist | 8,761 8,761 35,286 45,311 227 | 42,277 42,277 12,270 4 12,274 3,547 3,547 22,135 23,599 126 | 0 0 256 0 256 0 0 0 | 70% 70% 47% 10% 47% 40% 40% 63% 52% 56% | 0% 0% 1% 0% 1% 0% 2% 0% |
| rs - Core | 8,761 35,286 45,311 | 42,277 42,277 12,270 4 12,274 3,547 3,547 22,135 23,599 | 0 0 256 0 256 0 0 0 1,063 | 70% 70% 47% 10% 47% 40% 40% 52% 56% 44% | 0% 0% 1% 0% 1% 0% 0% 0% 0% 0% |
| rs - Core - Hoist | 8,761 8,761 35,286 45,311 227 | 42,277 42,277 12,270 4 12,274 3,547 3,547 22,135 23,599 126 | 0 0 256 0 256 0 0 0 | 70% 70% 47% 10% 47% 40% 40% 63% 52% 56% | 0% 0% 1% 0% 1% 0% 2% 0% |
| ction Construction s - Core Hoist | 8,761 8,761 35,286 45,311 227 340 | 42,277 42,277 12,270 4 12,274 3,547 3,547 22,135 23,599 126 149 | 0 0 256 0 256 0 0 0 1,063 | 70% 70% 47% 10% 47% 40% 40% 52% 56% 44% | 0% 0% 1% 0% 1% 0% 0% 0% 0% 0% |
| ction Construction s - Core Hoist | 8,761 8,761 35,286 45,311 227 340 5,332 | 42,277 42,277 12,270 4 12,274 12,274 3,547 3,547 22,135 23,599 126 149 385 | 0 0 256 0 256 0 0 1,063 0 | 70% 70% 47% 10% 47% 40% 40% 63% 52% 56% 44% 7% | 0% 0% 1% 0% 1% 0% 0% 0% 0% 0% |
| on onstruction - Core oist | 26,201 40 26,241 8,761 8,761 35,286 45,311 227 340 5,332 0 5,432 | 42,277 42,277 12,270 4 12,274 3,547 3,547 22,135 23,599 126 149 385 0 432 | 0 0 256 0 256 0 0 1,063 0 0 0 | 70% 70% 47% 10% 47% 40% 40% 63% 52% 56% 444% 7% 0% 8% | 0% 0% 1% 0% 1% 0% 0% 0% 0% 0% 0% 0% 0% |
| on onstruction Core | 26,201 40 26,241 8,761 8,761 35,286 45,311 227 340 5,332 0 | 42,277 42,277 12,270 4 12,274 3,547 3,547 22,135 23,599 126 149 385 0 | 0 0 0 256 0 256 0 0 1,063 0 0 | 70% 70% 47% 10% 47% 40% 40% 63% 52% 56% 44% 7% 0% | 0% 0% 1% 0% 1% 0% 0% 0% 0% 0% 0% 0% |
| ction Construction Section Construction Construction Construction Construction Construction Construction | 26,201 40 26,241 8,761 8,761 35,286 45,311 227 340 5,332 0 5,432 91,927 | 42,277 42,277 12,270 4 12,274 3,547 3,547 22,135 23,599 126 149 385 0 432 46,824 | 0 0 256 0 256 0 0 1,063 0 0 0 0 1,063 | 70% 70% 47% 10% 47% 40% 40% 63% 52% 56% 444% 7% 0% 8% 51% | 0% 0% 1% 0% 1% 0% 0% 0% 0% 0% 1% 1% |
| tion Construction s - Core Hoist tings | 26,201 40 26,241 8,761 8,761 35,286 45,311 227 340 5,332 0 5,432 91,927 | 42,277 42,277 12,270 4 12,274 3,547 3,547 22,135 23,599 126 149 385 0 432 46,824 | 0 0 256 0 256 0 0 1,063 0 0 0 1,063 | 70% 70% 47% 10% 47% 40% 40% 63% 52% 56% 44% 7% 0% 8% 51% | 0% 0% 1% 0% 1% 0% 0% 0% 0% 0% 0% 0% 0% 0% 0% 0% |
| ruction ins Construction re tors - Core III - Hoist Coatings | 26,201 40 26,241 8,761 8,761 35,286 45,311 227 340 5,332 0 5,432 91,927 | 42,277 42,277 12,270 4 12,274 3,547 3,547 22,135 23,599 126 149 385 0 432 46,824 | 0 0 256 0 256 0 0 1,063 0 0 0 0 1,063 | 70% 70% 47% 10% 47% 40% 40% 63% 52% 56% 444% 7% 0% 8% 51% | 0% 0% 1% 0% 1% 0% 0% 0% 0% 0% 1% 1% |
| truction ins Construction re etors - Core coatings net | 60,221 26,201 40 26,241 8,761 8,761 35,286 45,311 227 340 5,332 0 5,432 91,927 5,126 5,126 | 42,277 42,277 12,270 4 12,274 12,274 3,547 3,547 22,135 23,599 126 149 385 0 432 46,824 3,564 3,564 | 0 0 256 0 256 0 0 1,063 0 0 0 1,063 | 70% 70% 47% 10% 47% 40% 40% 63% 52% 56% 44% 7% 0% 8% 51% | 0% 0% 1% 0% 1% 0% 0% 0% 0% 0% 0% 0% 0% 0% 0% 0% 0% |
| ors - Core - Hoist batings | 26,201 40 26,241 8,761 8,761 35,286 45,311 227 340 5,332 0 5,432 91,927 5,126 5,126 4,585 | 42,277 42,277 12,270 4 12,274 12,274 3,547 3,547 22,135 23,599 126 149 385 0 432 46,824 3,564 3,564 3,419 | 0 0 0 256 0 256 0 0 1,063 0 0 0 0 1,063 | 70% 70% 47% 10% 47% 40% 40% 63% 52% 56% 44% 7% 0% 8% 51% 70% 70% | 0% 0% 1% 0% 1% 0% 0% 0% 0% 0% 0% 0% 0% 0% 0% 0% 0% 0% |
| construction - Core | 60,221 26,201 40 26,241 8,761 8,761 35,286 45,311 227 340 5,332 0 5,432 91,927 5,126 5,126 | 42,277 42,277 12,270 4 12,274 12,274 3,547 3,547 22,135 23,599 126 149 385 0 432 46,824 3,564 3,564 | 0 0 256 0 256 0 0 1,063 0 0 0 1,063 | 70% 70% 47% 10% 47% 40% 40% 63% 52% 56% 44% 7% 0% 8% 51% | 0% 0% 1% 0% 1% 0% 0% 0% 0% 0% 0% 0% 0% 0% 0% 0% 0% |
| Core pist | 26,201 40 26,241 8,761 8,761 35,286 45,311 227 340 5,332 0 5,432 91,927 5,126 5,126 4,585 | 42,277 42,277 12,270 4 12,274 12,274 3,547 3,547 22,135 23,599 126 149 385 0 432 46,824 3,564 3,564 3,419 | 0 0 0 256 0 256 0 0 1,063 0 0 0 0 1,063 | 70% 70% 47% 10% 47% 40% 40% 63% 52% 56% 44% 7% 0% 8% 51% 70% 70% | 0% 0% 1% 0% 1% 0% 0% 0% 0% 0% 0% 0% 0% 0% 0% 0% 0% 0% |
| struction ore | 26,201 40 26,241 8,761 8,761 35,286 45,311 227 340 5,332 0 5,432 91,927 5,126 5,126 4,585 | 42,277 42,277 12,270 4 12,274 12,274 3,547 3,547 22,135 23,599 126 149 385 0 432 46,824 3,564 3,564 3,419 | 0 0 0 256 0 256 0 0 1,063 0 0 0 0 1,063 | 70% 70% 47% 10% 47% 40% 40% 63% 52% 56% 44% 7% 0% 8% 51% 70% 70% | 0% 0% 1% 0% 1% 0% 0% 0% 0% 0% 0% 0% 0% 0% 0% 0% 0% 0% |
| es | 26,201 40 26,241 8,761 8,761 35,286 45,311 227 340 5,332 0 5,432 91,927 5,126 5,126 4,585 4,585 | 42,277 42,277 42,277 12,270 4 12,274 3,547 3,547 22,135 23,599 126 149 385 0 432 46,824 3,564 3,564 3,419 3,419 5,872 | 0 0 0 256 0 256 0 0 1,063 0 0 0 1,063 | 70% 70% 70% 47% 10% 47% 40% 40% 63% 52% 56% 44% 7% 0% 8% 51% 70% 70% | 0% 0% 1% 0% 1% 0% 0% 0% 0% 0% 0% 0% 0% 0% 0% 0% 0% |
| struction ore | 26,201 40 26,241 8,761 8,761 35,286 45,311 227 340 5,332 0 5,432 91,927 5,126 5,126 4,585 4,585 | 42,277 42,277 42,277 12,270 4 12,274 3,547 3,547 22,135 23,599 126 149 385 0 432 46,824 3,564 3,564 3,419 3,419 | 0 0 0 256 0 0 0 1,063 0 0 0 1,063 0 0 0 0 0 0 0 0 0 0 0 0 0 0 0 0 0 0 | 70% 70% 47% 10% 47% 40% 40% 63% 52% 56% 444% 7% 0% 8% 51% 70% 70% 75% 45% | 0% 0% 1% 0% 1% 0% 0% 0% 0% 0% 0% 0% 0% 0% 0% 0% 0% 0% |



This report reflects the cumulative hours worked through February 2020 Subcontractor Total for Midwest Pro Painting Sports Fields, Inc. Cache Valley Electric Co. Total for Sports Fields, Inc. Gephart/Morse - DAS Morse - DAS MD Electric Total for Gephart/Morse DAS Industrial Door Southwest Specialty Coatings Harris Danny's Construction - IDC Total for Industrial Door Sahara Concrete - Decorative Site TB Penick Triton Structural Concrete Penhall - TB Penick Merli - TB Penick CMC Rebar - Sahara TAB - Sahara Merli Concrete = Sahara Total for Sahara Concrete - Decorative Site Southwest Specialty Contractors Total for Southwest Specialty Contractors Architectural Southwest Stone Total for Architectural Southwest Stone Sunstone Building Specialties Total for Sunstone Building Specialties Southwest Specialty Coatings Total for Southwest Specialty Coatings Western Millwork Total for Western Millwork Raydeo Enterprise Steel Partners Standard Steel Expansion Specialties Total for Raydeo Enterprise Master Craft Floors Total for Master Craft Floors ISEC Total for ISEC **Custom Hearth Distributors** Total for Custom Hearth Distributors Corona Stud & Deck Total for Corona Stud & Deck Aggregate Industries A Affordable Striping & Sealing MC4 Construction, Inc Total for Aggregate Industries - Pavement Golden Bay Fence Plus Iron Works, Inc. REB Construction Harris Rebar - Golden Bay Total for Golden Bay Fence Plus Iron Works Stewart & Sundell

Total for Stewart & Sundell - Decorative Concrete

| | Total Hours 28,652 492 56 548 | Total Minority/Female 15,844 | Total Veteran | Total Minority/Female % 55% | Total Veteran % 0% |
|---|--|------------------------------|-------------------|------------------------------|--------------------------|
| | Hours 28,652 492 56 548 | Minority/Female 15,844 | Veteran | Minority/Female % | Veteran % |
| | 28,652 492 56 548 | 15,844 | | | |
| | 492 56 548 | | U | | |
| | 56 548 | 40 | | 0070 | 0 /6 |
| | 56 548 | | 0 | 8% | 0% |
| | 548 | 0 | 0 | 0% | 0% |
| | _ | 40 | 0 | 7% | 0% |
| | _ | | | | |
| | 0 | 0 | 0 | 0% | 0% |
| | 33,557 | 17,111 | 2,243 | 51% | 7% |
| | 19,089 | 8,031 | 2,600 | 42% | 14% |
| | 52,646 | 25,142 | 4,843 | 48% | 9% |
| | | | | 20/ | 00/ |
| | 0 642 | 0 261 | 0 | 0% 41% | 0% 0% |
| | 183 | 179 | 0 | 98% | 0% |
| | 5,133 | 1,761 | 579 | 34% | 11% |
| | 5,958 | 2,201 | 579 | 37% | 10% |
| | | | | | |
| | 7,690 | 7,624 | 0 | 99% | 0% |
| | 0 | 0 | 0 | 0% | 0% |
| | 3,606 | 2,507 | 0 | 70% | 0% |
| | 92 | 62 | 0 | 67% | 0% |
| | 63 | 0 | 0 | 0% | 0% |
| | 427 | 410 | 0 | 96% | 0% |
| | 338 | 193 | 0 | 57% | 0% |
| _ | 79 | 24 | 0 | 30% | 0% |
| _ | 12,295 | 10,819 | 0 | 88% | 0% |
| H | 8,631 | 7.607 | 0 | 88% | 0% |
| - | 8,631 | 7,607 7,607 | 0 | 88% | 0% |
| | 0,001 | 1,001 | _ | 0070 | 0,0 |
| | 12,749 | 12,842 | 0 | 101% | 0% |
| | 12,749 | 12,842 | 0 | 101% | 0% |
| | , | , | | | |
| | 297 | 22 | 0 | 7% | 0% |
| | 297 | 22 | 0 | 7% | 0% |
| | | | | | |
| | 12,398 | 8,533 | 0 | 69% | 0% |
| | 12,398 | 8,533 | 0 | 69% | 0% |
| | 4 400 | 4.400 | | 070/ | 00/ |
| - | 4,192 4,192 | 1,122 1,122 | 0 0 | 27% 27% | 0% 0% |
| | 4,132 | 1,122 | 0 | 21 /0 | 0 /6 |
| | 1,091 | 310 | 0 | 28% | 0% |
| | 11,410 | 3,305 | 2,066 | 29% | 18% |
| | 1,074 | 167 | 0 | 16% | 0% |
| | 214 | 176 | 0 | 82% | 0% |
| | 13,789 | 3,959 | 2,066 | 29% | 15% |
| | | | | | |
| | 526 | 522 | 0 | 99% | 0% |
| | 526 | 522 | 0 | 99% | 0% |
| | | | | | |
| | 5,694 | 2,394 | 0 | 42% | 0% |
| - | 5,694 | 2,394 | 0 | 42% | 0% |
| _ | 1 105 | 540 | 0 | 400/ | 00/ |
| | 1,105 1,036 | 542 | 126 | 49% | 0% 12% |
| H | 2,141 | 640 1,182 | 126 126 | 62% 55% | 6% |
| H | _, | 1,102 | .23 | 55 76 | J 70 |
| H | 13,172 | 4,201 | 2,983 | 32% | 23% |
| Г | 13,172 | 4,201 | 2,983 | 32% | 23% |
| | | | | | |
| | 4,655 | 1,812 | 0 | 39% | 0% |
| Ľ | 40 | 34 | 0 | 84% | 0% |
| | 3,768 | 3,112 | 0 | 83% | 0% |
| L | 8,463 | 4,957 | 0 | 59% | 0% |
| L | 0.015 | 1.00: | | 200/ | 201 |
| L | 2,249 | 1,801 | 0 | 80% | 0% |
| H | 92 | 14 | 0 | 15% | 0% |
| H | 361 2 701 | 150 1,965 | 0 0 | 42% 73% | 0% 0% |
| ┝ | 2,701 | 1,300 | U | 1370 | U-70 |
| | 5,442 | 5,290 | 0 | 97% | 0% |
| | ∪, ++ ∠ | 5,290 5,290 | 0 | 97% | 0% |



| This report reflects the cumulative hours worked through February 2 Subcontractor |
|--|
| |
| YESCO |
| Union Erectors |
| Flippins Trenching |
| Total for YESCO |
| |
| Jones Sign Co. |
| SW Specialty Coatings |
| Total for Jones Sign Co., Inc. |
| |
| Camatic |
| Seating Installation Group |
| Total for Camatic |
| Dimensional Innovations |
| P1 Group, Inc. |
| Valley Steel |
| Total for Dimensional Innovations |
| |
| Vector Foiltec |
| Danny's Construction |
| Unforgettable Coatings |
| Total for Vector Foiltec |
| |
| Austin Millwork & Cabintry |
| Total for Austin Millwork & Cabintry, Inc. |
| Drinktview I anderson Development |
| Brightview Landscape Development Total for Brightview Landscape Development |
| Total for Brightview Landscape Development |
| Davis Glass & Mirror |
| Sunstone Building Specialties |
| Total for Davis Glass & Mirror |
| |
| Spilker Pacific |
| Total for Spilker Pacific |
| |
| T. Nickolas |
| Total for T. Nickolas |
| |
| Technicoat Management |
| Total for Technicoat Management |
| Valley Steel |
| Total for Valley Steel |
| |
| Las Vegas Demolition |
| Total for Las Vegas Demolition |
| |
| Niles Industrial Coatings |
| Total for Niles Industrial Coatings |
| |
| |
| TOTAL LIQUIDO |
| TOTAL HOURS |

| | Cumulative hours through February 2020 | | | | | | |
|-----------|--|---------|-------------------|-----------|--|--|--|
| Total | Total | Total | Total | Total | | | |
| Hours | Minority/Female | Veteran | Minority/Female % | Veteran % | | | |
| 4,430 | 1,073 | 0 | 24% | 0% | | | |
| 264 | 264 | 0 | 100% | 0% | | | |
| 79 | 71 | 0 | 90% | 0% | | | |
| 4,773 | 1,408 | 0 | 29% | 0% | | | |
| ., | ., | | 2070 | 0,0 | | | |
| 2,974 | 282 | 287 | 9% | 10% | | | |
| 476 | 385 | 0 | 81% | 0% | | | |
| 3,449 | 666 | 287 | 19% | 8% | | | |
| 5,110 | | 20. | 1070 | 070 | | | |
| 0 | 0 | 0 | 0% | 0% | | | |
| 4,704 | 3,477 | 0 | 74% | 0% | | | |
| 4,704 | 3,477 | 0 | 74% | 0% | | | |
| 4,104 | 0,477 | • | 1 4 70 | 070 | | | |
| 0 | 0 | 0 | 0% | 0% | | | |
| 99 | 36 | 21 | 36% | 21% | | | |
| 761 | 471 | 0 | 62% | 0% | | | |
| 860 | 507 | 21 | 59% | 2% | | | |
| 860 | 507 | 21 | 39% | Z 70 | | | |
| | 0 | 0 | 00/ | 00/ | | | |
| 0 | 0 | 0 | 0% | 0% | | | |
| 1,381 | 508 | 93 | 37% | 7% | | | |
| 221 | 221 | 0 | 100% | 0% | | | |
| 1,602 | 729 | 93 | 45% | 6% | | | |
| | | | | | | | |
| 449 | 120 | 0 | 27% | 0% | | | |
| 449 | 120 | 0 | 27% | 0% | | | |
| | | | | | | | |
| 2,471 | 2,471 | 0 | 100% | 0% | | | |
| 2,471 | 2,471 | 0 | 100% | 0% | | | |
| | | | | | | | |
| 329 | 118 | 0 | 36% | 0% | | | |
| 38 | 5 | 0 | 12% | 0% | | | |
| 366 | 122 | 0 | 33% | 0% | | | |
| | | | | | | | |
| 1,210 | 674 | 0 | 56% | 0% | | | |
| 1,210 | 674 | 0 | 56% | 0% | | | |
| | | | | | | | |
| 13,221 | 11,638 | 0 | 88% | 0% | | | |
| 13,221 | 11,638 | 0 | 88% | 0% | | | |
| | | | | | | | |
| 3,840 | 2,865 | 0 | 75% | 0% | | | |
| 3,840 | 2,865 | 0 | 75% | 0% | | | |
| | | | | | | | |
| 8 | 8 | 0 | 100% | 0% | | | |
| 8 | 8 | 0 | 100% | 0% | | | |
| | | | | | | | |
| 822 | 838 | 0 | 102% | 0% | | | |
| 822 | 838 | 0 | 102% | 0% | | | |
| | | | | | | | |
| 195 | 82 | 0 | 42% | 0% | | | |
| 195 | 82 | 0 | 42% | 0% | | | |
| | | | | | | | |
| | | | | | | | |
| 4,278,869 | 2,660,432 | 97,395 | 62% | 2% | | | |
| , -, | , -, - | Goal | 38% | 1 | | | |

IN THE COMMUNITY





RAIDERS SUPPORT NEVADA YOUTH FOOTBALL LEAGUE

The Raiders Foundation, Raiders Alumni and Raider Rusher were on hand to show their support and donate to the Nevada Youth Football League, a nonprofit organization that facilitates competitions for football and cheer programs in Nevada. Raiders Alumni Lincoln Kennedy and Keith Moody presented the Nevada Youth Football League with a check for \$125,000, proceeds from the Raiders Foundation Poker Tournament, during the NYFL Opening Day.



RAIDERS STAFF SPEAK TO HIGH SCHOOL STUDENTS ABOUT CAREERS IN SPORTS INDUSTRY

Members of the Raiders front office staff took part in the Henderson Chamber of Commerce I CAN BE program, where they spoke to students at Foothill High School about working in the sports industry. The program helps high school students focus on career path choices and to pick classes that best fit their goals. Front office staff from the Raiders engaged in one-on-one with students to discuss the various opportunities in sports.

EARTHCAM VIEW - MARCH 26, 2020





ADDITIONAL INFORMATION / UPDATES

StadCo has, and continues to, comply with Section 35 (2)(c) and 35 (2)(e) of the Act as evidenced by JLL's Report.

In accordance with Section 31- (c)(1)(2)(3) of the Act, Mortenson | McCarthy Las Vegas Stadium, A Joint Venture is following the process described below to verify the payment of applicable prevailing wages.

Contractors that are awarded construction contracts for the work are required to follow the NRS 338 requirements outlined in the Act. This section pertains to the prevailing wage for public works projects as governed by the Nevada Labor Commissioner.

Mortenson | McCarthy has implemented LCPTracker Construction Certified Payroll—Labor Compliance Software which is a widely recognized tracking and certification software for prevailing wage projects. Mortenson | McCarthy maintains and updates the required prevailing wage rates in the database, based on those published by the Nevada Labor Commissioner's website. All contractors that have received a construction contract and are subject to the prevailing wage requirements are required to report payroll hours and wages for designated workers through this system. The contractor's entries into this system verifies compliance with wages and fringes as noted in the NRS 338 requirements.




North exterior elevation.

Allegiant Stadium continues to track toward an on-time completion. Architectural metal panels/ ribbonry install work continues. Allegiant Stadium naming rights signs are being installed on both the exterior and interior of the building. ETFE roof pillow installation began in March. Interior construction and finishes continue throughout the building. The NE primary videoboard installation was completed in March and the NW board installation began. Fixed seating and bowl railings continue to be installed from upper levels down. Field tray waterproofing was completed this month. Hardscape and landscape work continues to take place around the site.



Above: Naming rights sign being installed on the NW side of the building.

Below: View of the South exterior of the building, including the field tray.

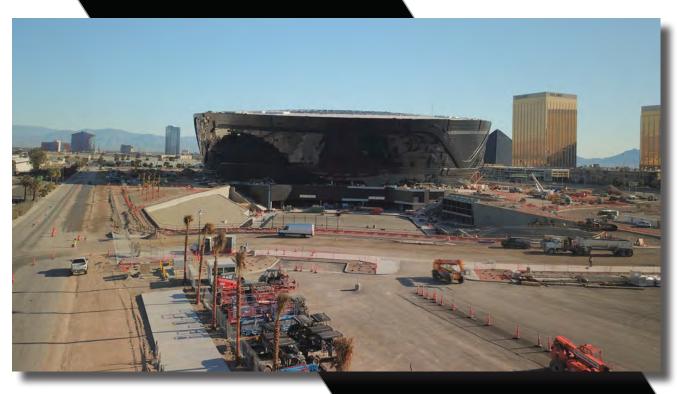

All photographs appearing in this document are the property of LV Stadium Events Company, LLC. They are protected by U.S. Copyright Laws, and are not to be shared or reproduced in any way without the written permission of LV Stadium Events Company, LLC. Copyright 2018 LV Stadium Events Company, LLC. All Rights Reserved.



Above: View from the NW side of the site.

Below: Naming rights sign installed on the North interior of the bowl.

